

Mingei International Museum

Progress Report to the Balboa Park Committee

08/06/20



Mingei International Museum - Amphitheatre



Mingei International Museum – Library



Mingei International Museum – Nakashima



Mingei International Museum – Sculpture Court Yard




Mingei International Museum – MPR



Progress Photos – MPR as at 04.30.20



Progress Photos – MPR Last Week

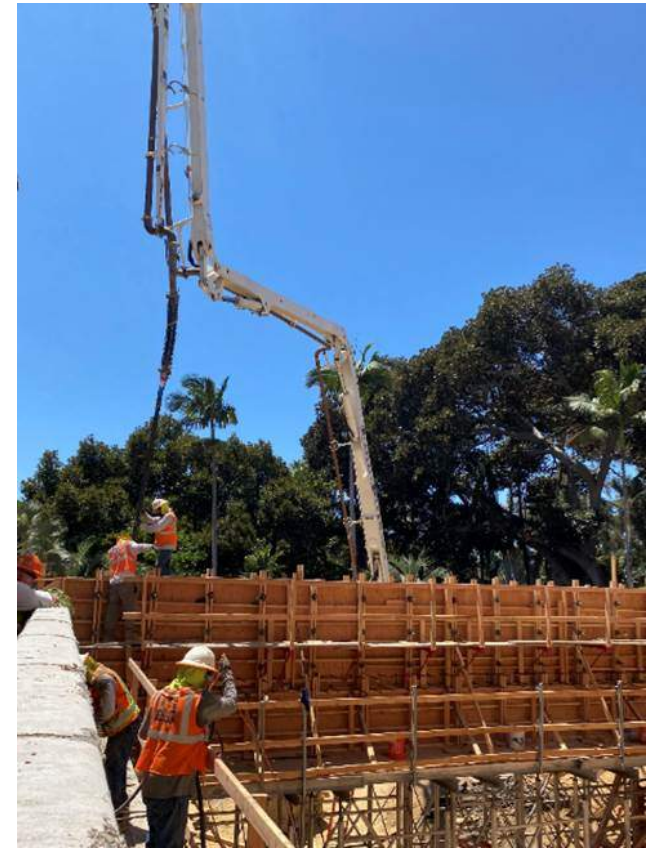

Multi-Purpose Room's Cast in Place Architectural Board Form concrete placement from Friday 7/31; with 9 truck loads we place approximately 85 cubic yards of concrete.

Progress Photos – MPR This Week



This week we are in the process of removing extensive bracing and panel formwork (shown below form pour date) to expose the board form finish; we intend to let the board form slats gradually come off the wall to get the best desired finish.

Progress Photos – Gallery level – GFRG Ceiling



Gallery level custom GFRG ceiling panel progress on the Gallery level along with ongoing framing and MEP rough-in the back ground.

Progress Photos – as at 06.10.20



Landing the new roof top chiller equipment with approximately 300 ton crane on the early morning of June 10th.

Progress Photos



Layton team engaging with the Luce et Studio design team in the Collaborative level, in the Arcade, and atop the Chihuly Stair Tower.
