

Mercado Apartments Project

PTS 696585

Waste Management Plan

April 2023 | 08400.00002.001

Prepared for:

MAAC Development
1355 Third Avenue
San Diego, CA 91911

Prepared by:

HELIX Environmental Planning, Inc.
7578 El Cajon Boulevard
La Mesa, CA 91942

This page intentionally left blank

Table of Contents

| <u>Section</u> | <u>Page</u> |
|--|--------------------|
| 1.0 INTRODUCTION..... | 1 |
| 1.1 Purpose of the Report..... | 1 |
| 1.2 Project Location | 1 |
| 1.3 Project Description | 1 |
| 2.0 REGULATORY FRAMEWORK..... | 2 |
| 2.1 State of California | 2 |
| 2.2 Local Regulations | 3 |
| 2.2.1 City of San Diego CEQA Significance Determination Thresholds..... | 3 |
| 2.2.2 City of San Diego Refuse, Organic Waste, and Recyclable Materials Storage Ordinance..... | 4 |
| 3.0 PRE-CONSTRUCTION WASTE | 7 |
| 3.1 Demolition | 7 |
| 3.1.1 Building Demolition | 7 |
| 3.1.2 Pavement Demolition | 9 |
| 3.2 Clearing and Grubbing | 9 |
| 3.3 Grading..... | 10 |
| 3.4 Summary of Pre-Construction Waste Generation and Diversion..... | 10 |
| 3.4.1 Summary of Salvage Material | 12 |
| 3.4.2 Summary of Recycled Material | 12 |
| 4.0 CONSTRUCTION WASTE..... | 12 |
| 4.1 Estimate Construction Waste Generation and Diversion | 13 |
| 4.1.1 Proposed Post-Consumer Content Construction Materials | 14 |
| 5.0 OCCUPANCY WASTE | 14 |
| 5.1 Storage..... | 14 |
| 5.2 Waste Generation – Existing Uses | 15 |
| 5.3 Waste Generation – Project Uses..... | 15 |
| 5.4 Change in Waste Generation | 16 |
| 6.0 WASTE REDUCTION, RECYCLING, AND DIVERSION MEASURES..... | 17 |
| 6.1 Construction Waste Management, Coordination, and Oversight | 17 |
| 6.1.1 Contractor Agreements and City Coordination | 17 |
| 6.1.2 Designation of a Solid Waste Management Coordinator | 17 |
| 6.1.3 Contractor Waste Management Training..... | 18 |
| 6.1.4 Daily Site Inspections by Contractor(s)..... | 19 |
| 6.1.5 Regular Removal of Waste Materials | 19 |
| 6.1.6 City Verification..... | 19 |

Table of Contents (continued)

| <u>Section</u> | <u>Page</u> |
|-----------------------|---|
| 6.2 | Construction Waste Reduction, Diversion Compliance, and Verification 20 |
| 6.2.1 | Identification, Separation, and Diversion of Recyclable/Reusable Materials 20 |
| 6.2.2 | Source Reduction Measures 21 |
| 6.3 | Operational Waste Management and Diversion Measures 21 |
| 7.0 | CONCLUSION..... 23 |
| 7.1 | Summary of Waste Generation and Diversion 23 |
| 7.2 | Compliance with City and State Regulations 23 |
| 7.2.1 | State of California 24 |
| 7.2.2 | City of San Diego 24 |
| 8.0 | LIST OF PREPARERS 25 |
| 9.0 | REFERENCES 26 |

LIST OF APPENDICES

| | |
|---|--|
| A | Certified Construction & Demolition Recycling Facility Directory |
| B | City of San Diego C&D Debris Conversion Rate Table |
| C | City of San Diego Waste Generation Factors – Occupancy Phase |

LIST OF FIGURES

| <u>No.</u> | <u>Title</u> | <u>Follows Page</u> |
|-------------------|------------------------|----------------------------|
| 1 | Regional Location..... | 2 |
| 2 | Project Vicinity..... | 2 |
| 3 | Site Plan | 2 |

Table of Contents (continued)

LIST OF TABLES

| <u>No.</u> | <u>Title</u> | <u>Page</u> |
|------------|---|-------------|
| 1 | Minimum Exterior Refuse, Organic Waste, and Recyclable Material Storage Areas for Residential Development | 5 |
| 2 | City C&D Deposit Schedule | 6 |
| 3 | Existing Structure Demolition Waste Content | 8 |
| 4 | Pre-Construction Demolition, Clearing/Grubbing, and Grading Solid Waste Generation, Diversion Rates, and Facilities | 11 |
| 5 | Construction Solid Waste Generation, Diversion Rates, and Facilities..... | 14 |
| 6 | Estimated Annual Solid Waste Generation and Diversion Rates – Existing Buildings | 15 |
| 7 | Estimated Annual Solid Waste Generation and Diversion Rates – Proposed Buildings | 16 |

Acronyms and Abbreviations

| | |
|------------|---|
| AB | Assembly Bill |
| APN | Accessor's Parcel Number |
| C&D | Construction and Demolition |
| CalRecycle | California Department of Resources Recycling and Recovery |
| CDP | Coastal Development Permit |
| CEQA | California Environmental Quality Act |
| CUP | Central Utility Plant |
| CY | cubic yard(s) |
| DSD | Development Services Department (City of San Diego) |
| ESD | Environmental Services Department (City of San Diego) |
| FEMA | Federal Emergency Management Agency |
| IBC | International Building Code |
| ICC | International Code Council |
| IWMP | Integrated Waste Management Plan |
| lbs | pounds |
| NDP | Neighborhood Development Permit |
| SB | Senate Bill |
| SDMC | San Diego Municipal Code |
| SDP | Site Development Permit |
| SF | square foot/feet |
| SRRE | Source Reduction and Recycling Element |
| SWMC | Solid Waste Management Coordinator |
| TM | Tentative Parcel Map |
| WDM | Waste Diversion Measures |
| WMP | Waste Management Plan |

1.0 INTRODUCTION

1.1 PURPOSE OF THE REPORT

The purpose of this Waste Management Plan (WMP) is to identify the quantity of solid waste that would be generated by the Mercado Apartments Project (project) throughout demolition, construction, and operation, and to identify measures to reduce the potential impacts associated with management of such waste.

Proper separation and diversion of recyclable waste materials is required to divert each material type to a recycling/reuse facility with the highest possible diversion rate. As discussed further in Section 2.0, *Regulatory Framework*, to comply with City of San Diego (City) waste reduction ordinances and the waste diversion goals established by State Assembly Bill (AB) 341, the project must achieve a 75 percent diversion rate during demolition and construction. The City's California Environmental Quality Act (CEQA) Significance Thresholds for solid waste identify a threshold of 1,500 tons of waste or more during construction and demolition (C&D) for direct solid waste impacts, and 60 tons of waste or more during C&D for potentially significant cumulative solid waste impacts. The City Environmental Services Department's (ESD) Certified C&D Recycling Facility Directory (City 2023; Appendix A) provides guidance on identifying recycling/reuse facility locations, accepted materials, recycling/reuse rates, and associated disposal fees and/or the value of the materials accepted for recycling/reuse.

This WMP has been prepared consistent with applicable federal, State, and local laws, regulations, and standards pertinent to the Project. Its goal is to implement an approach for managing waste that conserves landfill space, preserves environmental quality, conserves natural resources, and reduces disposal costs. Responsibility for ensuring ongoing WMP compliance would be under the direction of the Project Solid Waste Management Coordinator (SWMC), as assigned by MAAC Development (Applicant).

1.2 PROJECT LOCATION

The Project is located at 2001 Newton Avenue in the Barrio Logan Neighborhood of the City of San Diego. The Project site is located within the Barrio Logan Community Plan, south of Downtown San Diego and west of Interstate (I-)5 (Figure 1, *Regional Location*). The Project site is comprised of one parcel (Assessor's Parcel Number [APN] 209-121-01-00) totaling 4.34 acres (Figure 2, *Project Vicinity*).

1.3 PROJECT DESCRIPTION

The Project proposes to demolish the two existing two story buildings on a 0.98-acre property currently occupied by Mercado Apartments totaling approximately 12,000 square feet (SF) as well as parking lot and trash enclosure. The Project would construct one new four-story structure encompassing six substructures, totaling 100,169 SF, for 92 units of affordable housing residential apartments. The Project also includes 5,886 SF of outdoor courtyard and plaza space. Parking is not included as part of the Project; no development is proposed outside currently paved/developed areas (Figure 3, *Site Plan*). Direct site access for pedestrians would be provided by the new main entry off Evans Street, and two new entries off Main Street. A vehicular service access driveway would also be provided off Main Street. Other indirect vehicular access would be provided by an existing driveway off Newton Street, which provides access to the existing apartment complex surrounding the project site. The exiting driveway

off Evans Street would be removed as part of the Project. Grading is estimated to require even cut and fill of 750 cubic yards over a 42,790 square-foot area, with no export.

The Project is proposed to be constructed in one phase, with construction assumed to be completed in 2026.

2.0 REGULATORY FRAMEWORK


2.1 STATE OF CALIFORNIA

The State of California (State) Integrated Waste Management Act of 1989 (California Assembly Bill [AB] 939; as modified in 2010 by Senate Bill [SB] 1016), which is administered by the California Department of Resources Recycling and Recovery (CalRecycle), requires counties to develop an Integrated Waste Management Plan (IWMP) that describes local waste diversion and disposal conditions, and identifies realistic programs to achieve waste diversion goals. IWMPs compile Source Reduction and Recycling Elements (SRREs) that are required to be prepared by each local government, including cities. SRREs analyze the local waste stream to determine where to focus diversion efforts and provide a framework to meet waste reduction mandates. The goal of the solid waste management efforts is not to increase recycling, but to decrease the amount of waste entering landfills. AB 939 required all cities and counties to divert a minimum 50 percent of all solid waste from landfill disposal.

In 2011, the State legislature enacted AB 341 (California Public Resource Code Section 42649.2), increasing the diversion target to 75 percent statewide. AB 341 also requires the provision of recycling service to commercial and residential facilities that generate 4 cubic yards (CY) or more of solid waste per week.

In October 2014, Governor Brown signed AB 1826 Chesbro (Chapter 727, Statutes of 2014), which builds on the success of the mandatory commercial recycling program established by AB 341 by mandating a phased recycling program based on the amount of organic waste businesses generate per week. Organic waste means food waste, green waste, landscape and pruning waste, nonhazardous wood waste, and food-soiled paper waste that is mixed in with food waste. For businesses that generate 8 or more CY of organic waste per week, this requirement begins April 1, 2016, while those that generate 4 CY of organic waste per week must have an organic waste recycling program in place beginning January 1, 2017. This law also requires that on and after January 1, 2016, local jurisdictions across the State implement an organic waste recycling program to divert organic waste generated by businesses, including multi-family residential dwellings that consist of five or more units. This law phases in the mandatory recycling of commercial organics over time, while also offering an exemption process for rural counties.

In September 2016, SB 1383 (Chapter 395, Statutes of 2016) was approved, requiring a statewide reduction of organic waste disposal. Specifically, SB 1383 requires a 50 percent reduction of the statewide disposal of organic waste from the 2014 level by 2020, and a 75 percent reduction of the 2014 level by 2025. SB 1383 requires cities and counties to adopt regulations to achieve the specified targets for reducing organic waste in landfills. Further, CalRecycle adopted regulations in November 2020 took effect in January 2022.

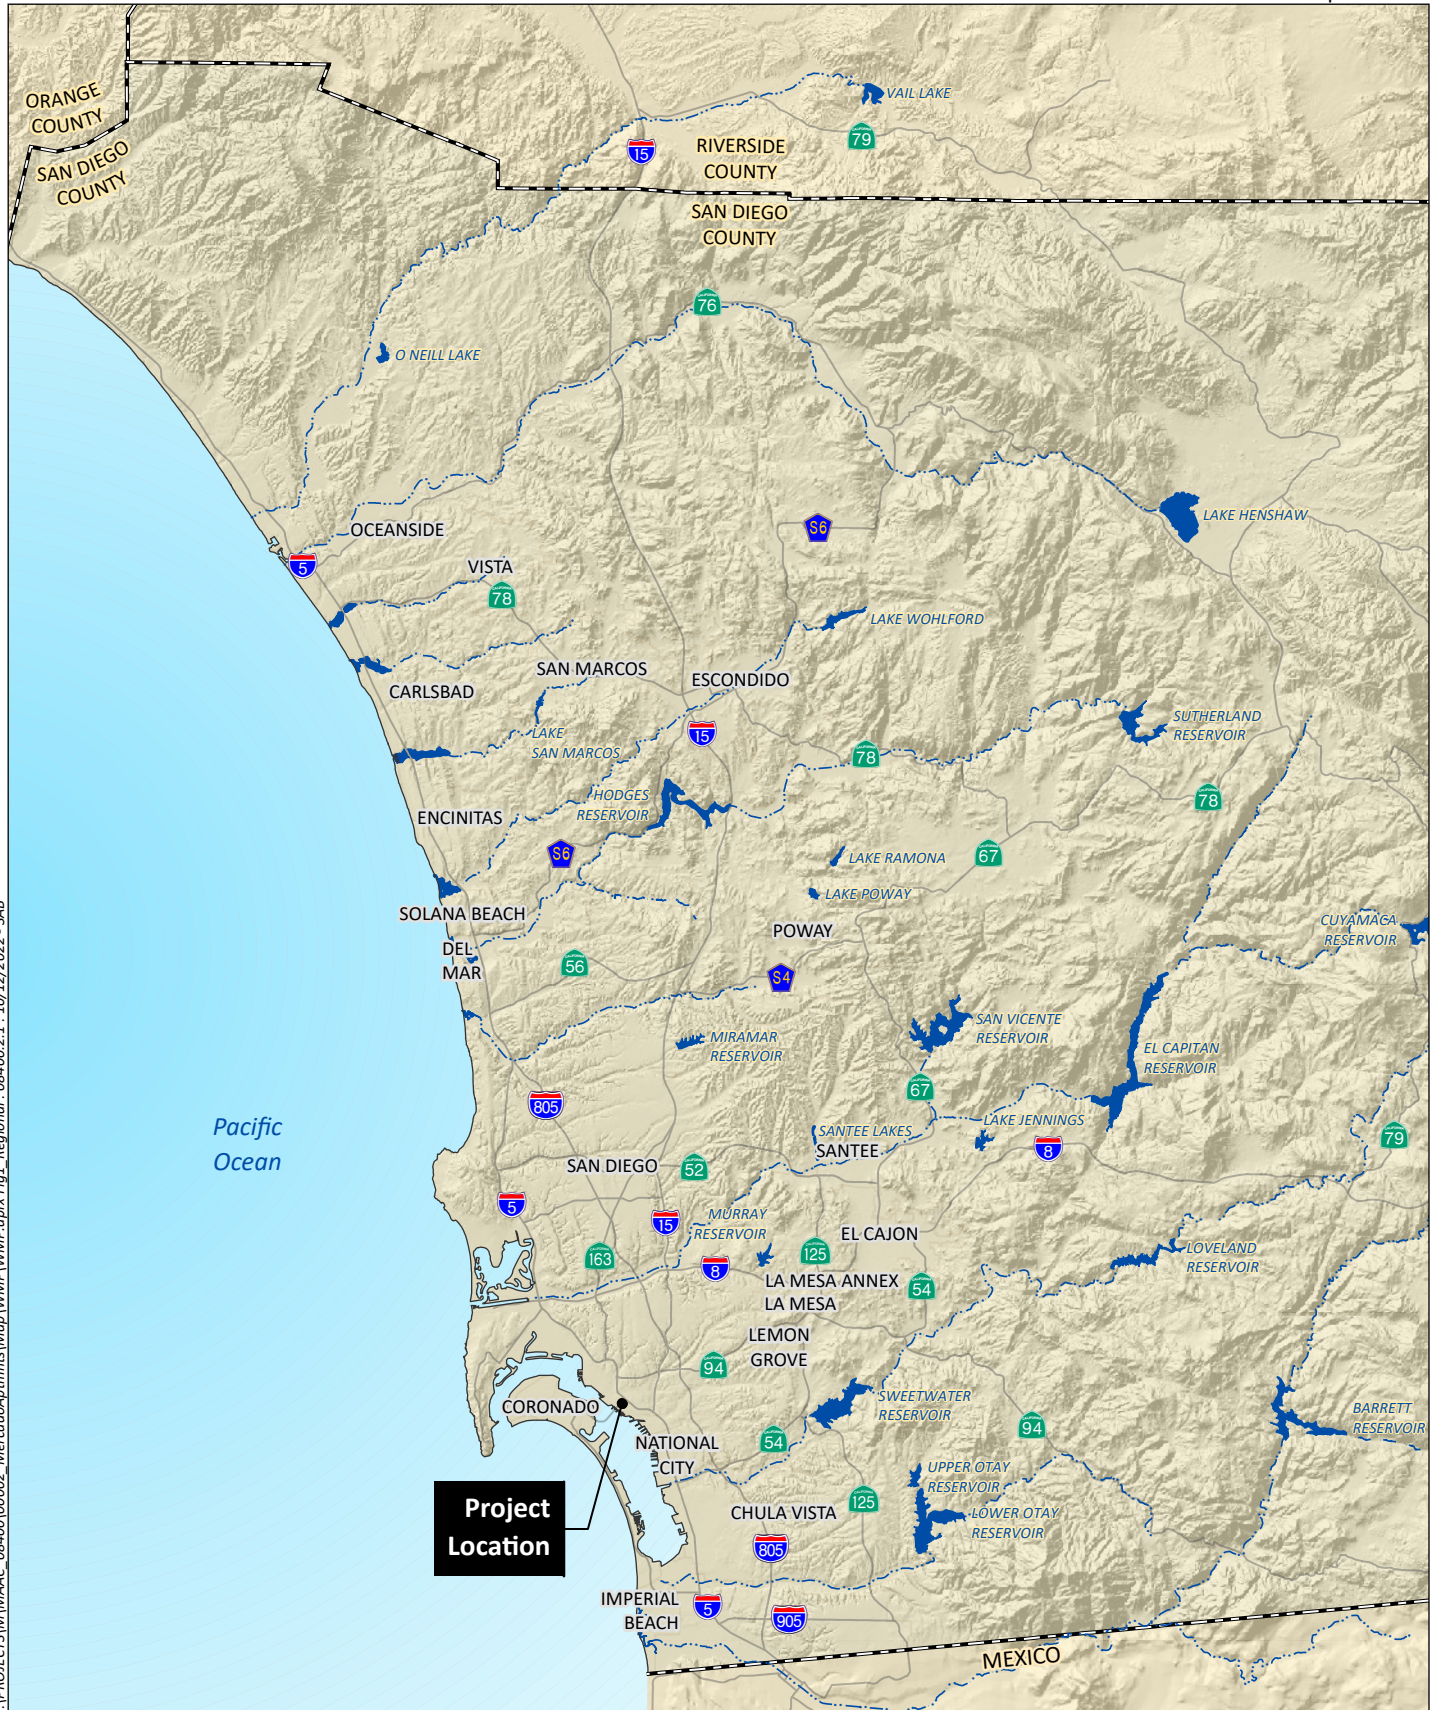

I:\PROJECTS\I\MAAC_08400\00002_MercadoAptmnts\Map\WMP\WMP.aprx Fig1_Regional : 08400.2.1 : 10/12/2022 - SAB

Pacific Ocean

Project Location




Source: Base Map Layers (SanGIS, 2016)



I:\PROJECTS\I\MAAC_08-001\00002_MercadoApartments\Map\WMP\WMP.aprx Fig2_Vicinity : 08400.2.1 : 10/12/2022 - SAB

Source: Aerial (NearMap, 2019)



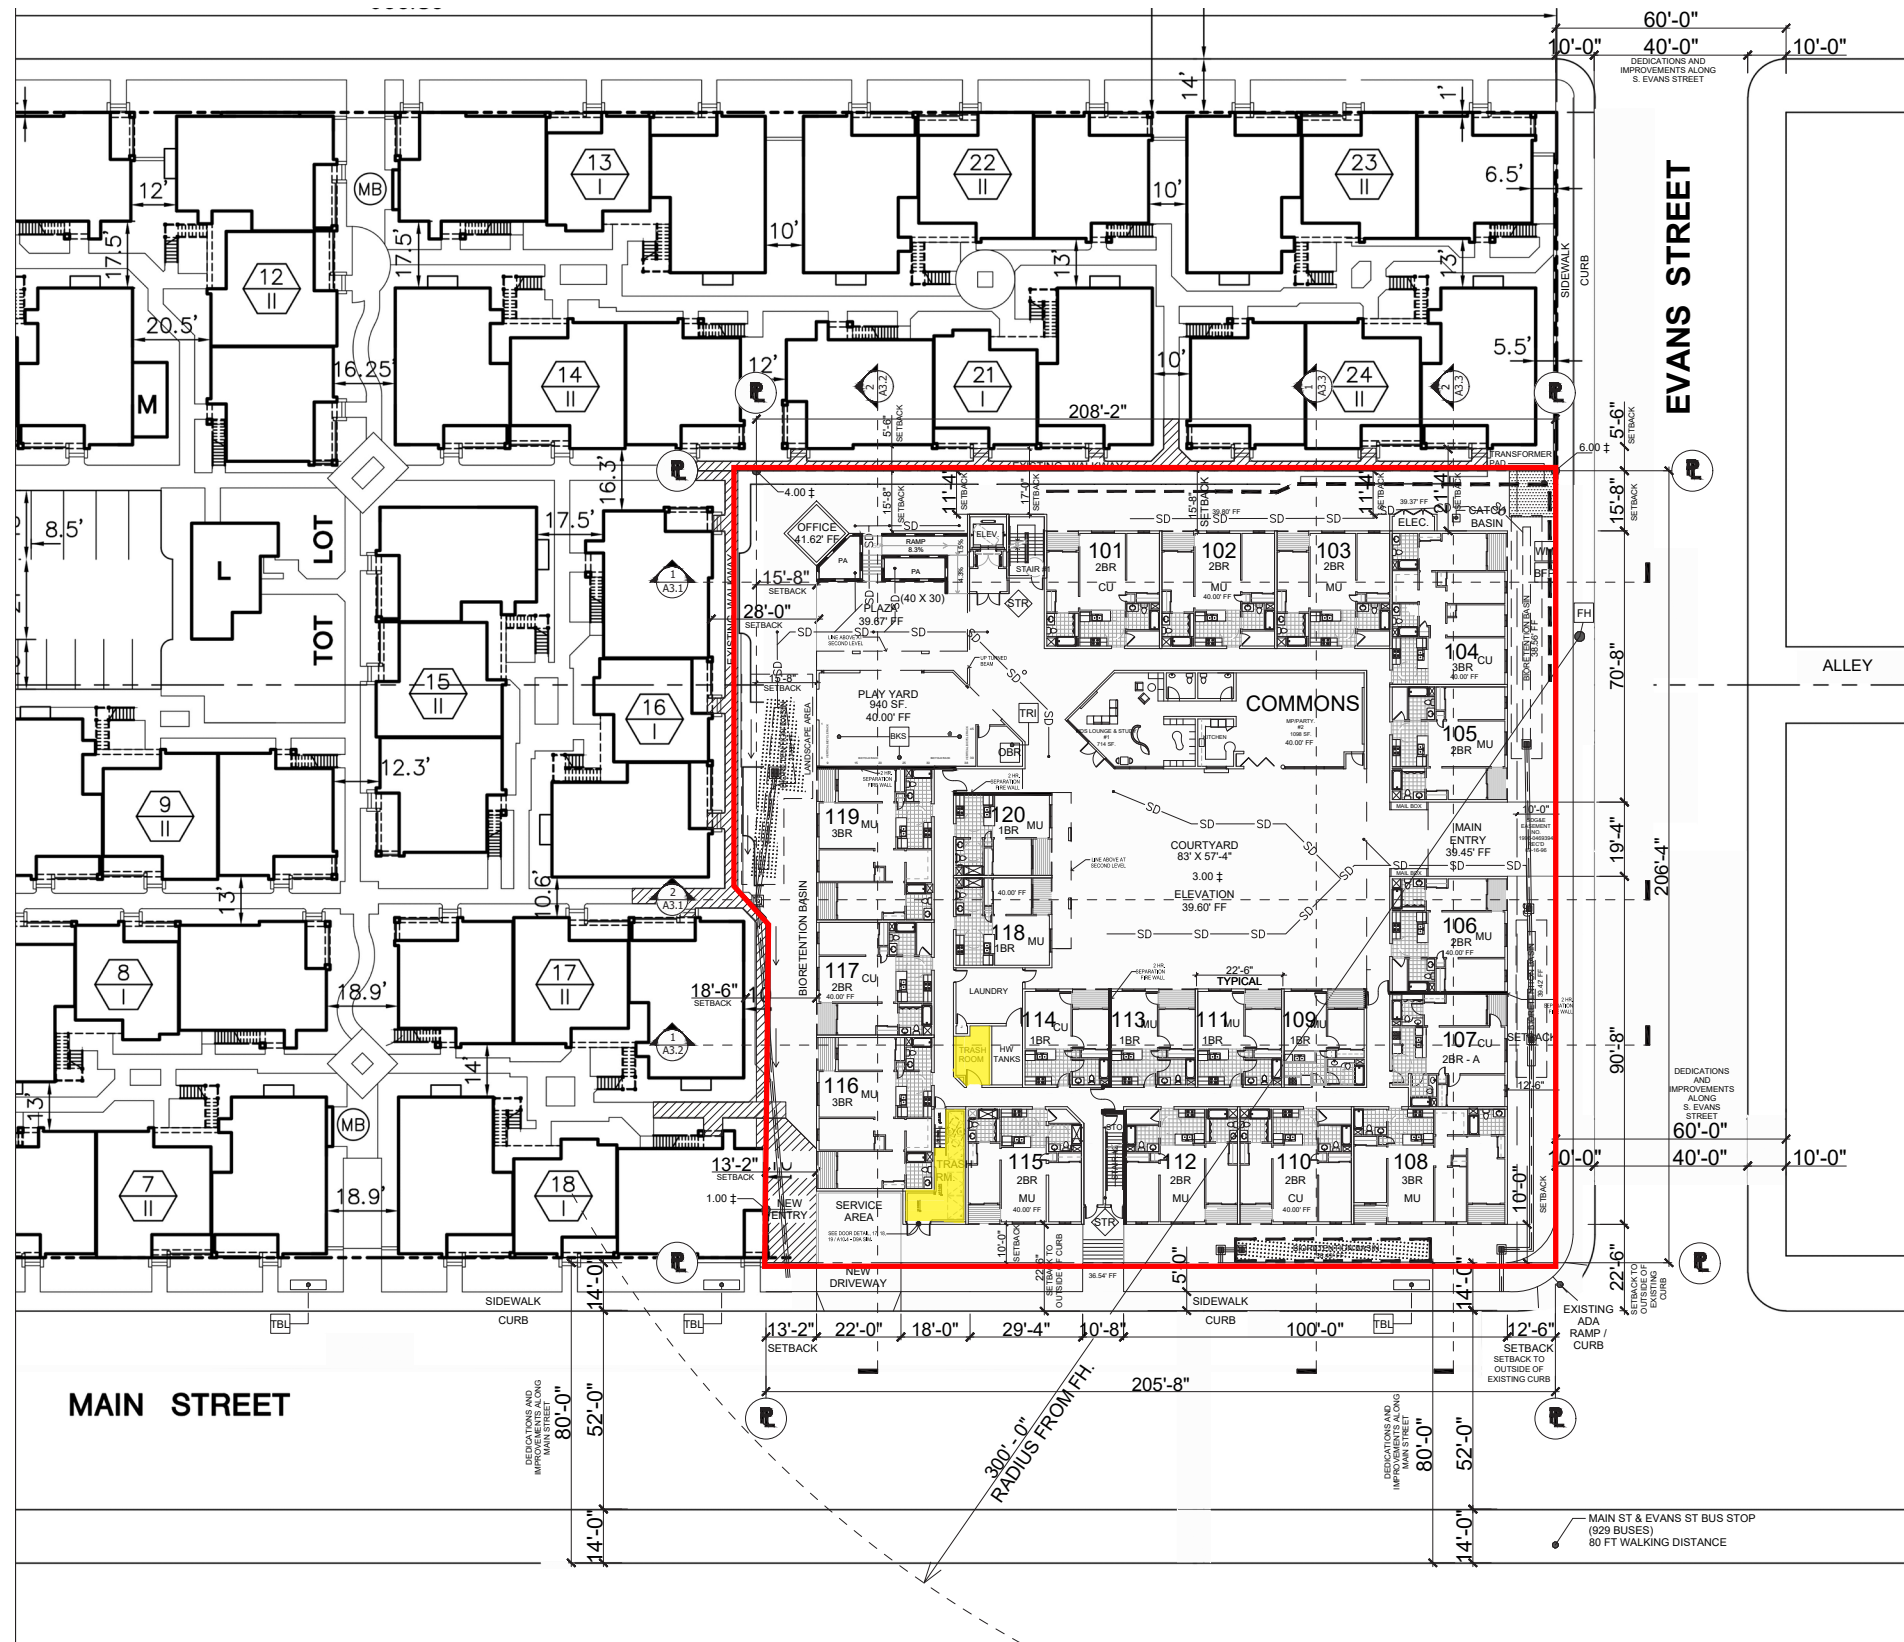

UNIT DISTRIBUTION

| | 1BR | 2BR | 3BR | TOTAL |
|---------|-----|-----|-----|-------|
| LEVEL 1 | 6 | 10 | 4 | 20 |
| LEVEL 2 | 8 | 10 | 6 | 24 |
| LEVEL 3 | 8 | 10 | 6 | 24 |
| LEVEL 4 | 8 | 8 | 8 | 24 |
| | 30 | 38 | 24 | 92 |

STORAGE DISTRIBUTION

| | STORAGE |
|---------------|---------------|
| LEVEL 1 | 0 SF |
| LEVEL 2 | 295 SF |
| LEVEL 3 | 295 SF |
| LEVEL 4 | 295 SF |
| TOTAL: | 885 SF |

WASTE STORAGE DISTRIBUTION

| | WASTE STORAGE |
|---------------|---------------|
| LEVEL 1 | 495 SF |
| LEVEL 2 | 47 SF |
| LEVEL 3 | 47 SF |
| LEVEL 4 | 47 SF |
| TOTAL: | 636 SF |

NOTES:
 1) THE PROPOSED PROJECT WILL COMPLY WITH ALL THE REQUIREMENTS OF THE CURRENT CITY OF SAN DIEGO STORM WATER STANDARDS MANUAL BEFORE A GRADING OR BUILDING PERMIT IS ISSUED. IT IS THE RESPONSIBILITY OF THE OWNER/DESIGNER/APPLICANT TO ENSURE THAT THE CURRENT STORM WATER PERMANENT BMP DESIGN STANDARDS ARE INCORPORATED INTO THE PROJECT.

SYMBOLS

| | |
|-----|--|
| STR | STAIR TO ROOF |
| WM | WATER METERS |
| BFP | BACK FLOW PREVENTOR |
| FH | FIRE HYDRANT (EXISTING) |
| TBL | TRANSPORTATION INFRASTRUCTURE LIGHTING AND/OR BENCH ON MAIN STREET |
| OBR | ON SITE BICYCLE REPAIR |

I:\PROJECTS\1\MAAC_08400\00002_MercadoAptmnts\Map\WMP\Fig3_SitePlan.indd 08400.2.1 3/31/23 - SAB

Source: Martinez + Cutri, 2022

2.2 LOCAL REGULATIONS

The City has enacted codes and policies directed at the achievement of State-required diversion levels, including the Refuse and Recyclable Materials Storage Regulations (City 1997; Municipal Code Chapter 14, Article 2 Division 8), Recycling Ordinance (City 2022b; Municipal Code Chapter 6, Article 6, Division 7), and the Construction and Demolition Debris Deposit Ordinance (City 2016a; Municipal Code Chapter 6, Article 6, Division 6). The City's Zero Waste Plan, a component of the City's Climate Action Plan, was approved and adopted by City Council on July 13, 2015. The Zero Waste Plan identifies goals and strategies to achieve 75 percent diversion by 2020, 90 percent diversion by 2035, and "zero" waste by 2040 (City 2015). Additionally, the City is in the process of implementing extensive procedural changes to comply with SB 1383, including developing collection operations, adopting purchasing policies, amending the City's Municipal Recycling Code, enacting building requirements, preparing enforcement responsibilities, and strategizing public education and outreach efforts. As part of this effort, starting in 2022, the City and City-certified private waste haulers will expand organic waste collection services for residents and businesses to meet the organic waste reduction goals set by SB 1383.

As stated in the City Development Services Department (DSD) CEQA Significance Determination Thresholds (City 2022c), implementation of these regulations and ordinances alone is not projected to achieve a 50 percent diversion rate, far below the current 75 percent diversion level targeted by the State and identified in the Zero Waste Plan for 2020. The City's ESD estimates that compliance with existing City ordinances and regulations alone achieves only an approximate 30 and 40 percent diversion rate for small and large projects, respectively (City 2013). Therefore, discretionary projects must undertake additional measures to comply with existing regulations.

2.2.1 City of San Diego CEQA Significance Determination Thresholds

The City's CEQA Significance Determination Thresholds establish solid waste generation thresholds for discretionary projects. Proposed projects that involve construction, demolition, and/or renovation that meet or exceed the thresholds described below are considered to have potentially significant solid waste impacts and require the preparation of a WMP.

Direct Impacts

A project would have a direct impact on solid waste services if it would generate 1,500 tons of waste or more during demolition and construction. Projects that include the construction, demolition, or renovation of 1,000,000 SF or more of building space are considered by the City to have the potential to generate this amount of waste, and therefore may have direct impacts on solid waste services. Additional considerations are as follows:

- The generation of large amounts of waste result in direct impacts that bring facilities closer to daily throughput limits, shorten facility lifespans, require increased numbers of trucks and other equipment, and make it difficult for the City to achieve required waste reduction levels. Waste management planning is based on a steady rate of waste generation and does not assume increased waste generation due to growth.

- While all projects are required to comply with the City’s waste management ordinances, direct and cumulative impacts are mitigated by the implementation of project-specific WMPs, which may reduce solid waste impacts to below a level of significance.
- For projects over 1,000,000 SF, a significant direct and cumulative solid waste impact would result if the compliance with the City’s ordinances and the WMP fail to reduce the impacts of such projects to below a level of significance and/or if a WMP for the project is not prepared and conceptually approved by the ESD prior to distribution of the draft environmental document for public review.

Cumulative Impacts

A project would have a cumulative impact on solid waste services if it would generate 60 tons of waste or more per year. Projects that include the construction, demolition, and/or renovation of 40,000 SF or more of building space are considered by the City to potentially generate this amount of waste, and therefore may have cumulative impacts on solid waste services. Other projects such as new single-family residences on public streets or projects creating a demand for litter bin service may also cumulatively impact solid waste services.

While all projects are required to comply with the City’s waste management ordinances, cumulative impacts are mitigated by the implementation of a project-specific WMP that reduces solid waste impacts to below a level of significance.

Project Potential Impacts

The Project does not propose the construction, demolition, or renovation of 1,000,000 SF or more of building space; however, the Project has the potential to generate more than 1,500 tons of solid waste materials during demolition and construction and therefore may exceed the City’s threshold for direct solid waste impacts. The Project proposes construction of more than 40,000 SF, thereby exceeding the City’s threshold for cumulative solid waste impacts without implementation of solid waste diversion measures.

Because implementation of the Project without waste diversion measures may exceed direct and cumulative solid waste thresholds, the City has required preparation of this WMP in compliance with CEQA and City Guidelines, to ensure that the Project contribution to the overall waste produced within the City would be reduced sufficiently to allow the City to comply with the waste reduction targets established in the Public Resources Code and State statutes.

2.2.2 City of San Diego Refuse, Organic Waste, and Recyclable Materials Storage Ordinance

San Diego Municipal Code (SDMC) Section 142.0801 et seq. contains the language of the Refuse, Organic Waste, and Recyclable Materials Storage Regulations (Storage Ordinance), an ordinance that is required by State law. The Storage Ordinance was adopted in December 1997. An amendment to the Ordinance was approved by the City Council on January 27, 2022 (effective February 26, 2022). The purpose of the Storage Ordinance is to provide permanent, adequate, and convenient space for the storage and collection of refuse, organic waste, and recyclable material. The storage required for the project would meet the general regulations detailed within the Storage Ordinance. Additionally, each dwelling unit shall be equipped with an interior refuse, organic waste, and recyclable material storage area.

Table 1, *Minimum Exterior Refuse, Organic Waste, and Recyclable Material Storage Areas for Residential Development*, (SDMC Table 142 08B) provides information on minimum exterior refuse and recyclable material storage areas for multiple unit residential development.

**Table 1
MINIMUM EXTERIOR REFUSE, ORGANIC WASTE, AND RECYCLABLE MATERIAL STORAGE AREAS
FOR RESIDENTIAL DEVELOPMENT**

| Number of Dwelling Units Per Development | Minimum Refuse Storage Area Per Development (SF) | Minimum Organic Waste Storage Area Per Development (SF) | Minimum Recyclable Material Storage Area Per Development (SF) | Total Minimum Storage Area Per Development (SF) |
|--|---|---|---|--|
| 1 | 6.25 | 6.25 | 6.25 | 18.75 |
| 2-6 | 12 | 12 | 12 | 36 |
| 7-15 | 24 | 24 | 24 | 72 |
| 16-25 | 48 | 48 | 48 | 144 |
| 26-50 | 96 | 96 | 96 | 288 |
| 51-75 | 144 | 144 | 144 | 432 |
| 76-100 | 192 | 192 | 192 | 576 |
| 101-125 | 240 | 240 | 240 | 720 |
| 126-150 | 288 | 288 | 288 | 864 |
| 151-175 | 336 | 336 | 336 | 1,008 |
| 176-200 | 384 | 384 | 384 | 1,152 |
| 201+ | 384 plus 48 square feet for every 25 dwelling units above 201 | 384 plus 48 square feet for every 25 dwelling units above 201 | 384 plus 48 square feet for every 25 dwelling units above 201 | 1,152 plus 144 square feet for every 25 dwelling units above 201 |

SF = square feet

City of San Diego Recycling Ordinance

The City’s Recycling Ordinance, found in SDMC Section 66.0701 et seq., was adopted in November 2007 (City 2022b). An amendment to the Ordinance was approved by the City Council on May 5, 2022 (effective June 8, 2022). The Recycling Ordinance requires the provision of recycling service for all commercial facilities, all single-family residences, and multi-family residences. The Ordinance states that occupants of residential facilities that receive solid waste collection services from a Recyclable Materials Collector shall participate in a recycling program by separating recyclable materials from other solid waste, depositing the recyclable materials in the designated recycling containers, and placing the recycling containers out for collection at the time and place designated by the Recyclable Materials Collector. The Ordinance also provides an exemption for multi-family residential facilities, commercial facilities, and mixed-use facilities that generate 0.001 cubic yard or less per week of solid waste including recyclable materials mixed with solid waste. This requirement makes the provision of recycling service a virtually universal requirement. In addition, the Recycling Ordinance requires that apartments and condominiums with two or more units serviced by private haulers must recycle organic waste food scraps, food-soiled paper, yard trimmings and nonhazardous wood waste and provide weekly collection services. The Recycling Ordinance also requires development of educational materials to ensure occupants are informed about the City’s Ordinance and recycling services, including information on types of recyclable materials accepted.

City of San Diego Construction and Demolition Debris Deposit Ordinance

On July 1, 2008, the City’s C&D Debris Deposit Ordinance became effective (City 2016a). An amendment to the Ordinance and revisions to the associated C&D deposit schedule were approved by the City Council on December 10, 2013 (effective January 1, 2014) and on April 19, 2016 (effective June 22, 2016). The C&D Debris Deposit Ordinance is designed to keep C&D materials out of local landfills and ensure that materials are diverted from disposal. The Ordinance creates an economic incentive to recycle C&D debris through the collection of fully refundable deposits that are returned, in whole or in part, upon proof of the amount of C&D debris the Project applicant diverted from landfill disposal. The Ordinance requires that the majority of construction, demolition and remodeling projects requiring building, combination, and demolition permits pay a refundable C&D Debris Recycling Deposit and divert at least 75 percent of their debris by recycling, reusing, or donating usable materials. The deposit is held until the applicant provides receipts demonstrating that a minimum 75 percent of the material generated has been diverted from disposal in landfills.

The C&D Ordinance stipulates that projects will be required to divert 75 percent of their wastes when mixed debris facilities with a permitted daily tonnage capacity of at least 1,000 tons maintain a 75 percent diversion rate for three consecutive calendar year quarters. Greater than 75 percent diversion also may be required for a project if a higher goal is specified during discretionary permitting. Mixed debris recyclers in San Diego County currently achieve between 69 and 86 percent diversion rates at their facilities (City 2023; Appendix A). This is because not everything that comes through the door is usable or marketable. While one of the facilities achieves a diversion rate equal to or greater than 86 percent, six facilities have a diversion rate of 69 percent. For a project that would dispose of mixed debris at the facility that achieves a 69 percent diversion rate, virtually all clean C&D waste from a project must be source separated and sent to a material-specific recycling facility, such as aggregate and metal recyclers, to achieve an overall diversion rate of 75 percent. Higher diversion rates can also be accomplished by salvage and/or on-site reuse of C&D materials. The City’s C&D thresholds and deposit amounts are shown below in Table 2, *City C&D Deposit Schedule*.

**Table 2
CITY C&D DEPOSIT SCHEDULE**

| Building Category | Deposit per SF¹ | Minimum SF Subject to Ordinance | Maximum SF Subject to Ordinance | Range of Deposits |
|---|-----------------------------------|--|--|--------------------------|
| Residential New Construction, Non-residential Alterations, Demolition | \$0.40 | 1,000 | 100,000 | \$400-\$40,000 |
| Non-residential New Construction | \$0.20 | 1,000 | 50,000 | \$200-\$10,000 |
| Flat Rate | | | | |
| Residential Alterations | \$1,000 | 1,000 | 6,999 | \$1,000 |

Source: City 2016b

¹ Deposit amounts are applied to the entire area(s) where work will be performed and are calculated based on square footage.

SF = square foot/feet

3.0 PRE-CONSTRUCTION WASTE

Prior to initiation of the Project’s construction activities, site preparation would require clearing/grubbing and demolition. Clearing and grubbing would require removal of existing ornamental vegetation associated with the existing buildings. Project construction would require demolition of two buildings, paved areas, and other improvements within the existing site.

All C&D-generated waste would be subject to compliance with the source separation and diversion requirements contained in this WMP to divert, recycle, and/or re-use these materials to the maximum degree possible. As identified in the City’s Certified C&D Recycling Facility Directory (City 2023; Appendix A), “Mixed C&D Debris” recyclers attain at most an 86 percent diversion rate, whereas “source separated” material recyclers can attain nearly 100 percent diversion rates (City 2023). As a result, in order to achieve the highest level of waste diversion from landfills, and highest dollar value for the quality of materials, the Project would source separate (segregate) clean recyclable materials on site by material type, to the maximum extent practicable, and divert them for recycling or reuse at City-certified facilities specializing in each material type (refer to Appendix A).

3.1 DEMOLITION

3.1.1 Building Demolition

The existing development includes two buildings that are proposed to be demolished, 6,000 SF each. In total, 12,000 SF of building space would be demolished. The buildings are Type V construction, composed of combustible (e.g., wood) and non-combustible materials (e.g., concrete, brick, steel, etc.).

Salvage

No salvage of materials in the existing buildings is proposed.

3.1.1.1 Recycling

The overall estimated quantity of debris from the buildings are based on the “General Building Formula” contained in the Federal Emergency Management Agency’s (FEMA) Debris Estimating Field Guide (2010). The formula multiplies building length, width, and height (in feet) by a constant of 0.33 to account for air space in the building, and divides the resulting number by 27 to convert cubic feet to cubic yards (FEMA 2010):

$$\frac{\text{Length} \times \text{Width} \times \text{Height} \times 0.33}{27} = \text{CY}$$

The existing buildings were assumed to have a total approximate height of 20 ft. The square footage listed in Section 3.1.1, above, equals their length times width. Using these dimensions, structural debris for the first building as an example is estimated as follows:

$$\frac{(6,000 \text{ SF} \times 20 \text{ feet} \times 0.33)}{27} = \mathbf{1,467 \text{ CY}}$$

Since the two buildings are the same size, this formula provides the same estimated quantity of demolition debris, totaling approximately 2,933 CY for both buildings.

As specific materials contained in the existing building are not known, estimates were pulled from the Military Base Closure Handbook - A Guide to Construction and Demolition Materials Recovery (CalRecycle 2002). According to this handbook, demolition of typical wood (Type V) residential structures results in a C&D waste stream (by volume) as follows:¹

- 4 percent concrete,
- 13 percent brick
- 80 percent wood
- 3 percent metal

In addition to the percentages listed above, it is assumed that there are other recyclable “mixed debris” materials present in unknown quantities, which are estimated to comprise 20 percent of the total demolition debris. These materials would be too damaged or mixed to be source separated into clean materials and would be disposed of accordingly. An additional eight percent of non-recyclable “waste” also was factored into the total waste stream anticipated for demolition of the buildings. Factoring in the 28 percent mixed debris and trash that would be generated during demolition, the concrete, brick, wood, and metal breakdown provided in the Military Base Closure Handbook would account for the remaining 72 percent of total waste. The complete breakdown of waste types and volumes of demolition waste anticipated to be generated are shown in Table 3, *Existing Structure Demolition Waste Content*.

**Table 3
EXISTING STRUCTURE DEMOLITION WASTE CONTENT**

| Material | Percent Waste by Material (%) ¹ | Volume Waste by Material (CY) ² |
|-----------------------------|--|--|
| Structures | | |
| Concrete | 3% | 88 |
| Brick | 9% | 264 |
| Wood – Clean ³ | 29% | 851 |
| Wood – Treated ³ | 29% | 851 |
| Metal | 2% | 59 |
| Mixed debris | 20% | 587 |
| Trash | 8% | 235 |
| Structures Total | 100% | 2,933 |

Sources: FEMA 2010; CalRecycle 2002

¹ Estimated percentages for concrete, brick, wood, and metal provided by the Military Base Closure Handbook – A Guide to Construction and Demolition Materials Recovery (CalRecycle 2002) were broken down from the 72 percent of demolition materials remaining after subtracting 20 percent mixed debris and 8 percent trash. For example, the percent waste by material for concrete was generated by multiplying 72 percent by 4 percent (the concrete composition in wood structures) to yield 3 percent of the total waste generated during demolition.

² Table information subject to field verification during demolition.

³ For estimation purposes, wood waste materials are split 50 percent clean, and 50 percent treated to conservatively account for inability to recycle treated wood.

CY = cubic yard

¹ The *Military Base Closure Handbook – A Guide to Construction and Demolition Materials Recovery* has the percentage total of waste equaling 99 percent. This is likely due to rounding that was not disclosed in the document. To allow for balanced equations, 0.2 percent was added to concrete, brick, wood, and metal materials in the calculations.

It is assumed that treated wood, in addition to approximately eight percent of demolition waste, would not be recyclable. These materials would be disposed of at a local landfill at a zero percent diversion rate. The additional 20 percent of “mixed debris” demolition materials would be disposed of at a City-approved mixed debris materials recycling facility at a minimum 69 percent diversion rate (City 2023; Appendix A).

3.1.2 Pavement Demolition

Pavement demolition is expected to occur within areas paved with concrete and asphalt throughout the site during Project construction, including demolition of existing concrete walkways/sidewalks, curbs/gutters, and the asphalt parking lot. In total, the Project would include the removal of 6,000 SF of concrete and 30,000 SF of asphalt. Demolition estimates for these materials have been calculated based on the following assumptions:

- Demolition estimate for concrete assumes 4 inches thick and 150 pounds (lbs) per cubic foot. This would equate to approximately 300,000 lbs, or 150 tons, based on the 6,000 SF of existing on-site concrete to be demolished.
- Demolition estimate for asphalt assumes 5 inches thick and 142 lbs per cubic foot. This would equate to approximately 1,775,000 lbs, or 888 tons, based on the 30,000 SF of existing on-site asphalt to be demolished.

Therefore, the Project would result in a combined total of 2,075,000 lbs, or 1,038 tons, of concrete and asphalt to be demolished.

Salvage

Concrete may have the potential to be salvaged and reused on-site. As a conservative estimate, it is assumed that all pavement material will be removed from the site.

Recycling

Quantities of paved concrete and asphalt materials are estimated to total approximately 1,038 tons. The diversion rate for asphalt and concrete is 100 percent. Therefore, by adding 100 percent of the asphalt (888 tons) and 100 percent of the concrete (150 tons), the quantity diverted and recycled is estimated to total 1,038 tons.

3.2 CLEARING AND GRUBBING

Clearing and grubbing involves the removal of existing vegetation. Based on information provided by the Applicant, the Project is anticipated to require a net export of approximately 20 truckloads of removed vegetation consisting of brush, landscaping, trees, and grass during the clearing and grubbing process. There are approximately 16 CY of vegetation in an average truckload. Therefore, the Project is expected to require a net export of 320 CY of vegetation. Based on the City’s C&D Debris Conversion Rate Table, which identifies a weight of 0.15 tons/CY of vegetation (City 2016c; Appendix B), the net export of removed brush, landscaping, trees, and grass during the clearing and grubbing process is anticipated to be approximately 48 tons. Other waste materials associated with the clearing and grubbing are anticipated to include relatively negligible amounts of waste generated by contractors working on the site during the clearing and grubbing process.

Salvage

Although there is potential for some existing landscaping to be retained and reused on site, most of the existing ornamental landscaping within the Project is assumed to be removed.

Recycling

Vegetation would be processed and recycled at a target rate of 100 percent diversion at Miramar Greenery, a City-certified green waste recycling facility. The City's Certified C&D Recycling Facility Directory (City 2023; Appendix A) states the diversion rate for clean source-separated materials shall be 100 percent. Other waste materials associated with the clearing and grubbing are anticipated to include negligible amounts of waste generated by contractors working on the site during the clearing and grubbing process.

3.3 GRADING

According to information provided by the Applicant, grading is not anticipated to require a soil export or import.

In the case that minor amounts of soil export are required, excavated soil is designated as 100 percent for reuse or recycling. Excavated soil not reused is anticipated to be diverted at a rate of 100 percent to one of the facilities from the City's Certified C&D Recycling Facility Directory (City 2023; Appendix A). Certified facilities include the following:

- Alpine Asphalt and Concrete Recycling, 5690 Willows Road, Alpine, CA 91901
- Alpine Asphalt and Concrete Recycling, 0 Duro Road, Escondido, CA 92028
- Enniss Inc., 12421 Vigilante Road, Lakeside, CA 92040
- Hanson Aggregates West, Miramar, 9229 Harris Plant Road, San Diego, CA 92126
- Moody's, 3210 Oceanside Boulevard, Oceanside, CA 92056
- Robertson's Ready Mix, 2094 Willow Glen Drive, El Cajon, CA 92019
- Terra Bella Nursery, 302 Hollister Street, San Diego, CA 92154
- Vulcan Carol Canyon Landfill and Recycle Site, 10051 Black Mountain Road, San Diego, CA 92126

Other waste materials associated with grading are anticipated to include negligible amounts of waste generated by contractors working on site during the grading process.

3.4 SUMMARY OF PRE-CONSTRUCTION WASTE GENERATION AND DIVERSION

As discussed above, the waste materials to be generated during demolition, clearing and grubbing, and grading for Project implementation would be source-separated for recycling or reuse at City-certified facilities specializing in each material type, as applicable. A summary of anticipated waste generation volumes and diversion rates for pre-construction activities is provided in Table 4, *Pre-Construction Demolition, Clearing/Grubbing, and Grading Solid Waste Generation, Diversion Rates, and Facilities*. As shown in the table, during pre-construction the Project would generate 386 tons and divert 2,015 tons.

Table 4
PRE-CONSTRUCTION DEMOLITION, CLEARING/GRUBBING, AND GRADING SOLID WASTE GENERATION, DIVERSION RATES, AND FACILITIES

| Source of Material | Material | Volume (CY) | Tons/Unit Conversion Factor | Tons | Diversion Rate (Percent) | Facility/Destination of Materials | Tons Diverted | Tons Disposed |
|---------------------|------------------|-------------|-----------------------------|--------------|--------------------------|-----------------------------------|---------------|---------------|
| Building Demolition | Concrete | 88 | 1.2 | 106 | 100% | A | 106 | 0 |
| | Brick | 264 | 0.7 | 185 | 100% | A | 185 | 0 |
| | Clean Wood | 851 | 0.15 | 128 | 100% | B | 128 | 0 |
| | Treated Wood | 851 | 0.15 | 128 | 0% | C | 0 | 128 |
| | Paperboard | 0 | 0.05 | - | 100% | A | 0 | 0 |
| | Metal | 59 | 0.51 | 30 | 100% | A | 30 | 0 |
| | Mixed Debris | 587 | 1.19 | 698 | 69% | A | 482 | 216 |
| | Trash | 235 | 0.18 | 42 | 0% | C | 0 | 42 |
| Pavement Demolition | Asphalt/Concrete | -- | -- | 1,038 | 100% | A | 1,038 | 0 |
| Clearing/Grubbing | Vegetation | - | 0.15 | 48 | 100% | B | 48 | 0 |
| TOTAL | | | | 2,401 | 84% | -- | 2,015 | 386 |

Sources: City’s Certified C&D Recycling Facility Directory (City 2023; Appendix A), City’s C&D Debris Conversion Rate Table (City 2016c; Appendix B)

Facility/Destination Key:

A. Appropriate facility on City’s Certified C&D Recycling Facility Directory

B. Miramar Greenery, 5180 Convoy Street, San Diego, CA 92111

C. Sycamore Landfill, 8514 Mast Boulevard, Santee, CA 92071

Notes:

- Table information subject to field verification during pre-construction.
- The Applicant would contract with source separating recycling facilities listed in the City’s Certified C&D Recycling Facility Directory (City 2023) with an equal or greater diversion rate to ensure diversion rates meet those estimated in this table.
- The Tons/Unit Conversion Factor for concrete/steel was not provided in the City’s C&D Debris Conversion Rate Table; therefore, concrete’s factor of 1.2 was used in the estimates.
- Total diversion rate based on the percentage of total tons of waste diverted over the total tons of waste generated.

CF = cubic feet; CY = cubic yard

3.4.1 Summary of Salvage Material

Demolition of the buildings, parking lot, and curb/gutter/sidewalk would generate salvageable materials such as concrete to be used for aggregate, soils, etc. However, the values of salvage and recycling are not defined for the existing buildings, no specific inventory of reusable items has been conducted at this preliminary stage, and no salvage plan has been prepared. Therefore, the amount of salvage is undefined.

3.4.2 Summary of Recycled Material

Materials generated during pre-construction demolition, clearing and grubbing, and grading that are designated for recycling would be source separated on site during these activities. The City's Certified C&D Recycling Facility Directory, updated quarterly, states the diversion rate for these materials shall be 100 percent, except mixed C&D debris, which achieves a maximum 86 percent diversion rate at the Otay C&D/Inert Debris Processing Facility (City 2023).

4.0 CONSTRUCTION WASTE

To estimate the quantity of waste generated during construction, City ESD staff recommends assuming each material type (carpet, ceiling tiles, etc.) would approximately equal the square footage of each structure. This square footage can then be multiplied by the weight of the material and divided by 10 to account for 10 percent waste generated during the construction process. A 10 percent construction waste generation rate is a very conservative figure based on the following reasoning:

- The cost of purchasing construction materials in excess of the quantity required is prohibitive.
- Many materials, such as metal studs, come prefabricated in specific sizes, such that the contractor can accurately predict and purchase the specific quantity that would be required.
- Contractors can return unused and unneeded items (such as metal studs, appliances, fixtures, etc.) and/or utilize materials (such as brick or drywall) on other projects.
- Not all materials would be utilized throughout project square footage, so generation rates based on the total square footage are bound to be overestimated.

The Project proposes to build one main structure, a 100,169-SF building containing 92 residential units and associated facilities. The Project also proposes 5,886 SF of common areas.

In the International Building Code (IBC), the International Code Council (ICC) classifies buildings into five categories based on their type of construction (ICC 2015). Construction Type I buildings are considered to be fire resistive, often by using non-combustible materials such as steel with a fire-resistant coating and concrete. Construction Type II buildings typically have non-combustible walls but are not considered to be fire resistive. Construction Type III buildings are combustible, typically built with block or brick walls and a wooden roof. Buildings that utilize heavy timber in their framework are classified as Construction Type IV. Construction Type V buildings have wooden frames are considered to be combustible. The proposed building would be Type V construction (combustible).

The Project also would provide exterior “common areas,” which would include concrete and asphalt paving 7,086 SF for walkways/sidewalks, curb/gutter, and driveways/roadways within the property. Based on the proposed structures and common areas, the following building materials that may generate waste are likely to be used during construction:

- Wood/Heavy timber
- Drywall
- Carpet/Carpet padding
- Metals
- Concrete
- Asphalt
- Ceramic tile
- Ceiling tile
- Brick/Masonry
- Roofing materials

Other waste generated would consist of packaging materials from construction material, appliances, windows, etc., including the following:

- Corrugated cardboard (packaging)
- Industrial plastics (plastic wrap, fasteners, etc.)
- Styrofoam (appliance packaging, not peanuts)

4.1 ESTIMATE CONSTRUCTION WASTE GENERATION AND DIVERSION

The City uses a rule of thumb of 3 lbs/SF of waste materials generated during construction (3 lbs = 0.0015 tons). Material quantities are based on City guidance as follows:

- Total Project SF x each material type = Total quantity of construction materials required
- Total construction material required x 10 percent = Anticipated quantity of construction waste generated

Anticipated Project construction waste generation is shown in Table 5, *Construction Solid Waste Generation, Diversion Rates, and Facilities*.

**Table 5
CONSTRUCTION SOLID WASTE GENERATION, DIVERSION RATES, AND FACILITIES**

| Source of Material | New Gross SF | Material | Diversion Rate (Percent) ¹ | Tons Diverted ² | Tons Disposed |
|---|--------------|-----------------------|---------------------------------------|----------------------------|---------------|
| Project Residential Building | 100,169 | Metals | 100% | 15.0 | 0.0 |
| | | Concrete/Asphalt | 100% | 15.0 | 0.0 |
| | | Wood | 100% | 15.0 | 0.0 |
| | | Brick/Masonry | 100% | 15.0 | 0.0 |
| | | Drywall | 69% | 10.4 | 4.7 |
| | | Carpet/Carpet Padding | 69% | 10.4 | 4.7 |
| | | Mixed Debris | 69% | 10.4 | 4.7 |
| | | Trash | 0% | 0.0 | 15.0 |
| PROJECT RESIDENTIAL BUILDING TOTAL | | 76% | 91.2 | 29.0 | |
| Common Areas³ | 5,886 | Concrete/Asphalt | 100% | 0.9 | 0.0 |
| COMMON AREAS TOTAL | | 100% | 0.9 | 0.0 | |
| TOTAL | | | 76% | 92.1 | 29.0 |

¹ Trash would be taken to a local landfill at a zero percent diversion rate. All other construction debris would be taken to an appropriate facility listed on the City’s Certified C&D Recycling Facility Directory. Facilities that process metals, concrete/asphalt, and wood all achieve a 100 percent diversion rate for these materials. Facilities that process mixed debris achieve a minimum 69 percent diversion rate, which was conservatively assumed for this Project (City 2023; Appendix A).

² For each material type, construction waste quantities are calculated based on:
 Three lbs of waste per building SF (e.g., 100,169 SF for Building OAS7 x 3 lbs/SF = 300,507 lbs, or 150 tons);
 Total construction material required x 10 percent = anticipated quantity of construction waste generated (15 tons)

³ Common areas include pedestrian concrete paving and vehicular concrete paving.

Note that numbers may not total due to rounding.

lbs = pounds; SF = square feet/footage

4.1.1 Proposed Post-Consumer Content Construction Materials

To further minimize waste, the Project would utilize recycled content construction materials, where feasible. Given the preliminary nature of the Project plans, a minimum target of five percent is anticipated, with verification of purchase of materials equating to this target to be provided prior to or during the pre-construction meeting. See Section 6.1, for the construction waste management, coordination, and oversight measures that would be implemented pursuant to this WMP.

5.0 OCCUPANCY WASTE

5.1 STORAGE

The Project would be managed under the Applicant or its designee(s). The City’s Storage Ordinance (Municipal Code Section 142.0801 et seq.) requires the provision of separate bins for recyclable waste products to be separated from non-recyclable solid waste. To comply with the Storage Ordinance, recycling containers would be provided at convenient locations throughout the development, meeting or exceeding the minimums shown in Table 1.

5.2 WASTE GENERATION – EXISTING USES

The Project site’s existing uses that would be demolished as part of the Project are residential. To understand the change in waste generated during occupancy, estimates of existing waste generation of buildings that will be demolished were calculated. The City’s ESD provides a list of waste generation factors for the occupancy phase of development, included as Appendix C of this report (City 2012). Table 6, *Estimated Annual Solid Waste Generation and Diversion Rates – Existing Buildings*, shows the estimated waste generation and diversion for the existing buildings on the site.

Table 6
ESTIMATED ANNUAL SOLID WASTE GENERATION AND DIVERSION RATES – EXISTING BUILDINGS

| Source of Material | Square Footage | Existing Building Use | Tons/Year/Unit | Tons Generated (per year) | Expected Percent Diverted from Source-Separated Recycling ¹ | Tons Diverted (per year) | Tons Disposed (per year) |
|---------------------|-----------------|-----------------------|----------------|---------------------------|--|--------------------------|--------------------------|
| Existing Building 1 | 6,000 (6 units) | Multi-Family Unit | 1.2 | 7 | 50% | 3.5 | 3.5 |
| Existing Building 2 | 6,000 (6 units) | Multi-Family Unit | 1.2 | 7 | 50% | 3.5 | 3.5 |
| TOTAL | | | | 14 | -- | 7 | 7 |

¹ Reflects compliance with existing City Storage Ordinance and City Recycling Ordinance (City 2022b) and SB 1383. Note that numbers may not total due to rounding.

As shown in the table, the existing buildings planned to be demolished currently generate approximately 14 tons of waste. With compliance with the City’s Recycling Ordinance and SB 1383, the existing buildings are assumed to divert 50 percent, which estimates that 7 tons of waste generated by the existing use would be disposed and 7 tons would be diverted. These estimates are based on the City’s 2012 waste generation factors, and do not consider any additional sustainability measures and recycling or organic waste diversion programs that may be implemented by current vendors.

5.3 WASTE GENERATION – PROJECT USES

The estimated waste generation and diversion for the proposed buildings are shown in Table 7, *Estimated Annual Solid Waste Generation and Diversion Rates – Proposed Buildings*.

Table 7
ESTIMATED ANNUAL SOLID WASTE GENERATION AND DIVERSION RATES – PROPOSED BUILDINGS

| Source of Material | Square Footage | Proposed Building Use ¹ | Waste Generation Factor ¹ or tons/year/unit | Tons Generated (per year) | Expected Percent Diverted from Source-Separated Recycling ^{2,3} | Tons Diverted (per year) | Tons Disposed (per year) |
|------------------------------|--------------------|------------------------------------|--|---------------------------|--|--------------------------|--------------------------|
| Project Residential Building | 100,169 (92 units) | Multi-Family Unit | 1.2 | 110 | 50% | 55 | 55 |
| Community Area | 1,848 | Unclassified Services ⁴ | 0.0042 | 7.8 | 50% | 4 | 4 |
| TOTAL | | | | 117.8 | -- | 59 | 59 |

¹ Waste generation factors provided in Appendix C to this report; for buildings providing a variety of uses, the most conservative waste generation factor was used.

² Reflects compliance with existing City Storage Ordinance and City Recycling Ordinance (City 2022b) and SB 1383.

³ The Applicant would contract with City-approved recycling haulers and disposal facilities.

⁴ The community area is the indoor public use clubhouse area within the residential building

*Note that numbers may not total due to rounding.

As shown in the table, it is anticipated that at full buildout, approximately 59 tons of waste are anticipated to be disposed of annually, and approximately 59 tons are estimated to be diverted in association with the new building and associated structures. These estimates are based on the City’s 2012 waste generation factors, which do not take into consideration additional sustainability measures and recycling and organic waste diversion programs that may be implemented at the Project and exceed the overall 50 percent diversion estimated by the City for occupancy.

5.4 CHANGE IN WASTE GENERATION

Based on the difference between the existing buildings’ waste generation and the proposed Project’s waste generation, the Project would result in a net increase of 104 tons of waste. Using an estimated 50 percent diversion rate, which accounts for compliance with the City’s Storage Ordinance and Recycling Ordinance and SB 1383, 52 tons would be disposed, and 52 tons would be diverted from the landfill. As noted, these estimates are conservative based on the assigned building uses, and do not consider potential additional sustainability programs that are proposed to be implemented by the Project, as discussed in Chapter 6.0, below.

While the City’s Recycling Ordinance currently requires recycling of recyclable materials generated by residential and commercial facilities, City is in the process of implementing extensive procedural changes to comply with SB 1383 to increase diversion of organic waste starting in 2022 (City 2022b). Studies show that approximately 17 percent of the waste generated in the City and delivered for landfill disposal is paper and 32 percent is compostable organics (City 2022b; Municipal Code Section 66.0701). The City’s Zero Waste Plan evaluates the composition of the City’s waste-stream, with waste materials for commercial uses such as the proposed Project characterized as approximately 23.3 percent C&D materials; 21.5 percent paper; 17.4 percent food scraps; 14.2 percent organics (e.g., green waste); 11.6 percent plastic; and 11.8 percent other waste types such as special waste, metal, glass, mixed residue, electronics, and household hazardous waste (City 2015). Assuming compliance with the City’s forthcoming changes in organic waste diversion pursuant to SB 1383, the Project would divert a

minimum of 50 percent of organic waste generated on site. The Project would add organic waste disposal bins accompanied by educational information explaining how to dispose of compostable waste to building occupants. Additionally, organic waste generated by the Project's routine landscaping would be diverted from the landfill. Therefore, Project operation may exceed the 50 percent diversion rate; however, a 50 percent diversion is conservatively used in this analysis. Additional waste reduction, recycling, and diversion measures that would further reduce the Project's operational waste disposal are described below in Section 6.3.

6.0 WASTE REDUCTION, RECYCLING, AND DIVERSION MEASURES

The Applicant is committed to waste reduction during all aspects of Project demolition, grading, construction, and operation, and would incorporate the Waste Diversion Measures (WDM) described below to ensure compliance with applicable solid waste disposal and waste reduction regulations and ordinances. Mandatory compliance with these measures shall be included in all Project contractor agreements, clearly reflected on Project plans, and verifiable by City ESD staff through written submittals and/or site inspections as described below.

6.1 CONSTRUCTION WASTE MANAGEMENT, COORDINATION, AND OVERSIGHT

6.1.1 Contractor Agreements and City Coordination

All WDM described herein shall be included as part of contractor agreements and clearly reflected on Project plans identifying activities required to be undertaken during clearing, grading, and construction. These measures shall also be provided in checklist format to City ESD staff prior to the initiation of any activities identified in the WMP. ESD staff shall be allowed access to the Project site, Project plans, and contractor education program meetings and materials (described below) to verify conformance with these measures.

6.1.2 Designation of a Solid Waste Management Coordinator

Prior to initiation of any construction, clearing, grading, or grubbing activities on site, the Applicant shall designate a SWMC for the property with the authority to provide guidelines and procedures for contractor(s) and staff to implement waste reduction and recycling efforts. These responsibilities shall include, but are not limited to, the following:

- Prepare a Contractor Education Program on the waste separation and diversion/disposal procedures specified in this WMP. The Contractor Education Program shall contain, at a minimum, the following information:
 - Written and visual description of each waste type required to be source separated
 - Written and graphic description of how each waste type must be treated prior to and during source separation
 - Direction on which waste types go to mixed-debris facilities
 - Direction on which waste types go to the landfill

- Direction on materials requiring special handling, such as hazardous materials
 - Contact for designated contractor in case of questions or emergency
 - Contact at City ESD in case of questions or emergency
 - Phone number, address, and telephone contact information for each contracted hauler and disposal/diversion facility to be utilized
- Ensure the correct number and signage of bins, as specified in this WMP.
 - Ensure a maximum five percent contamination by different waste types/non-recyclable materials by weight in the bins.
 - Ensure no overtopping of bins occurs.
 - Work with contractor(s) to refine estimated quantities of each type of material that would be recycled, reused, or disposed of as waste, then assist contractor(s) with documentation of that waste through receipts at each recycling and landfill facility identified in this WMP, or as otherwise agreed to by ESD staff.
 - Issue stop work orders if procedures and standards specified in this WMP are not being followed/met.
 - Coordinate with ESD and/or Mitigation Monitoring staff, including regular communication and invitations to the work site, and ensure appropriate staff members are involved at every stage.
 - Ensure ESD staff attendance at the contractor education meeting and pre-construction meetings of each phase of the development.

6.1.3 Contractor Waste Management Training

The Project's SWMC or an ESD-approved contractor designee shall carry out Contractor Education Program presentations ensuring all Project personnel are trained regarding content and requirements of this WMP. Prior to beginning work on any portion of the Project, each member of the team, including all workers, subcontractors, and suppliers, shall be provided with a copy of the WMP, and undergo training on proper waste management procedures applicable to the Project.

- The Project's SMWC, or ESD-approved Contractor-designee shall carry out contractor waste management training presentations for each new group or individual hired, contracted, or assigned to work on the Project.
- The SMWC and/or Contractor-designee shall ensure that each person working on the Project has completed the waste management training by maintaining a written log to be signed and dated by each trainee upon completion of the training program. Copies of this written log, along with a list of all applicable personnel, shall be provided to City ESD staff for verification during each phase of Project activities.

6.1.4 Daily Site Inspections by Contractor(s)

The Project contractor(s) shall conduct daily inspections of the construction site to ensure compliance with the requirements of this WMP and with all other applicable laws and ordinances. Daily inspections shall include verifying the availability and number of dumpsters based on amount of debris being generated, verifying trash and recycled materials dumpsters are correctly labeled, ensuring proper sorting and segregation of materials, and ensuring excess materials are properly salvaged. The Project contractor(s) shall report the results of the daily site inspections to the SWMC.

6.1.5 Regular Removal of Waste Materials

The Project contractor(s) shall ensure removal of construction waste materials in sufficient frequency to prevent over-topping of bins. The accumulation and burning of on-site grading/land-clearing and construction waste materials shall be prohibited.

6.1.6 City Verification

The Applicant shall ensure a representative of the City's ESD attends pre-construction meetings prior to clearing, grading, and construction to ensure that the following items are verified:

- Material segregation, recycling, and reuse is occurring per the WMP;
- Soil is being transported to an appropriate facility for reuse;
- Grubbed materials are sent to a suitable green waste recycling facility;
- Contract documents have appropriate estimates and constraints to avoid "overbuying" construction materials;
- Contract documents specify methods to achieve five percent post-consumer content goal;
- Contamination levels (i.e., different waste types/non-recyclable materials) do not exceed five percent by weight;
- An appropriate diversion rate (as specified in this WMP) has been included on the deposit form;
- Contract documents specify agreements for each recyclable/reusable material type to be taken to an appropriate recycling/reuse facility, as specified in this WMP; and
- Minimum exterior refuse, organic waste, and recyclable material storage areas have been incorporated into Project plans, as a requirement of the City Storage Ordinance (Municipal Code Section 142.0801 et seq.).

6.2 CONSTRUCTION WASTE REDUCTION, DIVERSION COMPLIANCE, AND VERIFICATION

6.2.1 Identification, Separation, and Diversion of Recyclable/Reusable Materials

The Applicant shall ensure that:

- Throughout Project activities, waste materials shall be source separated on site into the appropriate bin based on materials type, according to the categories in this WMP. Materials generated during clearing, grading, and construction that would-be source separated and recycled are listed below:
 - Mixed C&D (wood, dirt, concrete, drywall, brick, metals, rock, asphalt, tile, cardboard)
 - Metals
 - Concrete/Asphalt
 - Brick/Masonry
 - Wood
 - Drywall
 - Carpet/Carpet padding
 - Clean fill dirt
 - Green waste
- A separate bin for each clean waste material type to be generated during each phase of clearing, grading, and construction activity shall be provided on the site, subject to the following requirements:
 - Containers shall be clearly labeled, with a list of acceptable and unacceptable materials. The list of acceptable materials must be the same as the materials recycled at the receiving material recovery facility or recycling processor.
 - The collection containers for recyclable grading/land-clearing and construction waste shall contain no more than five percent non-recyclable materials, by weight.
 - Regular visual inspections of dumpsters and recycling bins shall be conducted to remove contaminants.
 - Recycling areas shall be clearly identified with large signs. Lists of acceptable and unacceptable materials shall be posted on recycling bins and throughout the project site and all recycled material signage shall be visible on at least two sides of haul containers.
 - Recycling bins shall be placed in areas that would be readily accessible and would minimize misuse or contamination. The SWMC shall be responsible for these efforts and they shall be reviewed at pre-construction meetings and/or during contractor education meetings, if conducted separately.

- Recyclable and/or reusable waste materials collected in source-separated bins shall be diverted to recycling/reuse facilities as designated in Tables 4 and 5 of this WMP, or to another facility listed on the City's *Certified C&D Recycling Facility Directory*, should the designated facilities not be available.

6.2.2 Source Reduction Measures

Project contractors and subcontractors, in cooperation with the Project's SWMC and ESD staff, as applicable, shall coordinate to minimize the over-purchasing of construction materials to lower the amount of materials taken to recycling and disposal facilities. The Project shall minimize over-purchasing through purchase of pre-cut materials, whenever feasible. The following steps shall be undertaken:

- Detailed material estimates shall be used to reduce risk of unplanned and potentially wasteful material cuts.
- Contractor and subcontractor material purchasing agreements shall include a waste reduction provision requesting that: materials and equipment be delivered in packaging made of recyclable material; vendors reduce the amount of packaging; packaging be taken back by vendors for reuse or recycling; and vendors take back all unused product. Contracts containing this language shall be made available to ESD staff during ESD site visits for inspection.
- Post-consumer content products shall be employed in the design and construction of the new building and associated structures, with the goal of achieving five percent post-consumer content materials. Efforts to use post-consumer content may include using products manufactured with post-consumer content materials (i.e., products that were bought, used, and recycled by consumers), such as natural textiles, aggregate, or concrete. Receipts demonstrating post-consumer content shall be provided to ESD staff at or prior to the pre-construction meetings.
- Prior to submittal, final project plans shall indicate the anticipated source and quantity of materials to be reused on site, and the source, quantity, and percentage of post-consumer content waste products anticipated to be utilized for project construction.
- Contractors shall include the anticipated source and quantity of post-consumer content products proposed for reuse or purchase in their project bid.
- Final project plans inclusive of the information above shall be provided to ESD for verification.

6.3 OPERATIONAL WASTE MANAGEMENT AND DIVERSION MEASURES

The Applicant shall undertake and/or shall specify in contract language and/or sales/lease agreements with any tenant, operator, and/or future owner, a list of recycling and organic waste composting requirements with which the Applicant or future tenants, operators, and/or owners shall be obligated to comply, including, but not limited to:

- Recycling and organic waste composting areas shall be clearly identified with large signs.
- Lists of acceptable and unacceptable materials shall be posted on recycling and compost bins.
- All recycled and organic waste material signage shall be visible on at least two sides of recycling and organic waste containers.
- Recycling and compost bins shall be placed in areas that would be readily accessible and would minimize misuse or contamination.
- Prepare and distribute recycling and composting educational materials for inspection by ESD prior to certificate of occupancy.
- After materials are approved, distribute to all project site owners/occupants.
- Green waste generated by ongoing landscaping and landscape maintenance activities shall be source separated by the landscaping contractor and diverted to Miramar Greenery.
- Vendor(s) for on-site custodial duties shall be educated regarding the appropriate waste diversion program to ensure the proper handling of waste.
- Pursuant to SB 1383, all tenants, operators, and/or future owners shall subscribe to a City-certified organic waste collection service that either “source-separates” the waste (e.g., separate bins), or transports all unsegregated waste to a facility that recovers 75 percent of the organic content collected from the system.
- Organic waste shall be collected in separate container(s) for pick up weekly for yard trimmings, non-hazardous wood waste, food scraps, and food-soiled paper.

Prior to issuance of any certificate of occupancy/tentative certificate of occupancy, the Applicant shall invite a representative of the City ESD to:

- Inspect and approve storage areas that have been provided consistent with the City’s Storage Ordinance;
- Ensure that a hauler has been retained to provide recyclable and organic materials collection, and, if applicable, landscape waste collection; and
- Inspect and approve education materials for building tenants/owners that are required pursuant to the City’s Recycling Ordinance.

For specialized product purchasing (e.g., with recycled content) to be used during occupancy, the Applicant shall provide for inspection by ESD the documentation that would be used to carry out this requirement.

7.0 CONCLUSION

As discussed under Regulatory Framework, a project may result in a significant direct impact under the City CEQA Significance Thresholds if it generates more than 1,500 tons of solid waste materials during construction and demolition. Projects that include the construction, demolition, and/or renovation of 40,000 SF or more of building space or generate approximately 60 tons of waste or more are considered to have potentially significant cumulative impacts on solid waste services. Further, AB 341 requires the diversion of 75 percent of solid waste and mandatory provision of recycling collection service during occupancy.

7.1 SUMMARY OF WASTE GENERATION AND DIVERSION

During pre-construction demolition, clearing/grubbing, and grading, the Project would produce 2,401 tons of excavated soils, green waste, asphalt/concrete, and other C&D waste, and divert 2,015 tons of these materials from the landfill, as identified in Table 4. Approximately 386 tons of solid waste material generated during pre-construction is anticipated to be disposed of as non-recyclable/ non-reusable waste at a local landfill, for an overall pre-construction diversion rate of 84 percent.

During construction, the Project would produce approximately 121 tons of solid waste (metal, concrete, concrete/steel, asphalt, brick/masonry, wood, drywall, carpet/carpet padding, mixed debris, and trash), and divert 92.1 tons of solid waste materials from the landfill, as identified in Table 5. The diverted material would consist of clean, source-separated (segregated) recyclable and/or reusable material, as well as mixed debris, to be deposited at the recycling/reuse facilities identified in the City's Certified C&D Recycling Facility Directory (City 2023; Appendix A). Approximately 29 tons of solid waste material generated during construction is anticipated to be disposed of as non-recyclable/non-reusable waste at a local landfill, for an overall diversion rate during construction of approximately 76 percent.

With the combined pre-construction and construction phases, the Project would produce 2,522 tons of solid waste and would divert 2,107 tons. This would be an overall diversion rate during pre-construction and construction of 80 percent.

During occupancy, it has been estimated that the Project would generate an additional 104 tons of waste per year over existing conditions. Using an estimated 50-percent diversion rate, which is based on compliance with SB 1383, 52 tons per year are calculated to be diverted to recycling/reuse facilities (refer to Table 7). An additional 52 tons per year, or 50 percent of occupancy material generated, are estimated to be disposed of as non-recyclable/non-reusable waste at a local landfill. The Project would also be required to comply with the forthcoming changes in organic waste diversion pursuant to SB 1383, which requires diversion of a minimum of 50 percent of organic waste generated on site, and a minimum of 75 percent of organic waste generated on site by 2025. Thus, the Project is expected to achieve a waste diversion rate of greater than 50 percent overall. Additional waste reduction, recycling, and diversion measures would further reduce the Project's operational waste disposal.

7.2 COMPLIANCE WITH CITY AND STATE REGULATIONS

Project compliance with City and State regulations is addressed below.

7.2.1 State of California

Based on the quantified waste generation and diversion rates discussed above, the Project would exceed the 75 percent solid waste diversion rate for waste produced during the pre-construction and construction phases. The Project would fail to meet the 75 percent waste reduction target annually once the buildings are occupied. This shortcoming is overcome by the following factors:

- The segregation proposed during pre-construction and construction would achieve an overall 80 percent diversion rate, exceeding the 75 percent target.
- The project would incorporate mandatory waste reduction, recycling, and diversion measures as identified in Sections 6.1 and 6.2 of this WMP during pre-construction and construction, to further reduce solid waste impacts.
- The project would subscribe to an organic waste collection service that either “source-separates” the waste (e.g., separate bins), or transports all unsegregated waste to a facility that recovers 75 percent of the organic content collected from the system.
- Ongoing diversion of green waste (landscaping debris) to Miramar Greenery would avoid unnecessary contributions to the regional landfills.
- To minimize generation of waste materials, the project would incorporate recycled, post-consumer content materials in interiors and exteriors, to the extent practicable.

In addition to these measures implemented during pre-construction and construction activities, the Applicant would commit to the recycling requirements identified in Section 6.3 of this WMP, to further reduce solid waste impacts during occupancy.

7.2.2 City of San Diego

Based on the quantified waste generation and diversion rates discussed above, the Project would result in a significant impact regarding the City’s CEQA Significance Determination Threshold for direct impacts to solid waste facilities during demolition and construction.

The Project would be above the City’s threshold (generation of more than 1,500 tons of solid waste materials) for direct impacts to solid waste facilities during demolition and construction (2,401 + 121 = 2,522 tons C&D materials to regional landfills).

Regarding cumulative impacts, the Project proposes greater than 40,000 SF of building space, and the Project would be above the City’s CEQA Significance Determination Threshold of 60 tons for disposal of waste during C&D. During occupancy, the Project would achieve an average 50 percent diversion of waste via source-separated recycling and would dispose of approximately 104 additional tons of waste per year once the buildings are occupied, compared to existing conditions. This would exceed the City’s CEQA Significance Determination Threshold for cumulative impacts to solid waste services.

As mitigation, the City requires implementation of this document, a Project-specific WMP, to identify measures for waste reduction. These waste exceedances would be overcome by the waste reduction achieved during construction through measures described in Sections 6.1 and 6.2 of this WMP. Through the quantified waste generation and diversion rates discussed in this document, the Project would

exceed the 75 percent solid waste diversion rate for waste produced during demolition and construction phases by achieving an overall 80 percent diversion rate. In addition, the measures specified for operation in Section 6.3 of this WMP would provide adequate waste management. Regarding trash, organic waste, and recycling storage space during operation, for the proposed buildings, the Project would provide at least 576 SF of trash, organic waste, and recycling storage space, per the City Storage Ordinance (Table 1). The Project would comply with the City Recycling Ordinance by providing adequate space, bins, and educational materials for recycling and organic waste disposal during occupancy.

Through compliance with waste diversion measures included in this WMP, plus implementation of sustainability and efficiency features, the Project's direct solid waste impact would be less than significant and the Project's contribution to a cumulative solid waste generation would be reduced to a level that is less than cumulatively considerable.

8.0 LIST OF PREPARERS

| | |
|---------------|-------------------------------|
| Jason Runyan | Environmental Project Manager |
| Ellia Simmons | Environmental Planner |

9.0 REFERENCES

California Department of Resources Recycling and Recovery (CalRecycle). 2002. Military Base Closure Handbook – A Guide to Construction and Demolition Materials Recovery. As amended, January (prepared under former agency name “California Integrated Waste Management Board”).

Federal Emergency Management Agency (FEMA). 2010. Debris Estimating Field Guide (FEMA 329). Federal Emergency Management Agency, U.S. Department of Homeland Security. September. Available at: http://www.fema.gov/pdf/government/grant/pa/fema_329_debris_estimating.pdf.

Georgia Forestry Commission. 1990. Georgia Forest Research Paper 79. Tables for Estimating Total-Tree Weights, Stem Weights, and Volumes of Planted and Natural Southern Pines in the Southeast. September.

International Code Council (ICC). 2015. 2015 International Building Code, Chapter 6: Types of Construction. October. Available at: <https://codes.iccsafe.org/content/IBC2015/chapter-6-types-of-construction>.

San Diego, City of. 2023. 2023 Certified Construction & Demolition Recycling Facility Directory. Environmental Services Department. January 11. Accessed January 17. Available at: <https://www.sandiego.gov/sites/default/files/certified-cd-recycling-facility-directory.pdf>.

2022a. Refuse, Organic Waste, and Recyclable Materials Storage Regulations (Municipal Code Chapter 14, Article 2 Division 8). February 26.

2022b. Recycling Ordinance Update. Accessed July 28. Available at: <https://www.sandiego.gov/environmental-services/recycling/ro>.

2022c. California Environmental Quality Act Significance Determination Thresholds. July.

2016a. Construction and Demolition Debris Deposit Ordinance (Municipal Code Chapter 6, Article 6, Division 6). June.

2016b. Construction and Demolition (C&D) Debris Recycling Fact Sheet. June 29. Available at: https://www.sandiego.gov/sites/default/files/legacy/development-services/pdf/industry/infobulletin/cd_fact_sheet_6_29_16.pdf.

2016c. City of San Diego Construction & Demolition Debris Conversion Rate Table. June 6.

2015. City of San Diego Zero Waste Plan. July. Available at: <https://www.sandiego.gov/sites/default/files/legacy/mayor/pdf/2015/ZeroWastePlan.pdf>.

2013. California Environmental Quality Act: Guidelines for a Waste Management Plan. June.

2012. City of San Diego Waste Generation Factors – Occupancy Phase. October 1.

State of California. 1989. California Integrated Waste Management Act of 1989. State of California Assembly Bill 939.

Appendix A

Certified Construction & Demolition Recycling Facility Directory



• **Material taken to a landfill is DISPOSAL. NO diversion credit is given for any material taken to a landfill.**

• You must use one of these facilities to receive diversion credit.

• Please call ahead to confirm details such as accepted materials, days and hours of operation, limitations on vehicle types, and cost.

• Ensure the project address and permit number are on the receipt.

The facilities marked below with an asterisk are transfer stations

IMPORTANT DRIVER INSTRUCTIONS - If you deliver to a transfer station, you must have your driver:

- State that your load is Construction and Demolition (C&D) debris, and ensure it is coded correctly on the receipt.

- Tickets coded as "MSW, trash, or refuse" will receive 0% credit.

| | Asphalt/Concrete | Brick/Block/Rock | Building Materials for Reuse | Cardboard | Carpet | Carpet Padding | Ceiling Tile | Ceramic Tile/Porcelain | Clean Fill Dirt | Clean Wood/Green Waste | Drywall | Industrial Plastics | Lamps/Light Fixtures | Metal | Mixed Inerts | Styrofoam Blocks | Trash | Mixed C & D Debris |
|--|------------------|------------------|------------------------------|-----------|--------|----------------|--------------|------------------------|-----------------|------------------------|---------|---------------------|----------------------|-------|--------------|------------------|-------|--------------------|
| *EDCO Recovery & Transfer* 3660 Dalbergia St, San Diego, CA 92113 619-234-7774 www.edcodisposal.com | • | | | | | | | | | • | | | | | | | • | 69% |
| *EDCO Station Transfer Station & Buy Back Center* 8184 Commercial St, La Mesa, CA 91942 619-466-3355 www.edcodisposal.com | • | | • | | | | | | | • | | • | | | | | • | 69% |
| *EDCO CDI Recycling & Buy Back Center* 224 S. Las Posas Rd, San Marcos, CA 92078 760-744-2700 www.edcodisposal.com | | | • | • | • | | | | | | | • | | | | | • | 77% |
| Escondido Resource Recovery 1044 W. Washington Ave, Escondido 760-745-3203 www.edcodisposal.com | | | | | | | | | | | | | | | | | | 69% |
| *Fallbrook Transfer Station & Buy Back Center* 550 W. Aviation Rd, Fallbrook, CA 92028 760-728-6114 www.edcodisposal.com | | | • | | | | | | | | | • | | | | | • | 69% |
| Otay C&D/Inert Debris Processing Facility 1700 Maxwell Rd, Chula Vista, CA 91913 619-421-3773 www.sd.disposal.com | | | | | | | | | | | | | | | | | | 86% |
| *Ramona Transfer Station & Buy Back Center* 324 Maple St, Ramona, CA 92065 760-789-0516 www.edcodisposal.com | | | • | | | | | | | | | • | | | | | • | 69% |
| SANCO Resource Recovery & Buy Back Center 6750 Federal Blvd, Lemon Grove, CA 91945 619-287-5696 www.edcodisposal.com | | | • | • | • | | | | | | | • | | | | | | 69% |
| Allan Company 6733 Consolidated Wy, San Diego, CA 92121 858-578-9300 www.allancompany.com/facilities | | | • | | | | | | | | | • | | | | | | |
| Allan Company Miramar Recycling 5165 Convoy St, San Diego, CA 92111 858-268-8971 www.allancompany.com/facilities | | | • | | | | | | | | | • | | | | | | |
| Alpine Asphalt & Concrete Recycling 5690 Willows Rd, Alpine, CA 91901 760-451-6481 www.alpineasphaltandconcrete.com | • | • | • | | | | | • | | | | | | | | | | |
| Alpine Asphalt & Concrete Recycling 0 Duro Rd, Escondido, CA 92028 760-451-6481 www.alpineasphaltandconcrete.com | • | • | • | | | | | • | | | | | | | | | | |
| Aquafil Carpet Collection 187 Mace St, Chula Vista, CA 91911 619-816-0787 www.aquafil.com | | | | • | • | | | | | | | | | | | | | |



- **Material taken to a landfill is DISPOSAL. NO diversion credit is given for any material taken to a landfill.**
- You must use one of these facilities to receive diversion credit.
- Please call ahead to confirm details such as accepted materials, days and hours of operation, limitations on vehicle types, and cost.
- Ensure the project address and permit number are on the receipt.

***If using a transfer station, you must:**

- State that your load is Construction and Demolition (C&D) debris, and ensure it is coded correctly on the receipt.
- Tickets coded as "MSW, trash, or refuse" will receive 0% credit.

| | Asphalt/Concrete | Brick/Block/Rock | Building Materials for Reuse | Cardboard | Carpet | Carpet Padding | Ceiling Tile | Ceramic Tile/Porcelain | Clean Fill Dirt | Clean Wood/Green Waste | Drywall | Industrial Plastics | Lamps/Light Fixtures | Metal | Mixed Inerts | Styrofoam Blocks | Trash | Mixed C & D Debris |
|--|------------------|------------------|------------------------------|-----------|--------|----------------|--------------|------------------------|-----------------|------------------------|---------|---------------------|----------------------|-------|--------------|------------------|-------|--------------------|
| Aquafil Carpet Collection 7720 Formula Pl, San Diego , CA 92126 602-562-0444 www.aquafil.com | | | | | • | • | | | | | | | | | | | | |
| Armstrong World Industries, Inc. 300 S. Myrida St, Pensacola, FL 32505 877-276-7876 (Press 1, Then 8) www.armstrong.com/commceilingsna | | | | | | • | | | | | | | | | | | | |
| CMS Recycling Inc. 1428 West Mission Rd, Escondido, CA 92029 760-741-6300 www.cmsmetals.com | | | • | | | | | | | | | • | | | | | | |
| DFS Flooring 10178 Willow Creek Rd, San Diego, CA 92131 858-630-5200 www.dfsflooring.com | | | | • | • | | | | | | | | | | | | | |
| Duco Metals 220 Bingham Drive Suite 100, San Marcos, CA 92069 760-747-6330 www.ducometals.com | | | | | | | | | | | | • | | | | | | |
| Enniss Inc. 12421 Vigilante Road, Lakeside, CA 92040 619-443-9024 www.ennissinc.com | • | • | | | | | • | • | | | | | | | | | | |
| Escondido Materials 500 N. Tulip St, Escondido, CA 92025 760-432-4690 www.weirasphalt.com | • | | | | | | | | | | | | | | | | | |
| F.J. Willert Contracting 2385 Cactus Rd, San Diego, CA 92154 619-421-1980 www.fjwillert.com | • | | | | | | | | | | | | | | | | | |
| Habitat for Humanity ReStore 8101 Mercury Ct, San Diego, CA 92108 619-516-5267 www.sandiegohabitat.org | | | • | | | | | | | | | | | | | | | |
| Hanson Aggregates - Hollister St 389 Hollister St, San Diego, CA 92154 858-974-3849 | • | | | | | | | | | | | | | | | | | |
| Hanson Aggregates West - Lakeside Plant 12560 Highway 67, Lakeside, CA 92040 858-547-2141 | • | | | | | | | | | | | | | | | | | |
| Hanson Aggregates West - Miramar 9229 Harris Plant Rd, San Diego, CA 92126 858-974-3849 | • | | | | | | | • | | | | | | | | | | |



- **Material taken to a landfill is DISPOSAL. NO diversion credit is given for any material taken to a landfill.**
- You must use one of these facilities to receive diversion credit.
- Please call ahead to confirm details such as accepted materials, days and hours of operation, limitations on vehicle types, and cost.
- Ensure the project address and permit number are on the receipt.

***If using a transfer station, you must:**

- State that your load is Construction and Demolition (C&D) debris, and ensure it is coded correctly on the receipt.
- Tickets coded as "MSW, trash, or refuse" will receive 0% credit.

| | Asphalt/Concrete | Brick/Block/Rock | Building Materials for Reuse | Cardboard | Carpet | Carpet Padding | Ceiling Tile | Ceramic Tile/Porcelain | Clean Fill Dirt | Clean Wood/Green Waste | Drywall | Industrial Plastics | Lamps/Light Fixtures | Metal | Mixed Inerts | Styrofoam Blocks | Trash | Mixed C & D Debris | |
|---|------------------|------------------|------------------------------|-----------|--------|----------------|--------------|------------------------|-----------------|------------------------|---------|---------------------|----------------------|-------|--------------|------------------|-------|--------------------|--|
| HVAC Exchange 2675 Faivre St, Chula Vista, CA 91911 619-423-1564 www.hvacx.com | | | | | | | | | | | | | | • | | | | | |
| Inland Pacific Resource Recovery 12650 Slaughterhouse Canyon Rd, Lakeside, CA 92040 619-390-1418 www.iprrgreen.com | | | | | | | | • | | | | | | | | | | | |
| Los Angeles Fiber Company 4920 S. Boyle Ave, Vernon, CA 90058 323-589-5637 www.lafiber.com | | | | • | • | | | | | | | | | | | | | | |
| Miramar Greenery, City of San Diego 5180 Convoy St, San Diego, CA 92111 858-694-7000 www.miramargreenery.com | • | | | | | | | • | | | | | | | | | | | |
| Moody's 3210 Oceanside Blvd, Oceanside, CA 92056 760-433-3316 www.moodyselcorazonrecycling.com | • | | | | | | | • | | | | | • | | | | | | |
| RAMCO 8354 Nelson Way, Escondido, CA 92026 760-205-1797 www.ramco.us.com | • | | | | | | | | | | | | | | | | | | |
| Reclaimed Aggregates Chula Vista 855 Energy Way, Chula Vista, CA 91913 619-656-1836 | • | | | | | | | | | | | | • | | | | | | |
| Robertson's Ready Mix 2094 Willow Glen Dr, El Cajon, CA 92019 619-593-1856 www.rrmca.com | • | | | | | | | • | | | | | • | | | | | | |
| Rockridge Crushing 12485 Highway 67, Lakeside, CA 92040 619-324-7065 | • | | | | | | | | | | | | | | | | | | |
| SA Recycling 3055 Commercial St, San Diego, CA 92113 619-238-6740 www.sarecycling.com | | | | | | | | | | | | | • | | | | | | |
| SA Recycling 1211 S. 32nd St, San Diego, CA 92113 619-234-6691 www.sarecycling.com | | | | | | | | | | | | | • | | | | | | |
| San Pasqual Valley Soils 16111 Old Milky Way, Escondido, CA 92027 760-746-4769 www.spvsoils.com | | | | | | | | • | | | | | | | | | | | |



• Material taken to a landfill is DISPOSAL. NO diversion credit is given for any material taken to a landfill.

• You must use one of these facilities to receive diversion credit.

• Please call ahead to confirm details such as accepted materials, days and hours of operation, limitations on vehicle types, and cost.

• Ensure the project address and permit number are on the receipt.

***If using a transfer station, you must:**

- State that your load is Construction and Demolition (C&D) debris, and ensure it is coded correctly on the receipt.

- Tickets coded as "MSW, trash, or refuse" will receive 0% credit.

| | Asphalt/Concrete | Brick/Block/Rock | Building Materials for Reuse | Cardboard | Carpet | Carpet Padding | Ceiling Tile | Ceramic Tile/Porcelain | Clean Fill Dirt | Clean Wood/Green Waste | Drywall | Industrial Plastics | Lamps/Light Fixtures | Metal | Mixed Inerts | Styrofoam Blocks | Trash | Mixed C & D Debris |
|--|------------------|------------------|------------------------------|-----------|--------|----------------|--------------|------------------------|-----------------|------------------------|---------|---------------------|----------------------|-------|--------------|------------------|-------|--------------------|
| SCOR Industries 2321 South Willow Ave, Bloomington, CA 92316 909-820-5046 www.scorindustries.com | • | • | • | | | • | | • | • | • | | • | • | | | | | |
| Terra Bella Nursery 302 Hollister St, San Diego, CA 92154 619-585-1118 www.terrabellanursery.com | | | | | | | | • | • | | | | | | | | | |
| Vulcan Carol Canyon Landfill and Recycle Site 10051 Black Mountain Rd, San Diego, CA 92126 858-530-9465 www.vulcanmaterials.com | • | • | | | | | | • | | | | | | • | | | | |
| Vulcan Materials Company 2275 Hard Rock Rd, Chula Vista, CA 91913 858-530-9472 www.vulcanmaterials.com | • | | | | | | | | | | | | | | | | | |
| Vulcan Otay Asphalt Recycle Center 7522 Paseo de la Fuente, San Diego, CA 92154 619-571-1945 www.vulcanmaterials.com | • | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |
| | | | | | | | | | | | | | | | | | | |

Appendix B

City of San Diego C&D Debris Conversion Rate Table



CITY OF SAN DIEGO

Construction & Demolition (C&D) Debris

Conversion Rate Table

This worksheet lists materials typically generated from a construction or demolition project and provides formulas for converting common units (i.e. cubic yards, square feet, and board feet) to tons. It is a tool that should be used for preparing your Waste Management Form - Part I, which requires that quantities be provided in tons.

Note: Weigh receipts are required for your refund request.

Step 1: Enter the estimated quantity for each applicable material in Column I, based on units
Step 2: Multiply by Tons/Unit figure listed in Column II. Enter the result for each material in Column III.
 If using Excel version, column III will automatically calculate tons.
Step 3: Enter quantities for each separated material from Column III on this worksheet into the corresponding section of your Waste Management Form - Part I.

| Category | Material | Column I | | Column II | | Column III |
|---|---------------------------|----------|-------|------------|----------|------------|
| | | Volume | Unit | Tons/Unit | Tons | |
| Asphalt/Concrete | Asphalt (broken) | _____ | cy | x | 0.70 | = _____ |
| | Concrete (broken) | _____ | cy | x | 1.20 | = _____ |
| | Concrete (solid slab) | _____ | cy | x | 1.30 | = _____ |
| Brick/Masonry/Tile | Brick (broken) | _____ | cy | x | 0.70 | = _____ |
| | Brick (whole, palletized) | _____ | cy | x | 1.51 | = _____ |
| | Masonry Brick (broken) | _____ | cy | x | 0.60 | = _____ |
| | Tile | _____ | sq ft | x | 0.00175 | = _____ |
| Building Materials (doors, windows, cabinets, etc.) | | _____ | cy | x | 0.15 | = _____ |
| Cardboard (flat) | | _____ | cy | x | 0.05 | = _____ |
| Carpet | By square foot | _____ | sq ft | x | 0.0005 | = _____ |
| | By cubic yard | _____ | cy | x | 0.30 | = _____ |
| Carpet Padding/Foam | | _____ | sq ft | x | 0.000125 | = _____ |
| Ceiling Tiles | Whole (palletized) | _____ | sq ft | x | 0.0003 | = _____ |
| | Loose | _____ | cy | x | 0.09 | = _____ |
| Drywall (new or used) | 1/2" (by square foot) | _____ | sq ft | x | 0.0008 | = _____ |
| | 5/8" (by square foot) | _____ | sq ft | x | 0.00105 | = _____ |
| | Demo/used (by cubic yd) | _____ | cy | x | 0.25 | = _____ |
| Earth | Loose/Dry | _____ | cy | x | 1.20 | = _____ |
| | Excavated/Wet | _____ | cy | x | 1.30 | = _____ |
| | Sand (loose) | _____ | cy | x | 1.20 | = _____ |
| Landscape Debris (brush, trees, etc) | | _____ | cy | x | 0.15 | = _____ |
| Mixed Debris | Construction | _____ | cy | x | 0.18 | = _____ |
| | Demolition | _____ | cy | x | 1.19 | = _____ |
| Scrap metal | | _____ | cy | x | 0.51 | = _____ |
| Shingles, asphalt | | _____ | cy | x | 0.22 | = _____ |
| Stone (crushed) | | _____ | cy | x | 2.35 | = _____ |
| Unpainted Wood & Pallets | By board foot | _____ | bd ft | x | 0.001375 | = _____ |
| | By cubic yard | _____ | cy | x | 0.15 | = _____ |
| Garbage/Trash | | _____ | cy | x | 0.18 | = _____ |
| Other (estimated weight) | | _____ | cy | x estimate | | = _____ |
| | | _____ | cy | x estimate | | = _____ |
| | | _____ | cy | x estimate | | = _____ |
| Total All | | | | | | _____ |

Appendix C

City of San Diego Waste Generation
Factors – Occupancy Phase

Waste Generation Factors – Occupancy Phase

The following factors are used by the City of San Diego Environmental Services Department to estimate the expected waste generation in a new residential or commercial development.

Residential Uses

Residential Unit = 1.6 tons/year/unit
 Multi-family Unit = 1.2 tons/year/unit

Example: To calculate the amount of waste that will be generated from a project with 100 new homes, multiply the number of homes by the generation factor.

100 single family homes x 1.6 = 160 tons/year
 100 multi-family units x 1.2 = 120 tons/year

Commercial/Industrial Uses

| | |
|-----------------------|--------|
| General Retail | 0.0028 |
| Restaurants & Bars | 0.0122 |
| Hotels/Motels | 0.0045 |
| Food Stores | 0.0073 |
| Auto/Service/Repair | 0.0051 |
| Medical Offices | 0.0033 |
| Hospitals | 0.0055 |
| Office | 0.0017 |
| Transp/Utilities | 0.0085 |
| Manufacturing | 0.0059 |
| Education | 0.0013 |
| Unclassified Services | 0.0042 |

Example: To calculate the amount of waste that could be generated from a new building with 10,000 square feet for offices and 10,000 square feet for manufacturing, multiply the square footage for each use by the generation factor.

10,000 square feet x 0.0017 = 17 tons/year

10,000 square feet x 0.0059 = 59 tons per year

Total estimated waste generation for building = 76 tons/year
