

# City of San Diego

**CONTRACTOR'S NAME:** VSS International, Inc.  
**ADDRESS:** 3785 Channel Drive, West Sacramento, CA 95691  
**TELEPHONE NO.:** (916) 373-1500 **FAX NO.:** \_\_\_\_\_  
**CITY CONTACT:** Juan E. Espindola, Senior Contract Specialist, Email: [JEEpindola@sandiego.gov](mailto:JEEpindola@sandiego.gov)  
Phone No. (619) 533-4491  
A. Vance / E. Wildberger / R. Dinjotian

## BIDDING DOCUMENTS



**FOR**

## SLURRY SEAL GROUP 2023

**BID NO.:** K-21-1975-DBB-3  
**SAP NO. (WBS/IO/CC):** 21004779  
**CLIENT DEPARTMENT:** 2116  
**COUNCIL DISTRICT:** 1, 5, 6, 7  
**PROJECT TYPE:** ID

**THIS CONTRACT WILL BE SUBJECT TO THE FOLLOWING:**

- THE CITY'S SUBCONTRACTING PARTICIPATION REQUIREMENTS FOR SLBE PROGRAM
- PREVAILING WAGE RATES: STATE  FEDERAL
- APPRENTICESHIP

**BID DUE DATE:**

**2:00 PM**  
**DECEMBER 1, 2020**

**CITY OF SAN DIEGO'S ELECTRONIC BIDDING SITE, PLANETBIDS**

<http://www.sandiego.gov/cip/bidopps/index.shtml>

**ENGINEER OF WORK**

The engineering Specifications and Special Provisions contained herein have been prepared by or under the direction of the following Registered Engineer:

  
\_\_\_\_\_  
For City Engineer

10/13/2020  
Date

Seal:



## TABLE OF CONTENTS

SECTION	PAGE
1. REQUIRED DOCUMENTS SCHEDULE .....	4
2. NOTICE INVITING BIDS.....	6
3. INSTRUCTIONS TO BIDDERS.....	10
4. PERFORMANCE AND PAYMENT BONDS .....	20
5. ATTACHMENTS:	
A. SCOPE OF WORK .....	23
B. RESERVED .....	25
C. RESERVED .....	26
D. PREVAILING WAGE.....	27
E. SUPPLEMENTARY SPECIAL PROVISIONS .....	31
1. Appendix A - Notice of Exemption .....	65
2. Appendix B - Fire Hydrant Meter Program.....	77
3. Appendix C - Materials Typically Accepted by Certificate of Compliance .....	91
4. Appendix D - Sample City Invoice with Cash Flow Forecast.....	93
5. Appendix E - Sample Contractor’s Daily Quality Control Inspection Report.....	96
6. Appendix F - Sample of Public Notice .....	101
7. Appendix G - List of Proposed Work.....	103
8. Appendix H - Overall Location Map.....	109
9. Appendix I - Resurfacing Limit Maps.....	111
10. Appendix J - Project Street List .....	125
F. RESERVED .....	132
G. CONTRACT AGREEMENT .....	133
6. CERTIFICATIONS AND FORMS .....	136

## REQUIRED DOCUMENTS SCHEDULE DURING BIDDING AND AWARDING

The Bidder's attention is directed to the City's Municipal Code §22.0807(e), (3)-(5) for important information regarding grounds for debarment for failure to submit required documentation.

The specified Equal Opportunity Contracting Program (EOCP) forms are available for download from the City's web site at:

<http://www.sandiego.gov/eoc/forms/index.shtml>

ITEM	DOCUMENT TO BE SUBMITTED	WHEN DUE	FROM
1.	Bid Bond (PDF via PlanetBids)	At Time of Bid	ALL BIDDERS
2.	Contractors Certification of Pending Actions	At Time of Bid	ALL BIDDERS
3.	Mandatory Disclosure of Business Interests	At Time of Bid	ALL BIDDERS
4.	Debarment and Suspension Certification for Prime Contractors	At Time of Bid	ALL BIDDERS
5.	Debarment and Suspension Certification for Subcontractors, Suppliers & Mfgs	At Time of Bid	ALL BIDDERS
6.	Bid Bond (Original)	By 5PM 3 working days after bid opening	5 APPARENT LOW BIDDERS
7.	SLBE Good Faith Effort Documentation	By 5PM 3 working days of bid opening	ALL BIDDERS
8.	Form AA60 – List of Work Made Available	By 5 PM Within 3 working days of bid opening with Good Faith Effort (GFE) documentation	ALL BIDDERS
9.	If the Contractor is a Joint Venture: <ul style="list-style-type: none"> <li>• Joint Venture Agreement</li> <li>• Joint Venture License</li> </ul>	Within 10 working days of receipt by bidder of contract forms	APPARENT LOW BIDDER
10.	Payment & Performance Bond; Certificates of Insurance & Endorsements; and Signed Contract Agreement Page	Within 10 working days of receipt by bidder of contract forms and NOI	APPARENT LOW BIDDER



ITEM	DOCUMENT TO BE SUBMITTED	WHEN DUE	FROM
11.	Listing of "Other Than First Tier" Subcontractors	Within 10 working days of receipt by bidder of contract forms	APPARENT LOW BIDDER

## NOTICE INVITING BIDS

1. **SUMMARY OF WORK:** This is the City of San Diego's (City) solicitation process to acquire Construction services for **Slurry Seal Group 2023**. For additional information refer to Attachment A.
2. **FULL AND OPEN COMPETITION:** This solicitation is subject to full and open competition and may be bid by Contractors on the City's approved Prequalified Contractors List. For information regarding the Contractors Prequalified list visit the City's web site: <http://www.sandiego.gov>.
3. **ESTIMATED CONSTRUCTION COST:** The City's estimated construction cost for this project is **\$4,640,000**.
4. **BID DUE DATE AND TIME ARE: DECEMBER 1, 2020 at 2:00 PM**
5. **PREVAILING WAGE RATES APPLY TO THIS CONTRACT:** Refer to Attachment D.
6. **LICENSE REQUIREMENT:** To be eligible for award of this contract, Prime contractor must possess the following licensing classifications: **A or C-12 or C-32**
7. **SUBCONTRACTING PARTICIPATION PERCENTAGES:** Subcontracting participation percentages apply to this contract.
  - 7.1. The City has incorporated **mandatory** SLBE-ELBE subcontractor participation percentages to enhance competition and maximize subcontracting opportunities. For the purpose of achieving the mandatory subcontractor participation percentages, a recommended breakdown of the SLBE and ELBE subcontractor participation percentages based upon certified SLBE and ELBE firms has also been provided to achieve the mandatory subcontractor participation percentages:

1. SLBE participation	<b>7.3%</b>
2. ELBE participation	<b>7.8%</b>
3. Total mandatory participation	<b>15.1%</b>
  - 7.2. The Bid may be declared non-responsive if the Bidder fails to meet the following requirements:
    - 7.2.1. Include SLBE-ELBE certified subcontractors at the overall mandatory participation percentage identified in this document; OR
    - 7.2.2. Submit Good Faith Effort documentation, saved in searchable Portable Document Format (PDF) and stored on a Universal Serial Bus (USB) Type-A, Compact Disc (CD) or Digital Video Disc (DVD), demonstrating the Bidder made a good faith effort to outreach to and include SLBE-ELBE Subcontractors required in this document within 3 Working Days of the Bid opening if the overall mandatory participation percentage is not met.

Due to circumstances related to Covid-19, until further notice, all submittals in searchable PDF shall be submitted electronically within the prescribed time

identified in the contract documents via a File Cloud link provided by the Contract Specialist to all bidders.

Upon circumstances returning to normal business as usual, the GFE shall once again be submitted to:

Engineering & Capital Projects Department, Contracts Division  
525 B Street, Suite 750 (7th Floor)  
San Diego, California, 92101  
Attention: Juan E. Espindola

**8. AWARD PROCESS:**

- 8.1.** The Award of this contract is contingent upon the Contractor's compliance with all conditions of Award as stated within these documents and within the Notice of Intent to Award.
- 8.2.** Upon acceptance of bids and determination of the apparent low bidder, the City will prepare the contract documents for execution within approximately 21 days of the date of the bid opening. The City will then award the contract upon receipt of properly signed Contract, bonds, and insurance documents.
- 8.3.** This contract will be deemed executed and effective only upon the signing of the Contract by the Mayor or his designee and approval as to form by the City Attorney's Office.
- 8.4.** The low Bid will be determined by the Base Bid.
- 8.5.** Once the low bid has been determined, the City may, at its sole discretion, award the contract for the Base bid alone.

**9. SUBMISSION OF QUESTIONS:**

- 9.1.** The Director (or Designee) of the Engineering & Capital Projects Department is the officer responsible for opening, examining, and evaluating the competitive Bids submitted to the City for the acquisition, construction and completion of any public improvement except when otherwise set forth in these documents. Any questions related to this solicitation shall be submitted to:

Engineering & Capital Projects Department, Contracts Division  
525 B Street, Suite 750 (7<sup>th</sup> Floor)  
San Diego, California, 92101  
Attention: Juan E. Espindola

OR:

[JEEspindola@sandiego.gov](mailto:JEEspindola@sandiego.gov)

- 9.2.** Questions received less than 14 days prior to the date for opening of Bids may not be considered.
- 9.3.** Questions or clarifications deemed by the City to be material shall be answered via issuance of an addendum and posted to the City's online bidding service.

- 9.4.** Only questions answered by formal written addenda shall be binding. Oral and other interpretations or clarifications shall be without legal effect. It is the Bidder's responsibility to be informed of any addenda that have been issued and to include all such information in its Bid.

**10. OPTION TO RENEW:**

- 10.1.** The City of San Diego expects to have additional miles of streets Slurry Coated by contract with additional funding this fiscal year or next fiscal year. The City of San Diego reserves the right to exercise one option to renew this contract at the City's sole discretion under the terms and conditions herein stated, with the work to be performed commencing no later than 180 days after completion of the original contract work. The option to renew must be exercised by the City within 365 days after the date of the bid opening for this project. By submitting this bid, the bidder agrees that it shall not decline the City's option to renew.
- 10.2.** The option to renew, if exercised, will be for one or more of the line items noted above as determined by the City, for quantities to be specified by the City that will be within 25% of the quantities listed, with the total price to be adjusted in proportion to the quantities specified. The time for performance of the additional work shall be the same as the time for completion of the original contract work, adjusted proportionately by the amount of the additional work compared to the amount of the original contract work.
- 10.3.** The option to renew shall be made at the bid pricing structure of the Bidder's original bid. In the event that the California Statewide Paving Asphalt Price Index (Index) has changed plus or minus ( $\pm$ ) 10% between the date of Bid opening ("Bid Opening Date") and the date the option to renew is exercised by the City ("Option Exercise Date"), the City may, at the Bidder's request, and at the City's sole discretion, grant a change to the pricing structure commensurate with the percentage change in the Index.
- 10.4.** If deemed necessary by the City, the option to renew will be exercised in writing by the City within 1 year of the date of the Bid opening for this project. The following conditions apply to the option to renew:
- 10.4.1.** The total price of the option to renew shall not exceed the original contract amount. The option to renew will be for one or more of the listed Bid items as determined by the City, for quantities to be specified by the City that will be within twenty five percent ( $\pm$  25%) of the quantities listed in the Bid.
- 10.4.2.** The increase in lump sum Bid amounts e.g., bond, mobilization, storm water protection, and traffic control shall be in proportion to the amount of the added quantities. Allowance Bid items have been provided for this purpose where needed.
- 10.4.3.** The Contract Time to perform the additional Work will be the same as for the original Work, adjusted proportionately to the amount of the added Work compared to the amount of the original Work.
- 10.4.4.** The Retention for both original and added Work will be administered in accordance with 7-3.2, "Partial and Final Payment" of the General Provisions.

- 10.4.5.** A separate NTP will be issued for the added Work.
- 10.4.6.** A separate NOC may be filed for the added Work if the time between completion of the original Work and the commencement of the added Work exceeds 60 days.
- 10.5.** The option to renew may be declined by the Bidder only if the California Statewide Paving Asphalt Price Index has increased by more than 10% from the date of Bid opening to the date the option to renew is exercised by the City.

## INSTRUCTIONS TO BIDDERS

### 1. PREQUALIFICATION OF CONTRACTORS:

- 1.1. Contractors submitting a Bid must be pre-qualified for the total amount proposed, including all alternate items, prior to the date of submittal. Bids from contractors who have not been pre-qualified as applicable and Bids that exceed the maximum dollar amount at which contractors are pre-qualified may be deemed **non-responsive** and ineligible for award.
- 1.2. The completed application must be submitted online no later than 2 weeks prior to the bid opening.
- 1.3. **Joint Venture Bidders Cumulative Maximum Bidding Capacity:** For projects with an engineer's estimate of \$30,000,000 or greater, Joint Ventures submitting bids may be deemed responsive and eligible for award if the cumulative maximum bidding capacity of the individual Joint Venture entities is equal to or greater than the total amount proposed.
  - 1.3.1. Each of the entities of the Joint Venture must have been previously prequalified at a minimum of \$15,000,000.
  - 1.3.2. Bids submitted with a total amount proposed of less than \$30,000,000 are not eligible for Cumulative Maximum Bidding Capacity prequalification. To be eligible for award in this scenario, the Joint Venture itself or at least one of the Joint Venture entities must have been prequalified for the total amount proposed.
  - 1.3.3. Bids submitted by Joint Ventures with a total amount proposed of \$30,000,000 or greater on a project with an engineer's estimate of less than \$30,000,000 are not eligible for Cumulative Maximum Bidding Capacity prequalification.
  - 1.3.4. The Joint Venture designated as the Apparent Low Bidder shall provide evidence of its corporate existence and furnish good and approved bonds in the name of the Joint Venture within 14 Calendar Days of receipt by the Bidder of a form of contract for execution.
- 1.4. Complete information and links to the on-line prequalification application are available at:  
<http://www.sandiego.gov/cip/bidopps/prequalification>
- 1.5. Due to the City's responsibility to protect the confidentiality of the contractors' information, City staff will not be able to provide information regarding contractors' prequalification status over the telephone. Contractors may access real-time information about their prequalification status via their vendor profile on [PlanetBids™](#).

2. **ELECTRONIC FORMAT RECEIPT AND OPENING OF BIDS:** Bids will be received in electronic format (eBids) EXCLUSIVELY at the City of San Diego's electronic bidding (eBidding) site, at: <http://www.sandiego.gov/cip/bidopps/index.shtml> and are due by the date, and time shown on the cover of this solicitation.
- 2.1. **BIDDERS MUST BE PRE-REGISTERED** with the City's bidding system and possess a system-assigned Digital ID in order to submit an electronic bid.
- 2.2. The City's bidding system will automatically track information submitted to the site including IP addresses, browsers being used and the URLs from which information was submitted. In addition, the City's bidding system will keep a history of every login instance including the time of login, and other information about the user's computer configuration such as the operating system, browser type, version, and more. Because of these security features, Contractors who disable their browsers' cookies will not be able to log in and use the City's bidding system.
- 2.3. The City's electronic bidding system is responsible for bid tabulations. Upon the bidder's or proposer's entry of their bid, the system will ensure that all required fields are entered. **The system will not accept a bid for which any required information is missing.** This includes all necessary pricing, subcontractor listing(s) and any other essential documentation and supporting materials and forms requested or contained in these solicitation documents.
- 2.4. **BIDS REMAIN SEALED UNTIL BID DEADLINE.** eBids are transmitted into the City's bidding system via hypertext transfer protocol secure (https) mechanism using SSL 128-256 bit security certificates issued from Verisign/Thawte which encrypts data being transferred from client to server. Bids submitted prior to the "Bid Due Date and Time" are not available for review by anyone other than the submitter who has until the "Bid Due Date and Time" to change, rescind or retrieve its proposal should it desire to do so.
- 2.5. **BIDS MUST BE SUBMITTED BY BID DUE DATE AND TIME.** Once the bid deadline is reached, no further submissions are accepted into the system. Once the Bid Due Date and Time has lapsed, bidders, proposers, the general public, and City staff are able to immediately see the results on line. City staff may then begin reviewing the submissions for responsiveness, EOCB compliance and other issues. The City may require any Bidder to furnish statement of experience, financial responsibility, technical ability, equipment, and references.
- 2.6. **RECAPITULATION OF THE WORK.** Bids shall not contain any recapitulation of the Work. Conditional Bids may be rejected as being non-responsive. Alternative proposals will not be considered unless called for.

**2.7. BIDS MAY BE WITHDRAWN** by the Bidder only up to the bid due date and time.

**2.7.1. Important Note:** Submission of the electronic bid into the system may not be instantaneous. Due to the speed and capabilities of the user's internet service provider (ISP), bandwidth, computer hardware and other variables, it may take time for the bidder's submission to upload and be received by the City's eBidding system. It is the bidder's sole responsibility to ensure their bids are received on time by the City's eBidding system. The City of San Diego is not responsible for bids that do not arrive by the required date and time.

**2.8. ACCESSIBILITY AND AMERICANS WITH DISABILITIES ACT (ADA) COMPLIANCE:** To request a copy of this solicitation in an alternative format, contact the Engineering & Capital Projects Department Contract Specialist listed on the cover of this solicitation at least five (5) working days prior to the Bid/Proposal due date to ensure availability.

**3. ELECTRONIC BID SUBMISSIONS CARRY FULL FORCE AND EFFECT:**

**3.1.** The bidder, by submitting its electronic bid, acknowledges that doing so carries the same force and full legal effect as a paper submission with a longhand (wet) signature.

**3.2.** By submitting an electronic bid, the bidder certifies that the bidder has thoroughly examined and understands the entire Contract Documents (which consist of the plans and specifications, drawings, forms, affidavits and the solicitation documents), and that by submitting the eBid as its bid proposal, the bidder acknowledges, agrees to and is bound by the entire Contract Documents, including any addenda issued thereto, and incorporated by reference in the Contract Documents.

**3.3.** The Bidder, by submitting its electronic bid, agrees to and certifies under penalty of perjury under the laws of the State of California, that the certification, forms and affidavits submitted as part of this bid are true and correct.

**3.4.** The Bidder agrees to the construction of the project as described in Attachment "A-Scope of Work" for the City of San Diego, in accordance with the requirements set forth herein for the electronically submitted prices. The Bidder guarantees the Contract Price for a period of 120 days from the date of Bid opening. The duration of the Contract Price guarantee shall be extended by the number of days required for the City to obtain all items necessary to fulfill all conditions precedent.

**4. BIDS ARE PUBLIC RECORDS:** Upon receipt by the City, Bids shall become public records subject to public disclosure. It is the responsibility of the respondent to clearly identify any confidential, proprietary, trade secret or otherwise legally privileged information contained within the Bid. General references to sections of the California Public Records Act (PRA) will not suffice. If the Contractor does not provide applicable case law that clearly establishes that the requested information is exempt from the disclosure requirements of the PRA, the City shall be free to release the information when required in accordance with the PRA, pursuant to any other applicable law,



or by order of any court or government agency, and the Contractor will hold the City harmless for release of this information.

**5. CONTRACTOR REGISTRATION AND ELECTRONIC REPORTING SYSTEM:**

**5.1. Prior** to the Award of the Contract or Task Order, you and your Subcontractors and Suppliers must register with the City’s web-based vendor registration and bid management system. For additional information go to:

<http://www.sandiego.gov/purchasing/bids-contracts/vendorreg>

**5.2.** The City may not award the contract until registration of all subcontractors and suppliers is complete. In the event this requirement is not met within the time frame specified in the Notice of Intent to Award letter, the City reserves the right to rescind the Notice of Award / Intent to Award and to make the award to the next responsive and responsible bidder / proposer.

**6. JOINT VENTURE CONTRACTORS:** Provide a copy of the Joint Venture agreement and the Joint Venture license to the City within 14 Calendar Days after receiving the Contract forms.

**7. INSURANCE REQUIREMENTS:**

**7.1.** All certificates of insurance and endorsements required by the contract are to be provided upon issuance of the City’s Notice of Intent to Award letter.

**7.2.** Refer to sections 5-4, “INSURANCE” of the Supplementary Special Provisions (SSP) for the insurance requirements which must be met.

**8. REFERENCE STANDARDS:** Except as otherwise noted or specified, the Work shall be completed in accordance with the following standards:

Title	Edition	Document Number
Standard Specifications for Public Works Construction (“The GREENBOOK”) <a href="http://www.greenbookspecs.org/">http://www.greenbookspecs.org/</a>	2018	PWPI010119-01
City of San Diego Standard Specifications for Public Works Construction (“The WHITEBOOK”)* <a href="https://www.sandiego.gov/ecp/edocref/greenbook">https://www.sandiego.gov/ecp/edocref/greenbook</a>	2018	PWPI010119-02
City of San Diego Standard Drawings* <a href="https://www.sandiego.gov/ecp/edocref/standarddraw">https://www.sandiego.gov/ecp/edocref/standarddraw</a>	2018	PWPI010119-03
Citywide Computer Aided Design and Drafting (CADD) Standards <a href="https://www.sandiego.gov/ecp/edocref/drawings">https://www.sandiego.gov/ecp/edocref/drawings</a>	2018	PWPI010119-04
California Department of Transportation (CALTRANS) Standard Specifications <a href="https://dot.ca.gov/programs/design/ccs-standard-plans-and-standard-specifications">https://dot.ca.gov/programs/design/ccs-standard-plans-and-standard-specifications</a>	2018	PWPI030119-05

Title	Edition	Document Number
CALTRANS Standard Plans <a href="https://dot.ca.gov/programs/design/ccs-standard-plans-and-standard-specifications">https://dot.ca.gov/programs/design/ccs-standard-plans-and-standard-specifications</a>	2018	PWPI030119-06
California Manual on Uniform Traffic Control Devices Revision 5 (CA MUTCD 2014 Rev 5) <a href="http://www.dot.ca.gov/programs/safety-programs/camutcd/camutcd-rev5">http://www.dot.ca.gov/programs/safety-programs/camutcd/camutcd-rev5</a>	2014	PWPI042220-09
<p><b>NOTE:</b> *Available online under Engineering Documents and References at: <a href="https://www.sandiego.gov/ecp/edocref/">https://www.sandiego.gov/ecp/edocref/</a></p> <p>*Electronic updates to the Standard Drawings may also be found in the link above</p>		

9. **CITY'S RESPONSES AND ADDENDA:** The City, at its discretion, may respond to any or all questions submitted in writing via the City's eBidding web site in the **form of an addendum**. No other responses to questions, oral or written shall be of any force or effect with respect to this solicitation. The changes to the Contract Documents through addenda are made effective as though originally issued with the Bid. The Bidders shall acknowledge the receipt of Addenda at the time of bid submission.
10. **CITY'S RIGHTS RESERVED:** The City reserves the right to cancel the Notice Inviting Bids at any time, and further reserves the right to reject submitted Bids, without giving any reason for such action, at its sole discretion and without liability. Costs incurred by the Bidder(s) as a result of preparing Bids under the Notice Inviting Bids shall be the sole responsibility of each bidder. The Notice Inviting Bids creates or imposes no obligation upon the City to enter a contract.
11. **CONTRACT PRICING:** This solicitation is for a Lump Sum contract with Unit Price provisions as set forth herein. The Bidder agrees to perform construction services for the City of San Diego in accordance with these contract documents for the prices listed below. The Bidder further agrees to guarantee the Contract Price for a period of 120 days from the date of Bid opening. The duration of the Contract Price guarantee may be extended, by mutual consent of the parties, by the number of days required for the City to obtain all items necessary to fulfill all contractual conditions.
12. **SUBCONTRACTOR INFORMATION:**
- 12.1. **LISTING OF SUBCONTRACTORS.** In accordance with the requirements provided in the "Subletting and Subcontracting Fair Practices Act" of the California Public Contract Code, the Bidder shall provide the **NAME** and **ADDRESS** of each Subcontractor who will perform work, labor, render services or who specially fabricates and installs a portion [type] of the work or improvement, in an amount in excess of 0.5% of the Contractor's total Bid. The Bidder shall also state within the description, whether the subcontractor is a **CONSTRUCTOR, CONSULTANT** or **SUPPLIER**. The Bidder shall state the **DIR REGISTRATION NUMBER** for all subcontractors and shall further state within the description, the **PORTION** of the work which will be performed by each subcontractor under this Contract. The Contractor shall list only one Subcontractor for each portion of the Work. The **DOLLAR VALUE** of the total Bid to be performed shall be stated for all subcontractors listed. Failure to comply with this requirement may result in the Bid being rejected as **non-responsive** and ineligible for award. The Bidder's attention is directed to the Special Provisions – Section 3-2, "SELF- PERFORMANCE", which stipulates the percent of the Work to be performed with the Bidders' own forces. The Bidder shall list all SLBE,

ELBE, DBE, DVBE, MBE, WBE, OBE, SDB, WoSB, HUBZone, and SDVOSB Subcontractors for which Bidders are seeking recognition towards achieving any mandatory, voluntary (or both) subcontracting participation goals.

Additionally, pursuant to California Senate Bill 96 and in accordance with the requirements of Labor Code sections 1771.1 and 1725.5, by submitting a bid or proposal to the City, Contractor is certifying that he or she has verified that all subcontractors used on this public work project are registered with the California Department of Industrial Relations (DIR). **The Bidder shall provide the name, address, license number, DIR registration number of any Subcontractor – regardless of tier** - who will perform work, labor, render services or specially fabricate and install a portion [type] of the work or improvement pursuant to the contract.

- 12.2. LISTING OF SUPPLIERS.** Any Bidder seeking the recognition of Suppliers of equipment, materials, or supplies obtained from third party Suppliers towards achieving any mandatory or voluntary (or both) subcontracting participation goals shall provide, at a minimum, the **NAME, LOCATION (CITY), DIR REGISTRATION NUMBER** and the **DOLLAR VALUE** of each supplier. The Bidder will be credited up to 60% of the amount to be paid to the Suppliers for materials and supplies unless vendor manufactures or substantially alters materials and supplies, in which case, 100% will be credited. The Bidder is to indicate within the description whether the listed firm is a supplier or manufacturer. If no indication is provided, the listed firm will be credited at 60% of the listed dollar value for purposes of calculating the Subcontractor Participation Percentage.
- 12.3. LISTING OF SUBCONTRACTORS OR SUPPLIERS FOR ALTERNATES.** For subcontractors or suppliers to be used on additive or deductive alternate items, in addition to the above requirements, bidder shall further note "ALTERNATE" and alternate item number within the description.
- 13. SUBMITTAL OF "OR EQUAL" ITEMS:** See Section 4-6, "Trade Names" in The WHITEBOOK and as amended in the SSP.
- 14. AWARD:**
  - 14.1.** The Award of this contract is contingent upon the Contractor's compliance with all conditions precedent to Award.
  - 14.2.** Upon acceptance of a Bid, the City will prepare contract documents for execution within approximately 21 days of the date of the Bid opening and award the Contract approximately within 7 days of receipt of properly executed Contract, bonds, and insurance documents.
  - 14.3.** This contract will be deemed executed and effective only upon the signing of the Contract by the Mayor or his designee and approval as to form the City Attorney's Office.

- 16. AVAILABILITY OF PLANS AND SPECIFICATIONS:** Contract Documents may be obtained by visiting the City's website: <http://www.sandiego.gov/cip/>. Plans and Specifications for this contract are also available for review in the office of the City Clerk or Engineering & Capital Projects Department, Contracts Division.
- 17. ONLY ONE BID PER CONTRACTOR SHALL BE ACCEPTED:** No person, firm, or corporation shall be allowed to make, file, or be interested in more than one (1) Bid for the same work unless alternate Bids are called for. A person, firm or corporation who has submitted a sub-proposal to a Bidder, or who has quoted prices on materials to a Bidder, is not hereby disqualified from submitting a sub-proposal or quoting prices to other Bidders or from submitting a Bid in its own behalf. Any Bidder who submits more than one bid will result in the rejection of all bids submitted.
- 18. SAN DIEGO BUSINESS TAX CERTIFICATE:** The Contractor and Subcontractors, not already having a City of San Diego Business Tax Certificate for the work contemplated shall secure the appropriate certificate from the City Treasurer, Civic Center Plaza, First floor and submit to the Contract Specialist upon request or as specified in the Contract Documents. Tax Identification numbers for both the Bidder and the listed Subcontractors must be submitted on the City provided forms within these documents.
- 19. BIDDER'S GUARANTEE OF GOOD FAITH (BID SECURITY) FOR DESIGN-BID-BUILD CONTRACTS:**
- 19.1.** For bids \$250,000 and above, bidders shall submit Bid Security at bid time. Bid Security shall be in one of the following forms: a cashier's check, or a properly certified check upon some responsible bank; or an approved corporate surety bond payable to the City of San Diego for an amount of not less than 10% of the total bid amount.
- 19.2.** This check or bond, and the monies represented thereby, will be held by the City as a guarantee that the Bidder, if awarded the contract, will in good faith enter into the contract and furnish the required final performance and payment bonds.
- 19.3.** The Bidder agrees that in the event of the Bidder's failure to execute this contract and provide the required final bonds, the money represented by the cashier's or certified check will remain the property of the City; and the Surety agrees that it will pay to the City the damages, not exceeding the sum of 10% of the amount of the Bid, that the City may suffer as a result of such failure.
- 19.4.** At the time of bid submission, bidders must upload and submit an electronic PDF copy of the aforementioned bid security. Whether in the form of a cashier's check, a properly certified check or an approved corporate surety bond payable to the City of San Diego, the bid security must be uploaded to the City's eBidding system. By 5PM 3 working days after the bid opening date, all bidders must provide the City with the original bid security.
- 19.5.** Failure to submit the electronic version of the bid security at the time of bid submission AND failure to provide the original by 5PM, 3 working days after bid opening date shall cause the bid to be rejected and deemed **non-responsive**.
- Due to circumstances related to Covid-19, until further notice, all original bid bond submittals must be received by 5 PM, 3 working days after bid opening date.

Upon circumstances returning to normal business as usual, the original bid bond shall once again be due by 5 PM the day after bid opening.

Original Bid Bond shall be submitted to:  
Engineering & Capital Projects Department, Contracts Division  
525 B Street, Suite 750 (7<sup>th</sup> Floor)  
San Diego, California, 92101  
To the Attention of the Contract Specialist on the Front Page of this solicitation.

**20. AWARD OF CONTRACT OR REJECTION OF BIDS:**

- 20.1.** This contract may be awarded to the lowest responsible and reliable Bidder.
- 20.2.** Bidders shall complete ALL eBid forms as required by this solicitation. Incomplete eBids will not be accepted.
- 20.3.** The City reserves the right to reject any or all Bids, to waive any informality or technicality in Bids received, and to waive any requirements of these specifications as to bidding procedure.
- 20.4.** Bidders will not be released on account of their errors of judgment. Bidders may be released only upon receipt by the City within 3 Working Days of the bid opening, written notice from the Bidder which shows proof of honest, credible, clerical error of a material nature, free from fraud or fraudulent intent; and of evidence that reasonable care was observed in the preparation of the Bid.
- 20.5.** A bidder who is not selected for contract award may protest the award of a contract to another bidder by submitting a written protest in accordance with the San Diego Municipal Code.
- 20.6.** The City of San Diego will not discriminate in the award of contracts with regard to race, religion creed, color, national origin, ancestry, physical handicap, marital status, sex or age.
- 20.7.** Each Bid package properly signed as required by these specifications shall constitute a firm offer which may be accepted by the City within the time specified herein.
- 20.8.** The City reserves the right to evaluate all Bids and determine the lowest Bidder on the basis of the base bid and any proposed alternates or options as detailed herein.

**21. BID RESULTS:**

- 21.1.** The availability of the bids on the City's eBidding system shall constitute the public announcement of the apparent low bidder. In the event that the apparent low bidder is subsequently deemed non-responsive or non-responsible, a notation of such will be made on the eBidding system. The new ranking and apparent low bidder will be adjusted accordingly.

**21. BID RESULTS:**

- 21.1.** The availability of the bids on the City's eBidding system shall constitute the public announcement of the apparent low bidder. In the event that the apparent low bidder is subsequently deemed non-responsive or non-responsible, a notation of such will be made on the eBidding system. The new ranking and apparent low bidder will be adjusted accordingly.
- 21.2.** To obtain the bid results, view the results on the City's web site, or request the results by U.S. mail and provide a self-addressed, stamped envelope. If requesting by mail, be sure to reference the bid name and number. The bid tabulations will be mailed to you upon their completion. The results will not be given over the telephone.

**22. THE CONTRACT:**

- 22.1.** The Bidder to whom award is made shall execute a written contract with the City of San Diego and furnish good and approved bonds and insurance certificates specified by the City within 14 days after receipt by Bidder of a form of contract for execution unless an extension of time is granted to the Bidder in writing.
- 22.2.** If the Bidder takes longer than 14 days to fulfill these requirements, then the additional time taken shall be added to the Bid guarantee. The Contract shall be made in the form adopted by the City, which includes the provision that no claim or suit whatsoever shall be made or brought by Contractor against any officer, agent, or employee of the City for or on account of anything done or omitted to be done in connection with this contract, nor shall any such officer, agent, or employee be liable hereunder.
- 22.3.** If the Bidder to whom the award is made fails to enter into the contract as herein provided, the award may be annulled and the Bidder's Guarantee of Good Faith will be subject to forfeiture. An award may be made to the next lowest responsible and reliable Bidder who shall fulfill every stipulation embraced herein as if it were the party to whom the first award was made.
- 22.4.** Pursuant to the San Diego City Charter section 94, the City may only award a public works contract to the lowest responsible and reliable Bidder. The City will require the Apparent Low Bidder to (i) submit information to determine the Bidder's responsibility and reliability, (ii) execute the Contract in form provided by the City, and (iii) furnish good and approved bonds and insurance certificates specified by the City within 14 Days, unless otherwise approved by the City, in writing after the Bidder receives notification from the City, designating the Bidder as the Apparent Low Bidder and formally requesting the above mentioned items.
- 22.5.** The award of the Contract is contingent upon the satisfactory completion of the above-mentioned items and becomes effective upon the signing of the Contract by the Mayor or designee and approval as to form by the City Attorney's Office. If the Apparent Low Bidder does not execute the Contract or submit required documents and information, the City

may award the Contract to the next lowest responsible and reliable Bidder who shall fulfill every condition precedent to award. A corporation designated as the Apparent Low Bidder shall furnish evidence of its corporate existence and evidence that the officer signing the Contract and bond for the corporation is duly authorized to do so.

- 23. EXAMINATION OF PLANS, SPECIFICATIONS, AND SITE OF WORK:** The Bidder shall examine carefully the Project Site, the Plans and Specifications, other materials as described in the Special Provisions, Section 3-9, "TECHNICAL STUDIES AND SUBSURFACE DATA", and the proposal forms (e.g., Bidding Documents). The submission of a Bid shall be conclusive evidence that the Bidder has investigated and is satisfied as to the conditions to be encountered, as to the character, quality, and scope of work, the quantities of materials to be furnished, and as to the requirements of the Bidding Documents Proposal, Plans, and Specifications.
- 24. CITY STANDARD PROVISIONS:** This contract is subject to the following standard provisions. See The WHITEBOOK for details.
- 24.1.** The City of San Diego Resolution No. R-277952 adopted on May 20, 1991 for a Drug-Free Workplace.
- 24.2.** The City of San Diego Resolution No. R-282153 adopted on June 14, 1993 related to the Americans with Disabilities Act.
- 24.3.** The City of San Diego Municipal Code §22.3004 for Contractor Standards.
- 24.4.** The City of San Diego's Labor Compliance Program and the State of California Labor Code §§1771.5(b) and 1776.
- 24.5.** Sections 1777.5, 1777.6, and 1777.7 of the State of California Labor Code concerning the employment of apprentices by contractors and subcontractors performing public works contracts.
- 24.6.** The City's Equal Benefits Ordinance (EBO), Chapter 2, Article 2, Division 43 of The San Diego Municipal Code (SDMC).
- 24.7.** The City's Information Security Policy (ISP) as defined in the City's Administrative Regulation 90.63.
- 25. PRE-AWARD ACTIVITIES:**
- 25.1.** The contractor selected by the City to execute a contract for this Work shall submit the required documentation as specified in the herein and in the Notice of Award. Failure to provide the information as specified may result in the Bid being rejected as **non-responsive**.
- 25.2.** The decision that bid is non-responsive for failure to provide the information required within the time specified shall be at the sole discretion of the City.

**PERFORMANCE BOND, LABOR AND MATERIALMEN'S BOND**

**FAITHFUL PERFORMANCE BOND AND LABOR AND MATERIALMEN'S BOND:**

VSS International, Inc., a corporation, as principal, and  
Western Surety Company, a corporation authorized to do  
business in the State of California, as Surety, hereby obligate themselves, their successors and assigns,  
jointly and severally, to The City of San Diego a municipal corporation in the sum of Three Million Nine  
Hundred Ninety Four Thousand One Hundred Twenty Dollars and Zero Cents (\$3,994,120.00) for the  
faithful performance of the annexed contract, and in the sum of Three Million Nine Hundred Ninety  
Four Thousand One Hundred Twenty Dollars and Zero Cents (\$3,994,120.00) for the benefit of  
laborers and materialmen designated below.

**Conditions:**

If the Principal shall faithfully perform the annexed contract with the City of San Diego,  
California, then the obligation herein with respect to a faithful performance shall be void; otherwise it  
shall remain in full force.

If the Principal shall promptly pay all persons, firms and corporations furnishing materials for  
or performing labor in the execution of this contract, and shall pay all amounts due under the  
California Unemployment Insurance Act then the obligation herein with respect to laborers and  
materialmen shall be void; otherwise it shall remain in full force.

The obligation herein with respect to laborers and materialmen shall inure to the benefit of  
all persons, firms and corporations entitled to file claims under the provisions of Article 2. Claimants,  
(iii) public works of improvement commencing with Civil Code Section 9100 of the Civil Code of the  
State of California.

Changes in the terms of the annexed contract or specifications accompanying same or  
referred to therein shall not affect the Surety's obligation on this bond, and the Surety hereby waives  
notice of same.

The Surety shall pay reasonable attorney's fees should suit be brought to enforce the  
provisions of this bond.

The Surety expressly agrees that the City of San Diego may reject any contractor or  
subcontractor which may be proposed by Surety in fulfillment of its obligations in the event of default  
by the Principal.

The Surety shall not utilize the Principal in completing the improvements and work specified  
in the Agreement in the event the City terminates the Principal for default.



**PERFORMANCE BOND, LABOR AND MATERIALMEN'S BOND (continued)**

Dated December 15, 2020

Approved as to Form

VSS International, Inc.

Principal

By \_\_\_\_\_

**Jordan Reed, Treasurer**

Printed Name of Person Signing for Principal

Mara W. Elliott, City Attorney

By \_\_\_\_\_

Deputy City Attorney

March 24, 2021

Western Surety Company

Surety

By \_\_\_\_\_

Anibal Samuel Campos, Attorney-in-fact

Approved:

8880 Cal Center Drive, Ste 410

Local Address of Surety

By \_\_\_\_\_

Stephen Samara

Principal Contract Specialist

Engineering & Capital Projects Department

Sacramento, CA 95826

Local Address (City, State) of Surety

925-884-2286

Local Telephone No. of Surety

Premium \$ 11,982.00

Bond No. 30116416

# ACKNOWLEDGMENT

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California  
County of Yolo )

On December 15, 2020 before me, Victri Wackford, Notary Public  
(insert name and title of the officer)

personally appeared Jordan Reed,  
who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.


I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature

*Victri Wackford*

(Seal)



**CALIFORNIA ACKNOWLEDGMENT**

CIVIL CODE § 1189


A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California }  
County of Contra Costa }

On DEC 15 2020 before me, Chelsea Arnold, Notary Public  
*Date Here Insert Name and Title of the Officer*

personally appeared Anibal Samuel Campos  
*Name(s) of Signer(s)*

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.



Place Notary Seal and/or Stamp Above

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature *Chelsea Arnold*  
*Signature of Notary Public*

**OPTIONAL**

*Completing this information can deter alteration of the document or fraudulent reattachment of this form to an unintended document.*

**Description of Attached Document**

Title or Type of Document: \_\_\_\_\_

Document Date: \_\_\_\_\_ Number of Pages: \_\_\_\_\_

Signer(s) Other Than Named Above: \_\_\_\_\_

**Capacity(ies) Claimed by Signer(s)**

Signer's Name: \_\_\_\_\_

Corporate Officer – Title(s): \_\_\_\_\_

Partner –  Limited  General

Individual  Attorney in Fact

Trustee  Guardian or Conservator

Other: \_\_\_\_\_

Signer is Representing: \_\_\_\_\_

Signer's Name: \_\_\_\_\_

Corporate Officer – Title(s): \_\_\_\_\_

Partner –  Limited  General

Individual  Attorney in Fact

Trustee  Guardian or Conservator

Other: \_\_\_\_\_

Signer is Representing: \_\_\_\_\_

# Western Surety Company

## POWER OF ATTORNEY APPOINTING INDIVIDUAL ATTORNEY-IN-FACT

Know All Men By These Presents, That WESTERN SURETY COMPANY, a South Dakota corporation, is a duly organized and existing corporation having its principal office in the City of Sioux Falls, and State of South Dakota, and that it does by virtue of the signature and seal herein affixed hereby make, constitute and appoint

**Steven N Passerine, Kathleen E Earle, Benjamin Wolfe, Anibal Samuel Campos, Chelsea Arnold, Individually**

of San Ramon, CA, its true and lawful Attorney(s)-in-Fact with full power and authority hereby conferred to sign, seal and execute for and on its behalf bonds, undertakings and other obligatory instruments of similar nature

### - In Unlimited Amounts -

and to bind it thereby as fully and to the same extent as if such instruments were signed by a duly authorized officer of the corporation and all the acts of said Attorney, pursuant to the authority hereby given, are hereby ratified and confirmed.

This Power of Attorney is made and executed pursuant to and by authority of the By-Law printed on the reverse hereof, duly adopted, as indicated, by the shareholders of the corporation.

In Witness Whereof, WESTERN SURETY COMPANY has caused these presents to be signed by its Vice President and its corporate seal to be hereto affixed on this 7th day of May, 2020.




WESTERN SURETY COMPANY

Paul T. Brufat  
Paul T. Brufat, Vice President

State of South Dakota }  
County of Minnehaha } ss

On this 7th day of May, 2020, before me personally came Paul T. Brufat, to me known, who, being by me duly sworn, did depose and say: that he resides in the City of Sioux Falls, State of South Dakota; that he is the Vice President of WESTERN SURETY COMPANY described in and which executed the above instrument; that he knows the seal of said corporation; that the seal affixed to the said instrument is such corporate seal; that it was so affixed pursuant to authority given by the Board of Directors of said corporation and that he signed his name thereto pursuant to like authority, and acknowledges same to be the act and deed of said corporation.

My commission expires  
June 23, 2021



J. Mohr  
J. Mohr, Notary Public

### CERTIFICATE

I, L. Nelson, Assistant Secretary of WESTERN SURETY COMPANY do hereby certify that the Power of Attorney hereinabove set forth is still in force, and further certify that the By-Law of the corporation printed on the reverse hereof is still in force. In testimony whereof I have hereunto subscribed my name and affixed the seal of the said corporation this 15th day of December, 2020.



WESTERN SURETY COMPANY

L. Nelson  
L. Nelson, Assistant Secretary

## ATTACHMENTS

**ATTACHMENT A**  
**SCOPE OF WORK**

## SCOPE OF WORK

1. **SCOPE OF WORK:** Slurry Seal Group 2023 involves furnishing all labor, materials, equipment, services, and construction related to slurry seal work on existing paved roadways in various areas throughout the City of San Diego. The work includes: placement of rubber polymer modified slurry (RPMS), crack sealing, removal of humps & pavement irregularities, asphalt mill and pave, and digouts, pavement base repairs, milling and disposal of pavement fabric, replacing traffic signal detection loops and stub outs, adjusting existing City manhole frames and covers to grade, raising appurtenances to grade (water, sewer), raising survey monuments to grade, reconstructing survey monument boxes, street and sidewalk sweeping, removal and replacement of existing thermoplastic striping and markings/legends, installation of striping modifications, traffic control drawings & permits, weed abatement, storm drain inlet protection, installation of inlet markers, sediment control, and possible night and weekend work. All work would occur within the public right-of-way (paved streets) or previously disturbed non-sensitive areas only, and outside of the City's Multiple Habitat Planning Area (MHPA). No sensitive vegetation would be impacted or removed. Storm Water Best Management Practices (BMPs) for erosion control preventing discharge, as well as Traffic Control Plan (TCP) would be implemented throughout construction.
  - 1.1. The Work shall be performed in accordance with:
    - 1.1.1. The Notice Inviting Bids and **Appendix G – List of Proposed Work**, inclusive.
2. **LOCATION OF WORK:** The location of the Work is as follows:

See **Appendix H – Overall Location Map** and **Appendix I – Resurfacing Limit Maps**.
3. **CONTRACT TIME:** The Contract Time for completion of the Work, shall be **110 Working Days**.

**ATTACHMENT B**  
**RESERVED**



**ATTACHMENT C**  
**RESERVED**

**ATTACHMENT D**  
**PREVAILING WAGE**

## PREVAILING WAGE

1. **PREVAILING WAGE RATES:** Pursuant to San Diego Municipal Code section 22.3019, construction, alteration, demolition, repair and maintenance work performed under this Contract is subject to State prevailing wage laws. For construction work performed under this Contract cumulatively exceeding \$25,000 and for alteration, demolition, repair and maintenance work performed under this Contract cumulatively exceeding \$15,000, the Contractor and its subcontractors shall comply with State prevailing wage laws including, but not limited to, the requirements listed below.
  - 1.1. **Compliance with Prevailing Wage Requirements.** Pursuant to sections 1720 through 1861 of the California Labor Code, the Contractor and its subcontractors shall ensure that all workers who perform work under this Contract are paid not less than the prevailing rate of per diem wages as determined by the Director of the California Department of Industrial Relations (DIR). This includes work performed during the design and preconstruction phases of construction including, but not limited to, inspection and land surveying work.
    - 1.1.1. Copies of such prevailing rate of per diem wages are on file at the City and are available for inspection to any interested party on request. Copies of the prevailing rate of per diem wages also may be found at <http://www.dir.ca.gov/OPRL/DPreWageDetermination.htm>. Contractor and its subcontractors shall post a copy of the prevailing rate of per diem wages determination at each job site and shall make them available to any interested party upon request.
    - 1.1.2. The wage rates determined by the DIR refer to expiration dates. If the published wage rate does not refer to a predetermined wage rate to be paid after the expiration date, then the published rate of wage shall be in effect for the life of this Contract. If the published wage rate refers to a predetermined wage rate to become effective upon expiration of the published wage rate and the predetermined wage rate is on file with the DIR, such predetermined wage rate shall become effective on the date following the expiration date and shall apply to this Contract in the same manner as if it had been published in said publication. If the predetermined wage rate refers to one or more additional expiration dates with additional predetermined wage rates, which expiration dates occur during the life of this Contract, each successive predetermined wage rate shall apply to this Contract on the date following the expiration date of the previous wage rate. If the last of such predetermined wage rates expires during the life of this Contract, such wage rate shall apply to the balance of the Contract.
  - 1.2. **Penalties for Violations.** Contractor and its subcontractors shall comply with California Labor Code section 1775 in the event a worker is paid less than the prevailing wage rate for the work or craft in which the worker is employed. This shall be in addition to any other applicable penalties allowed under Labor Code sections 1720 – 1861.
  - 1.3. **Payroll Records.** Contractor and its subcontractors shall comply with California Labor Code section 1776, which generally requires keeping accurate payroll records, verifying and certifying payroll records, and making them available for inspection. Contractor shall require its subcontractors to also comply with section 1776. Contractor and its subcontractors shall submit weekly certified payroll records online via the City's web-based

Labor Compliance Program. Contractor is responsible for ensuring its subcontractors submit certified payroll records to the City.

- 1.3.1.** Contractor and their subcontractors shall also furnish records specified in Labor Code section 1776 directly to the Labor Commissioner in the manner required by Labor Code section 1771.4.
- 1.4. Apprentices.** Contractor and its subcontractors shall comply with California Labor Code sections 1777.5, 1777.6 and 1777.7 concerning the employment and wages of apprentices. Contractor is held responsible for the compliance of their subcontractors with sections 1777.5, 1777.6 and 1777.7.
- 1.5. Working Hours.** Contractor and their subcontractors shall comply with California Labor Code sections 1810 through 1815, including but not limited to: (i) restrict working hours on public works contracts to eight hours a day and forty hours a week, unless all hours worked in excess of 8 hours per day are compensated at not less than 1½ times the basic rate of pay; and (ii) specify penalties to be imposed on contractors and subcontractors of \$25 per worker per day for each day the worker works more than 8 hours per day and 40 hours per week in violation of California Labor Code sections 1810 through 1815.
- 1.6. Required Provisions for Subcontracts.** Contractor shall include at a minimum a copy of the following provisions in any contract they enter into with a subcontractor: California Labor Code sections 1771, 1771.1, 1775, 1776, 1777.5, 1810, 1813, 1815, 1860 and 1861.
- 1.7. Labor Code Section 1861 Certification.** Contractor in accordance with California Labor Code section 3700 is required to secure the payment of compensation of its employees and by signing this Contract, Contractor certifies that "I am aware of the provisions of Section 3700 of the California Labor Code which require every employer to be insured against liability for workers' compensation or to undertake self-insurance in accordance with the provisions of that code, and I will comply with such provisions before commencing the performance of the work of this Contract."
- 1.8. Labor Compliance Program.** The City has its own Labor Compliance Program authorized in August 2011 by the DIR. The City will withhold contract payments when payroll records are delinquent or deemed inadequate by the City or other governmental entity, or it has been established after an investigation by the City or other governmental entity that underpayment(s) have occurred. For questions or assistance, please contact the City of San Diego's Prevailing Wage Unit at 858-627-3200.
- 1.9. Contractor and Subcontractor Registration Requirements.** This project is subject to compliance monitoring and enforcement by the DIR. A contractor or subcontractor shall not be qualified to bid on, be listed in a bid or proposal, subject to the requirements of section 4104 of the Public Contract Code, or engage in the performance of any contract for public work, unless currently registered and qualified to perform public work pursuant to Labor Code section 1725.5. It is not a violation of this section for an unregistered contractor to submit a bid that is authorized by Section 7029.1 of the Business and Professions code or by Section 10164 or 20103.5 of the Public Contract Code, provided the contractor is registered to perform public work pursuant to Section 1725.5 at the time the contract is awarded.

- 1.9.1.** A Contractor's inadvertent error in listing a subcontractor who is not registered pursuant to Labor Code section 1725.5 in response to a solicitation shall not be grounds for filing a bid protest or grounds for considering the bid non-responsive provided that any of the following apply: (1) the subcontractor is registered prior to bid opening; (2) within twenty-four hours after the bid opening, the subcontractor is registered and has paid the penalty registration fee specified in Labor Code section 1725.5; or (3) the subcontractor is replaced by another registered subcontractor pursuant to Public Contract Code section 4107.
- 1.9.2.** By submitting a bid or proposal to the City, Contractor is certifying that he or she has verified that all subcontractors used on this public work project are registered with the DIR in compliance with Labor Code sections 1771.1 and 1725.5, and Contractor shall provide proof of registration for themselves and all listed subcontractors to the City at the time of bid or proposal due date or upon request.
- 1.10. Stop Order.** For Contractor or its subcontractors engaging in the performance of any public work contract without having been registered in violation of Labor Code sections 1725.5 or 1771.1, the Labor Commissioner shall issue and serve a stop order prohibiting the use of the unregistered contractors or unregistered subcontractor(s) on ALL public works until the unregistered contractor or unregistered subcontractor(s) is registered. Failure to observe a stop order is a misdemeanor.
- 1.11. List of all Subcontractors.** The Contractor shall provide the list of subcontractors (regardless of tier), along with their DIR registration numbers, utilized on this Contract prior to any work being performed; and the Contractor shall provide a complete list of all subcontractors with each invoice. Additionally, Contractor shall provide the City with a complete list of all subcontractors (regardless of tier) utilized on this contract within ten working days of the completion of the contract, along with their DIR registration numbers. The City shall withhold final payment to Construction Management Professional until at least thirty (30) days after this information is provided to the City.
- 1.12. Exemptions for Small Projects.** There are limited exemptions for installation, alteration, demolition, or repair work done on projects of \$25,000 or less. The Contractor shall still comply with Labor Code sections 1720 et. seq. The only recognized exemptions are listed below:
- 1.12.1.** Registration. The Contractor will not be required to register with the DIR for small projects. (Labor Code section 1771.1).
- 1.12.2.** Certified Payroll Records. The records required in Labor Code section 1776 shall be required to be kept and submitted to the City of San Diego, but will not be required to be submitted online with the DIR directly. The Contractor will need to keep those records for at least three years following the completion of the Contract. (Labor Code section 1771.4).
- 1.12.3.** List of all Subcontractors. The Contractor shall not be required to hire only registered subcontractors and is exempt from submitting the list of all subcontractors that is required in section 1.11 above. (Labor code section 1773.3).

**ATTACHMENT E**  
**SUPPLEMENTARY SPECIAL PROVISIONS**

## SUPPLEMENTARY SPECIAL PROVISIONS

The following Supplementary Special Provisions (SSP) modifies the following documents:

1. The **2018 Edition** of the Standard Specifications for Public Works Construction (The "GREENBOOK").
2. The **2018 Edition** of the City of San Diego Standard Specifications for Public Works Construction (The "WHITEBOOK"), including the following:
  - a) General Provisions (A) for all Construction Contracts.

---

### PART 0 – EQUAL OPPORTUNITY CONTRACTING PROGRAM (EOCP)

#### SECTION A – GENERAL REQUIREMENTS

**0-12 CONTRACT RECORDS AND REPORTS.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. You shall maintain records of all subcontracts and invoices from your Subcontractors and Suppliers for work on this project. Records shall show name, telephone number including area code, and business address of each Subcontractor, Supplier, and joint venture partner, and the total amount actually paid to each firm. Project relevant records, regardless of tier, may be periodically reviewed by the City.
2. You shall retain all records, books, papers, and documents pertinent to the Contract for a period of not less than 5 years after Notice of Completion and allow access to said records by the City's authorized representatives.
3. You shall submit the following reports using the City's web-based contract compliance (Prism® portal):
  - a) **Monthly Payment.** You shall submit Monthly Payment Reporting by the 10<sup>th</sup> day of the subsequent month. Incomplete and/or delinquent reporting may cause payment delays, non-payment of invoices, or both.
4. The records maintained under item 1, described above, shall be consolidated into a Final Summary Report, certified as correct by an authorized representative of the Contractor. The Final Summary Report shall include all subcontracting activities and be sent to the EOCP Program Manager prior to Acceptance. Failure to comply may result in assessment of liquidated damages or withholding of retention. The City will review and verify 100% of subcontract participation reported in the Final Summary Report prior to approval and release of final retention to you. In the event your Subcontractors are owed money for completed Work, the City may authorize payment to subcontractor via a joint check from the withheld retention.

**SECTION 1 – GENERAL, TERMS, DEFINITIONS, ABBREVIATIONS, UNITS OF MEASURE, AND SYMBOLS**

**1-2 TERMS AND DEFINITIONS.** To the “WHITEBOOK”, items 43, 56, 69, and 102, DELETE in their entirety and SUBSTITUTE with the following:

- 43. **Field Order** -A Field Order is a written agreement by the Engineer to compensate you for Work items in accordance with 2-8, “EXTRA WORK” or 2-9, “CHANGED CONDITIONS”. A Field Order does not change the Contract Price, Contract Time, or the scope intent of the Contract. The unused portion of the Field Order shall revert to the City upon Acceptance.
- 56. **Notice of Completion (NOC)** - A document recorded with the County of San Diego to signify that the Contract Work has been completed and accepted by the City.
- 69. **Punchlist** - A list of items of Work or corrections generated after a Walk-through that is conducted when you consider that the Work and Services are complete, and as verified by the Owner. The Punchlist may be completed in phases if defined in the Contract.
- 102. **Walk-through** - An inspection the City uses to verify the completion of the Project or phase of the Project and to generate a Punchlist prior to Acceptance.

To the “WHITEBOOK”, item 54, “Normal Working Hours”, ADD the following:

The **Normal Working Hours** are **8:30 AM** to **3:30 PM**.

To the “WHITEBOOK”, ADD the following:

- 108. **Acceptance** – When all of the Contract Work, including all Punchlist items, is deemed officially complete by the City Asset Owning Department or Deputy City Engineer.
- 109. **Occupancy** – When the Owner deems a building is ready for use, the Owner will issue a certificate of Occupancy in writing.
- 110. **Substantial Completion** – When all Contract Work is deemed complete by the Contractor in writing, and as verified by the Owner. Substantial Completion may be completed in phases if defined in the Contract.

**1-7.1.3 Requests for Information (RFI).** To the “WHITEBOOK”, DELETE in its entirety and SUBSTITUTE with the following:

- 1. Should You discover a conflict, omission, errors in the Contract Documents, differences with existing field conditions, or have any questions concerning interpretation or clarification of Contract Documents, or when you propose deviations to the standards or design, you shall submit a Request for Information (RFI) to the City regarding your question or clarification within **1 Working Day**.



2. Your RFI shall meet the following requirements:
  - a) All RFIs, whether by You or your Subcontractor or supplier at any tier, shall be submitted by You to the City.
  - b) RFIs shall be numbered sequentially.
  - c) You shall clearly and concisely set forth the single issue for which interpretation or clarification is sought, indicate Specification Section numbers, Contract Drawing numbers, and details, or other items involved, and state why a response is required from the City.
  - d) RFIs shall be submitted within **1 Working Day** in order that they may be adequately researched and answered before the response affects any critical activity of the Work.
  - e) Should You believe that a response to an RFI causes a change to the requirements of the Contract, You shall, before proceeding, give written notice to the City, indicating that You believe that City response to the RFI to be a Change Order. Failure to give such written notice within **5 Working Days** of receipt of the City's response to the RFI shall waive Your right to seek additional time or cost.
3. The City will respond to RFIs within **5 Working Days** unless the City notifies You in writing that a response will take longer. The **5 Working Days** shall begin when the RFI is received and dated by the City. Responses from the City will not change any requirement of the Contract unless so noted by the City in the response to the RFI. The City will not issue a Change Order for Extra Work or additional time when the issue raised in the RFI was due to your fault, neglect, or any unauthorized deviations from the project design or specifications.
4. If You proceed in resolving a conflict, omission, or any error in the Contract Documents without sending the City an RFI in accordance with the requirements stated above, the City may require You to remove such work at Your cost or back charge You the cost to remove this work.

**1-7.2 Contract Bonds.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:

1. Before execution of the Contract, file payment and performance bonds with the City to be approved by the Board in the amounts and for the purposes noted. Bonds shall be executed by a responsible surety as follows:
  - a) If the Work is being funded with state or local money, consistent with California Code of Civil Procedure §995.670, the Surety shall be an "admitted surety" authorized by the State of California Department of Insurance to transact surety insurance in the State.
  - b) If the Work is being funded with federal money, the Surety shall be listed in the U.S. Treasury Department Circular 570 and shall be in conformance with the specified Underwriting Limitations.

To the "WHITEBOOK", item 2, subsection "a", subsection "i", DELETE in its entirety and SUBSTITUTE with the following:

- i. A "Payment Bond" (Materials and Labor Bond) is optional. If no bond is submitted, no payment shall be made until 35 Calendar Days after Acceptance and any lien requirements have been fulfilled. If a bond is submitted, progress payments shall be made in accordance with these Specifications.

To the "WHITEBOOK", item 2, subsection "d", DELETE in its entirety and SUBSTITUTE with the following:

- d) For Contracts over \$100,000:
  - i. A "Payment Bond" (Materials and Labor Bond) for 100% of the Contract Price to satisfy claims of material Suppliers and of mechanics and laborers employed on the Work. You shall maintain the bond in full force and effect until Acceptance and until all claims for materials and labor are paid and shall otherwise comply with the Government Code.
  - ii. A "Faithful Performance Bond" for 100% of the Contract Price to guarantee faithful performance of Work, within the time prescribed and in a manner satisfactory to the City, that materials and workmanship shall be free from original or developed defects.

To the "WHITEBOOK", item 7, DELETE in its entirety and SUBSTITUTE with the following:

7. You shall require the Surety to mail its standard "Bond Status" form to the Engineer at the following address:  
Deputy Director  
Construction Management and Field Engineering Division  
9573 Chesapeake Drive San Diego, CA 92123

## **SECTION 2 – SCOPE OF THE WORK**

### **2-7 CHANGES INITIATED BY THE AGENCY.**

#### **2-7.1 General.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The Engineer may substitute specific sites for asphalt overlay or slurry seal due to utility or construction conflicts or urgent community needs. The Engineer will adjust the location list provided in the Contract Documents as needed.
2. The location list provided by the City in the Contract Documents will be adjusted by the City as needed to match the Bid quantities at no additional cost to the City.
3. The Bid quantities are for estimating purposes only and will vary due to continued deterioration of the streets, such as streets quantified as having no tons of AC required, may in fact need AC repair (see 301-1.6).

## SECTION 3 – CONTROL OF THE WORK

**3-2 SELF-PERFORMANCE.** To the “GREENBOOK”, DELETE in its entirety and SUBSTITUTE with the following:

1. You shall perform, with your own organization, Contract Work amounting to at least 50% of the base Bid.

**3-3 SUBCONTRACTORS.** To the “WHITEBOOK”, ADD the following:

6. When a Subcontractor fails to prosecute a portion of the Work in a manner satisfactory to the City, you shall remove such Subcontractor immediately upon written request of the City, and shall request approval of a replacement Subcontractor to perform the Work in accordance with California Public Contract Code (PCC), Subletting and Subcontracting, Section 4107, at no added cost to the City.

**3-8.7 Contractor’s Quality Control Plan (QCP).** To the “WHITEBOOK”, ADD the following:

7. The establishment and implementation of a Quality Control Plan (QCP), as defined in the standard specifications, shall be required for this Contract. See example in **Appendix E - Sample Contractor’s Daily Quality Control Inspection Report.**
8. The Contractor’s Quality Control Plan shall be subject to approval by the Engineer.
9. Additions and Alterations to the Contractor’s Quality Control Plan may be requested at the discretion of the Engineer. The request for Additions and Alterations to the Contractor’s Quality Control Plan will be made to the Contractor in writing by the Engineer. Submission of Additions and Alterations to the Contractor’s Quality Control Plan shall be submitted within 5 business days from the date the request for Additions and Alterations is made by the Engineer.
10. Additions and Alterations to the Contractor’s Quality Control Plan shall be subject to approval by the Engineer.
11. The Contractor shall ensure that all Items of Work, regardless of their inclusion in or omission from the Contractors Quality Control Plan, conform to the Contract Documents.
12. Payment for the Contractor’s Quality Control Plan shall be included in the Contract Price.
13. No Additional Payment shall be made for Additions and Alterations to the Contractor’s Quality Control Plan.

**3-8.7.1 QCP Submittal.** To the “WHITEBOOK”, item 2, DELETE in its entirety and SUBSTITUTE with the following:

2. The QCP shall be organized to address, at a minimum, the following items:
  - a) Quality Control Administrator
  - b) Surface preparation and paving schedule

- c) Inspection and documentation requirements (Daily Quality Control Inspection Report)
- d) Material quality control testing plan
- e) Documentation of quality control activities
- f) Procedures for corrective action when quality control and/or acceptance criteria are not met
- g) If paving Work will be in areas prone to shade, provide curing time of product

**3-8.7.4**      **Documentation.** To the "WHITEBOOK", item 3, section "a", subsection "viii", DELETE in its entirety and SUBSTITUTE with the following:

- viii. Documentation that the following have been verified to be in compliance:
  - Proper storage of materials and equipment.
  - Proper operation of all equipment.
  - Adherence to plans and technical specifications.
  - Review of quality control tests.
  - Safety inspection.
  - Mixing properties of products against the approved submittal limits.

**3-12.1**      **General.** To the "WHITEBOOK", ADD the following:

- 2. You shall provide a PM-10 certified self-loading motorized street sweeper equipped with a functional water spray system for this project.
- 3. You shall sweep all paved areas within the Work site and all paved haul routes as specified below:
  - a) Prior to any slurry seal application.
  - b) As directed by the Engineer.

If these requirements would require you to sweep on a Holiday or Weekend, then you shall sweep the next available Working Day prior to that Holiday or Weekend.

**3-13.1**      **Completion.** To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:

- 1. You shall submit a written assertion that the Work has been completed and is ready for Owner Acceptance. If, in the Engineer's judgment, the Work has been completed in accordance with the Contract Documents, the Engineer will set forth in writing the date the Work was completed. This will be the date that you are relieved from responsibility to protect and maintain the Work and to which liquidated damages will be computed.

**3-13.1.1 Requirements Before Requesting a Walk-through.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

**3-13.1.1 Requirements Before Requesting Substantial Completion.**

1. The following items are required prior to requesting a Substantial Completion:
  - a) Remove temporary facilities from the Site.
  - b) Thoroughly cleaning the Site and removing all mark outs and construction staking.
  - c) Provide completed and signed Red-lines in accordance with 3-7.3 "Redlines and Record Documents".
  - d) Provide all material and equipment maintenance and operation instructions and/or manuals.
  - e) Provide all tools which are permanent parts of the equipment installed in the Project.
  - f) Provide and properly identify all keys for construction and all keys for permanent Work.
  - g) Provide all final Special Inspection reports required by the applicable building Code.
  - h) Provide all items specified to be supplied as extra stock. Wrap, seal, or place in a container all items as necessary to allow for storage by the City for future use. Verify the specified quantities.
  - i) Ensure that all specified EOCP and certified wage rate documentations covering the Contract Time have been submitted.
  - j) If the Work includes installing an irrigation system, provide the spare parts for the proposed irrigation system as specified in the Special Provisions.
  - k) If the Work includes sewer and storm drain installations, the inspection shall include televising in accordance with 306-18, "VIDEO INSPECTION".
  - l) If the Work includes a Plant Establishment Period, Work in accordance with 801-6, "MAINTENANCE AND PLANT ESTABLISHMENT" shall be completed prior to requesting Substantial Completion, unless approved otherwise by the Owner.
  - m) Notify the Engineer to arrange a final inspection of any permanent BMPs installed.

**3-13.1.2 Walk-through and Punchlist Procedure.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. You shall notify the Engineer 15 Working Days in advance of date of anticipated Substantial Completion to allow time for Engineer to schedule a Walk-through. After you complete the requirements in 3-13.1.1, "Requirements Before Requesting Substantial Completion" and when you consider that the Work is Substantially Complete, you will notify the Engineer in writing that the Project is Substantially

Complete. The Engineer will review your request and determine if the Project is ready for a Walk-through, by verifying whether you have completed all items as required by 3-13.1.1, "Requirements Before Requesting Substantial Completion". Within 7 Working Days, the City will either reject your request of a Walk-through in writing or schedule a Walk-through inspection. The Engineer shall facilitate the Walk-through.

2. The following documents shall be provided at the time of your Walk-through request: As-Built markup, Plans, specifications, technical data such as submittals and equipment manuals, draft final payment, warranties, material certifications, bonds, guarantees, maintenance service agreements, and maintenance and operating manuals.
3. Written warranties, except manufacturer's standard printed warranties, shall be on a letterhead addressed to you. Warranties shall be submitted in the format described in this section, modified as approved by the City, to suit the conditions pertaining to the warranty. Lack of submitting these items will delay start of Walk-through.
4. The Engineer will provide you with the Punchlist within 15 Working Days after the date of the Walk-through. The City shall not provide a preliminary Punchlist.
5. If the Engineer finds that the Project is not Substantially Complete as defined herein, the Engineer will terminate the Walk-through and notify you in writing.
6. If, at any time during the Engineer's evaluation of the corrective Work required by the Punchlist, the Engineer discovers that additional corrective Work is required, the Engineer may include that corrective Work in the Punchlist.
7. You shall remain solely responsible for the Project Site until the Project is completely operational, all Punchlist items have been corrected, and all operation and maintenance manuals have been accepted by the City.
8. The Engineer shall meet with you within 5 Working Days of notification that all Punchlist items are corrected. You shall complete the Punchlist within 30 Working Days, and Working Days will continue to be counted until Acceptance of the Project.
9. When a comment from the Punchlist is disputed, you shall submit in writing justification for the dispute within 15 day of receiving the punchlist.

**3-13.2 Acceptance.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. You shall provide the completed, signed, and stamped DS-563 to the Engineer prior to Acceptance.
2. You shall deliver the final As-builts and final billing prior to Acceptance.

3. You shall assemble and deliver to the Engineer a Final Summary Report and Affidavit of Disposal prior to Acceptance.
4. Acceptance shall occur after all of the requirements contained in the Contract Documents have been fulfilled. If, in the Engineer's judgment, you have fully performed the Contract, the Engineer will recommend to the City Engineer that your performance of the Contract be accepted. You shall receive notification of Acceptance in writing from the Owner and counting of working days shall cease and Warranty begins.
5. Retention can be released 35 Calendar Days after NOC. Submit your request for retention to the Resident Engineer and they will mail to you a "Release of Claims" form which shall be completed and returned before the retention will be released.

**3-13.3 Warranty.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. You shall warranty and repair all defective materials and workmanship for a period of 1 year. This call back warranty period shall start on the date the Work was accepted by the City.
2. You shall warranty the Work free from all latent defects for 10 years and patent defects for a period of 4 years.
3. The warranty period for specific items covered under manufacturers' or suppliers' warranties shall commence on the date they are placed into service at the direction of the Engineer in writing.
4. All express warranties from Subcontractors, manufacturers', or Suppliers', of any tier, for the materials furnished and Work performed shall be assigned, in writing, to the City, and shall be delivered to the Engineer prior to the Acceptance of your performance of the Contract.
5. Replace or repair defective materials and workmanship in a manner satisfactory to the Engineer after notice to do so from the Engineer and within the time specified in the notice. If you fail to make such replacements or repairs within the time specified in the notice, the City may perform the replacement or repairs at your expense. If you fail to reimburse the City for the actual costs, your Surety shall be liable for the cost
6. Items that shall be warrantied free from defective workmanship and materials for a period longer than 1 year are as follows:

<b>Specified Item</b>	<b>Minimum Warranty Period</b>
Detectable Warning Tile Construction	3 Years of Manufacturer's Warranty
All Work Under SECTION 500 – PIPELINE REHABILITATION	3 Years

Specified Item	Minimum Warranty Period
Fiber Optic Interconnect Cables	2 Years
Luminaires*	10 Years of Manufacturer's Warranty
LED Signal Modules	3 Years of Manufacturer's Warranty
Field Devices Associated with 700-6.3, "Adaptive Control Note"	See 700-6.3.9, "Warranty"

\* Provide documentation verifying that the induction luminaire models being offered for the Project are covered by the 10 year warranty.

7. If installed, you shall provide the City and property owner a copy of the manufacturer's warranty for private sewer pumps, including the alarm panel and all other accessories.
  - a) You shall involve the manufacturer in the installation and startup as needed to secure any extended warranty required.
  - b) Nothing in here is intended to limit any manufacturer's warranty which provides the City with greater warranty rights than set forth in this section or the Contract Documents.
  - c) The warranty shall include all components. The form of the warranty shall be approved by the Engineer in accordance with 3-13.3.2, "Warranty Format Requirements".
8. If, during the warranty period, any item of the Work is found to be Defective Work, you shall correct it promptly after receipt of written notice from the City to do so. The warranty period shall be extended with respect to portions of the Work corrected as part of the warranty requirements.

#### **SECTION 4 - CONTROL OF MATERIALS**

**4-3.6 Preapproved Materials.** To the "WHITEBOOK", ADD the following:

3. You shall submit in writing a list of all products to be incorporated in the Work that are on the AML.

**4-6 TRADE NAMES.** To the "WHITEBOOK", ADD the following:

11. You shall submit your list of proposed substitutions for an "equal" item **no later than 5 Working Days after the determination of the Apparent Low Bidder** and on the City's Product Submittal Form available at:

<https://www.sandiego.gov/ecp/edocref/>



## SECTION 5 – LEGAL RELATIONS AND RESPONSIBILITIES

**5-4 INSURANCE.** To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:

**5-4 INSURANCE.**

1. The insurance provisions herein shall not be construed to limit your indemnity obligations contained in the Contract.

**5-4.1 Policies and Procedures.**

1. You shall procure the insurance described below, at its sole cost and expense, to provide coverage against claims for loss including injuries to persons or damage to property, which may arise out of or in connection with the performance of the Work by you, your agents, representatives, officers, employees or Subcontractors.
2. Insurance coverage for property damage resulting from your operations is on a replacement cost valuation. The market value will not be accepted.
3. You shall maintain this insurance for the duration of this Contract and at all times thereafter when you are correcting, removing, or replacing Work in accordance with this Contract. Your liabilities under the Contract, e.g., your indemnity obligations, is not deemed limited to the insurance coverage required by this Contract.
4. The payment for insurance shall be included in the Contract Price as bid by you. Except as specifically agreed to by the City in writing, you are not entitled to any additional payment. Do not begin any Work under this Contract until you have provided and the City has approved all required insurance.
5. Policies of insurance shall provide that the City is entitled to 30 Days (10 Days for cancellation due to non-payment of premium) prior written notice of cancellation or non-renewal of the policy. Maintenance of specified insurance coverage is a material element of the Contract. Your failure to maintain or renew coverage or to provide evidence of renewal during the term of the Contract may be treated by the City as a material breach of the Contract.

**5-4.2 Types of Insurance.**

**5-4.2.1 Commercial General Liability Insurance.**

1. Commercial General Liability Insurance shall be written on the current version of the ISO Occurrence form CG 00 01 07 98 or an equivalent form providing coverage at least as broad.
2. The policy shall cover liability arising from premises and operations, XCU (explosions, underground, and collapse), independent contractors, products/completed operations, personal injury and advertising injury, bodily injury, property damage, and liability assumed under an insured's contract (including the tort liability of another assumed in a business contract).

3. There shall be no endorsement or modification limiting the scope of coverage for either "insured vs. insured" claims or contractual liability. You shall maintain the same or equivalent insurance for at least 10 years following completion of the Work.
4. All costs of defense shall be outside the policy limits. Policy coverage shall be in liability limits of not less than the following:

<u>General Annual Aggregate Limit</u>	<u>Limits of Liability</u>
Other than Products/Completed Operations	\$2,000,000
Products/Completed Operations Aggregate Limit	\$2,000,000
Personal Injury Limit	\$1,000,000
Each Occurrence	\$1,000,000

**5-4.2.2 Commercial Automobile Liability Insurance.**

1. You shall provide a policy or policies of Commercial Automobile Liability Insurance written on the current version of the ISO form CA 00 01 12 90 or later version or equivalent form providing coverage at least as broad in the amount of \$1,000,000 combined single limit per accident, covering bodily injury and property damage for owned, non-owned, and hired automobiles ("Any Auto").
2. All costs of defense shall be outside the limits of the policy.

**5-4.3 Rating Requirements.** Except for the State Compensation Insurance Fund, all insurance required by this Contract as described herein shall be carried only by responsible insurance companies with a rating of, or equivalent to, at least "A-, VI" by A.M. Best Company, that are authorized by the California Insurance Commissioner to do business in the State, and that have been approved by the City.

**5-4.3.1 Non-Admitted Carriers.** The City will accept insurance provided by non-admitted, "surplus lines" carriers only if the carrier is authorized to do business in the State and is included on the List of Approved Surplus Lines Insurers (LASLI list).

All policies of insurance carried by non-admitted carriers shall be subject to all of the requirements for policies of insurance provided by admitted carriers described herein.

**5-4.4 Evidence of Insurance.** Furnish to the City documents e.g., certificates of insurance and endorsements evidencing the insurance required herein, and furnish renewal documentation prior to expiration of this insurance. Each required document shall be signed by the insurer or a person authorized by the insurer to bind coverage on its behalf. We reserve the right to require complete, certified copies of all insurance policies required herein.

**5-4.5 Policy Endorsements.**

**5-4.5.1 Commercial General Liability Insurance.**

**5-4.5.1.1 Additional Insured.**

1. You shall provide at your expense policy endorsement written on the current version of the ISO Occurrence form CG 20 10 11 85 or an equivalent form providing coverage at least as broad.
2. To the fullest extent allowed by law e.g., California Insurance Code §11580.04, the policy shall be endorsed to include the City and its respective elected officials, officers, employees, agents, and representatives as additional insured.
3. The additional insured coverage for projects for which the Engineer's Estimate is \$1,000,000 or more shall include liability arising out of:
  - a) Ongoing operations performed by you or on your behalf,
  - b) your products,
  - c) your Work, e.g., your completed operations performed by you or on your behalf, or
  - d) premises owned, leased, controlled, or used by you.
4. The additional insured coverage for projects for which the Engineer's Estimate is less than \$1,000,000 shall include liability arising out of:
  - a) Ongoing operations performed by you or on your behalf,
  - b) your products, or
  - c) premises owned, leased, controlled, or used by you.

**5-4.5.1.2 Primary and Non-Contributory Coverage.** The policy shall be endorsed to provide that the coverage with respect to operations, including the completed operations, if appropriate, of the Named Insured is primary to any insurance or self-insurance of the City and its elected officials, officers, employees, agents and representatives. Further, it shall provide that any insurance maintained by the City and its elected officials, officers, employees, agents and representatives shall be in excess of your insurance and shall not contribute to it.

**5-4.5.1.3 Project General Aggregate Limit.** The policy or policies shall be endorsed to provide a Designated Construction Project General Aggregate Limit that will apply only to the Work. Only claims payments which arise from the Work shall reduce the Designated Construction Project General Aggregate Limit. The Designated Construction Project General Aggregate Limit shall be in addition to the aggregate limit provided for the products-completed operations hazard.

**5-4.5.2 Commercial Automobile Liability Insurance.**

**5-4.5.2.1 Additional Insured.** Unless the policy or policies of Commercial Auto Liability Insurance are written on an ISO form CA 00 01 12 90 or a later version of this form or equivalent form providing coverage at least as broad, the policy shall be endorsed to include the City and its respective elected officials, officers, employees, agents, and representatives as additional

insured, with respect to liability arising out of automobiles owned, leased, hired or borrowed by you or on your behalf. This endorsement is limited to the obligations permitted by California Insurance Code §11580.04.

**5-4.6 Deductibles and Self-Insured Retentions.** You shall pay for all deductibles and self-insured retentions. You shall disclose deductibles and self-insured retentions to the City at the time the evidence of insurance is provided.

**5-4.7 Reservation of Rights.** The City reserves the right, from time to time, to review your insurance coverage, limits, deductibles and self-insured retentions to determine if they are acceptable to the City. The City will reimburse you, without overhead, profit, or any other markup, for the cost of additional premium for any coverage requested by the Engineer but not required by this Contract.

**5-4.8 Notice of Changes to Insurance.** You shall notify the City 30 Days prior to any material change to the policies of insurance provided under this Contract.

**5-4.9 Excess Insurance.** Policies providing excess coverage shall follow the form of the primary policy or policies e.g., all endorsements.

**5-4.11 Workers' Compensation Insurance and Employers Liability Insurance.**

1. In accordance with the provisions of §3700 of the California Labor Code, you shall provide at your expense Workers' Compensation Insurance and Employers Liability Insurance to protect you against all claims under applicable state workers compensation laws. The City, its elected officials, and employees will not be responsible for any claims in law or equity occasioned by your failure to comply with the requirements of this section.

2. Limits for this insurance shall be not less than the following:

<u>Workers' Compensation</u>	<u>Statutory Employers Liability</u>
Bodily Injury by Accident	\$1,000,000 each accident
Bodily Injury by Disease	\$1,000,000 each employee
Bodily Injury by Disease	\$1,000,000 policy limit

3. By signing and returning the Contract you certify that you are aware of the provisions of §3700 of the Labor Code which requires every employer to be insured against liability for worker's compensation or to undertake self-insurance in accordance with the provisions of that code and you shall comply with such provisions before commencing the Work as required by §1861 of the California Labor Code.

**5-4.11.1 Waiver of Subrogation.** The policy or policies shall be endorsed to provide that the insurer will waive all rights of subrogation against the City and its respective elected officials, officers, employees, agents, and representatives for losses paid under the terms of the policy or policies and which arise from Work performed by the Named Insured for the City.

**5-10.2.1 Public Notice by Contractor.** To the "WHITEBOOK", items 2 and 3, DELETE in their entirety and SUBSTITUTE with the following:

2. No less than 5 Working Days in advance of Project construction activities and utility service interruptions, you shall notify all critical facilities, businesses, institutions, property owners, residents, or any other impacted stakeholders within a minimum 300-foot (90 m) radius of the Project. Verbal and written notifications shall be sent to critical facilities (including but not limited to police stations, fire stations, hospitals, and schools). A copy of written notifications sent to any critical facility shall also be sent to the Resident Engineer. You shall keep records of the people contacted, along with the dates of notification, and shall provide the record to the Engineer upon request. You shall identify all other critical facilities that need to be notified.
3. Furnish and distribute public notices in the form of door hangers using the City's format to all occupants and/or property owners along streets:
  - a) Where Work is to be performed at least Working 5 Working Days before starting construction or survey activities or impacting the community as approved by the Resident Engineer.
  - b) Within 5 Working Days of the completion of your construction activities where Work was performed, you shall distribute public notices in the form of door hangers, which outlines the anticipated dates of Asphalt Resurfacing or Slurry Seal.
  - c) 72 hours in advance of the scheduled resurfacing as approved by the Engineer.

**5-15.1 General.** To the "WHITEBOOK", item 10, DELETE in its entirety and SUBSTITUTE with the following:

10. If your construction activities have encountered flammable liquids or other hazardous substances, you shall ensure that construction staff have the required Hazardous Waste Operations and Emergency Response (HAZWOPER) certification. Construction staff shall include: City Engineers, City Laboratory Technicians, and City staff that perform onsite inspections.
  - a) If your Work encounters flammable liquids or other hazardous substances, you shall be responsible for scheduling training for all construction staff to attend and for submitting verification to the Engineer that construction staff have the required HAZWOPER certification prior to continuing that Work in that area. You shall maintain the HAZWOPER certifications annually until the construction activities triggering the requirement is complete, as approved by the Resident Engineer.

## SECTION 6 – PROSECUTION AND PROGRESS OF THE WORK

**6-1.1 Construction Schedule.** To the “WHITEBOOK”, item 1, subsections “e” and “s”, DELETE in its entirety and SUBSTITUTE with the following:

- e) Monthly progress payments are contingent upon the submittal of an updated Schedule to the Engineer. The Engineer may refuse to process the whole or part of any monthly payment if you refuse or fail to provide an acceptable schedule.
- s) Submit an updated cash flow forecast with every pay request (for each Project ID or WBS number provided in the Contract) showing periodic and cumulative construction billing amounts for the duration of the Contract Time. If there has been any Extra Work since the last update, include only the approved amounts.
  - i. Refer to the Sample City Invoice materials in **Appendix D – Sample City Invoice with Cash Flow Forecast** and use the format shown.
  - ii. See also the “Cash Flow Forecast Example” at the location below:  
<https://www.sandiego.gov/ecp/edocref/>

**6-1.3.1 Payment.** To the “WHITEBOOK”, ADD the following:

- 2. The payment for any work outside normal working hours, including weekend work and night work, shall be done at no additional cost to the City.
- 3. Payment for any work outside normal working hours, including weekend work and night work, shall be included in the Contract Price.

**6-1.5.2 Excusable Non-Compensable Delays.** To the “WHITEBOOK”, DELETE in its entirety and SUBSTITUTE with the following:

**6-1.5.2 Excusable Non-Compensable and Concurrent Delays.**

- 1. The City shall only issue an extension of time for Excusable Delays that meet the requirements of 6-4.2, “Extensions of Time” for the following circumstances:
  - a) Delays resulting from Force Majeure.
  - b) Delays caused by weather.
  - c) Delays caused by changes to County, State, or Federal law.
- 2. When a non-excusable delay is concurrent with an Excusable Delay, you shall not be entitled to an extension of Contract Time for the period the non-excusable delay is concurrent with the Excusable Delay.
- 3. When an Excusable Non-Compensable Delay is concurrent with an Excusable Compensable Delay, you shall be entitled to an extension of Contract Time, but shall not be entitled to compensation for the period the Excusable Non-Compensable Delay is concurrent with the Excusable Compensable Delay.

**6-3 TIME OF COMPLETION.** To the “WHITEBOOK”, ADD the following:

- 1. All construction related to plan sheets 41367-04-D, 41367-05-D and 41367-06-D (Phase 3) shall be completed first as part of this contract. Installation of water mains, water services, Fire hydrants and pertaining appurtenances.

#### 6-4.2

**Extensions of Time.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The Contract Time shall not be modified except by Change Order.
2. You shall notify the City in writing within **1 Working Day** after the occurrence and discovery of an event that impacts the Project Schedule.
  - a) If you believe this event requires a Change Order, you shall submit a written Change Order request with a report to the City that explains the request for Change Order within **5 Working Days**. The Change Order request must include supporting data, a general description of the discovery, the basis for extension, and the estimated length of extension. The City may grant an extension of time, in writing, for the Change Order request if you require more time to gather and analyze data.
3. The Engineer shall not grant an extension of Contract Time in accordance with 6-1.5, "Excusable Delays" unless you demonstrate, through an analysis of the critical path, the following:
  - a) The event causing the delay impacted the activities along the Project's critical path.
  - b) The increases in the time to perform all or part of the Project beyond the Contract Time arose from unforeseeable causes beyond your control and without your fault or negligence and that all project float has been used.
4. Any modifications to the Contract Time will be incorporated into the weekly document that the Engineer issues that stipulates the Contract Time. If you do not agree with this document, submit to the Engineer for review a written protest supporting your objections to the document within **30 Calendar Days** after receipt of the statement. Your failure to file a timely protest shall constitute your acceptance of the Engineer's weekly document.
  - a) Your protest will be considered a claim for time extension and shall be subject to 2-10.1, "Claims".

#### 6-4.4

**Written Notice and Report.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. Your failure to notify the Resident Engineer within **1 Working Day** OR provide a Change Order request within **5 Working Days** after the event, in accordance with 6-4.2, "Extensions of Time", will be considered grounds for refusal by the City to consider such request if your failure to notify prejudices the City in responding to the event.

**ADD:**

**6-6.1.1 Environmental Document.**

1. The City of San Diego has prepared a **Notice of Exemption** for **Slurry Seal Group S2023**, as referenced in the Contract Appendix. You shall comply with all requirements of the **Notice of Exemption** as set forth in **Appendix A**.
2. Compliance with the City's environmental document shall be included in the Contract Price, unless separate bid items have been provided.

**SECTION 7 – MEASUREMENT AND PAYMENT**

**7-2.1 Schedule of Values (SOV).** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:

1. You shall submit an SOV for the lump sum Bid items listed below to the Engineer for review and approval at the Pre-construction meeting:
  - a) Remove, Replace & Install Traffic Striping, Markers, Markings, and Devices
  - b) Traffic Control and Working Drawings

**7-3.1 General.** To the "GREENBOOK" and "WHITEBOOK", paragraph (8), DELETE in its entirety and SUBSTITUTE with the following:

If, within the time fixed by law, a properly executed notice to stop payment is filed with the City, due to your failure to pay for labor or materials used in the Work, all money due for such labor or materials will be withheld from payment in accordance with applicable laws.

To the "WHITEBOOK", ADD the following:

1. Unless specified otherwise, the Contract Price includes use, consumer, and other taxes mandated by applicable legal requirements.
2. As provided in §7105 of the California Public Contract Code, if the Contract is not financed by revenue bonds, you are not responsible for the cost of repairing or restoring damage to the Project when damage was proximately caused by an act of God, in excess of 5% of the Contract Price, if the following occur:
  - a) The Project damaged was built in accordance with the Contract requirements.
  - b) There are no insurance requirements in the Contract for the damages.



**7-3.2**

**Partial and Final Payment.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:

1. The Final Payment, which is the release of Retention, shall be paid to you after you have successfully submitted the following required documents:
  - a) An affidavit that payrolls and bills for materials, equipment, and other indebtedness connected with the Work for which the City or the City's property might be responsible for or encumbered by.
  - b) A certificate evidencing that insurances required by the Contract Documents shall remain in force after Final Payment is currently in effect and shall not be canceled or allowed to expire until at least a 30 Calendar Days prior written notice has been given to the Engineer.
  - c) Consent of Surety to Final Payment.
  - d) If required by the Engineer, other data establishing payment or satisfaction of obligations such as receipts, releases and waivers of liens, claims, and security interests or encumbrances arising out of the Contract Documents. If a Subcontractor refuses to furnish a release or waiver required by the City, you may furnish a bond satisfactory to the Engineer to indemnify the City against such lien.
  - e) If required in the Contract Documents, the successful completion and submittal of the required reports such as construction demolition, waste recycling, and hydrostatic discharge reports.
  - f) Required EOCP Final Summary Report in accordance with Section 0-12, "Contract Records and Reports", record drawings, operations manuals, test reports, warranty documentation, and UL labels shall be submitted before requesting the release of retention.
  - g) Acceptance of the completed Project by the asset owning Department.

To the "WHITEBOOK", ADD the following:

2. Submit an invoice for payment after you successfully complete the required documents and the City will pay the invoice within 30 Calendar Days. The City will pay 6% annually for late retention payments.

**7-3.2.1**

**Application for Progress Payment.** To the "WHITEBOOK", item 3, DELETE in its entirety and SUBSTITUTE with the following:

3. The City shall not pay progress or partial payments until you submit to the Engineer an acceptable updated Schedule. It is solely your responsibility to prepare and submit the Schedule updates.

**7-3.2.2 Amount of Progress Payments.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The City will pay 6% annually for late progress payments.
2. Progress payments will be considered "late" if the following occur:
  - a) The City does not pay the contractor within 30 Calendar Days from receipt of an undisputed and properly submitted invoice. A properly submitted payment invoice means that the City has approved for payment the entire invoice amount or if the Resident Engineer has not disputed any portion of the application within 7 Calendar Days of the date of submission.
  - b) The application for payment does not require signing of a Contract Change Order.
3. The Engineer may withhold payment for any of the following reasons:
  - a) Defective or incomplete Work.
  - b) Not providing an updated and accurate Cost Loaded Construction Schedule in accordance with 6-1.1, "Construction Schedule".
  - c) Stop notices, wage orders, or other withholdings required by Applicable Law. Your failure to comply with 5-3.3, "Payroll Records" and the Contractor Registration and Electronic Reporting System requirements of the Contract Documents.
4. The Engineer may back charge the contract for any of the following reasons:
  - a) Defective or incorrect Work not remedied.
  - b) Damage to City property or a third party's property that was caused by you.
  - c) Liquidated Damages.

**7-3.2.3 Waiver of Claims at Final Payment.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. Your acceptance of Final Payment constitutes a waiver of affirmative Claims by you, except those previously made in writing and identified as unsettled at the time of Final Payment.

**7-3.2.4 Withholding of Payment and Back Charge.** To the "WHITEBOOK", DELETE in its entirety.

**7-3.5.1 General.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. Unit Bid prices shall not be subject to adjustment regardless of quantity used, or if none is used, for the following Bid items:
  - a) imported backfill
  - b) shoring

- c) water services
  - d) house connection sewers
  - e) water pollution control items
2. Upon discovery and prior to the Work, you shall notify the Resident Engineer if there is a change in Bid item quantity that increases the total Contract Price by 5% or \$100,000 or more, whichever is less.

**7-3.8 Eliminated Items.** To the "GREENBOOK," DELETE in its entirety and SUBSTITUTE with the following:

1. Should any Bid Items, except Bid Items listed in item 2 of this section, be eliminated in their entirety, payment will be made to the Contractor for its actual costs incurred in connection with the eliminated item prior to notification in writing from the Engineer so stating its elimination.
2. If eliminated in their entirety, no payment will be made for actual costs incurred in connection with the following eliminated items:
  - a) "Crushed Miscellaneous Base"
  - b) "Asphalt Concrete with Pavement Fabric Material"
  - c) "Raise Appurtenance to Grade (Water, Sewer)"
  - d) "Adjust Existing Manhole Frame and Cover to Grade"
  - e) "Adjust Existing Survey Monument to Grade"
  - f) "Reconstruct Survey Monument Box"
  - g) "Crack Seal"
  - h) "Removal of Humps, Lumps, and Pavement Irregularities"
  - i) "Traffic Detector Loop Replacement or Conduit Stub Installed"
3. If material conforming to the Plans and Specifications is ordered for use in the eliminated items prior to the date of notification of elimination by the Engineer, and if the order for that material cannot be canceled, payment will be made to you for the actual cost of the material. In this case, the material shall become the property of the City and payment will be made to you for actual costs for any further handling. If the material is returnable, the material shall be returned, and payment will be made to you for actual cost of charges made by the supplier for handling and returning the material.

**7-3.9**

**Field Orders.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. If the cumulative total of Field Order items of Work does not exceed the "Field Orders" Bid Item, the City shall pay those Field Orders as shown below:

**TABLE 7-3.9**  
**FIELD ORDER LIMITS**

Contract Price	Maximum Field Order Work Amount
Less than \$100,001	\$2,500
\$100,001 to \$1,000,000	\$5,000
\$1,000,001 to \$5,000,000	\$10,000
\$5,000,001 to \$15,000,000	\$20,000
\$15,000,001 to \$30,000,000	\$40,000
Greater than \$30,000,000	\$50,000

2. Field Order items of Work for contracts greater than \$15,000,000 will require additional approvals from the City prior to its approval by the Resident Engineer.
3. The City will issue a Field Order only after the City's acceptance of the cost of the field order amount.
4. Field Orders shall not be used to add scope or to include extensions of time related to changes in work.
5. If in the event there is a change related to the critical path on the project which necessitates an extension of time and the change amount is within the Field Order limits shown on Table 7-3.9, then a Field Order can be issued to compensate you for the approved costs. Any extensions of time associated with the change shall be included in a subsequent Change Order and no additional compensation shall be granted as part of the change order for the extension of time.
6. The unused portions of Field Orders Bid item shall revert to the City upon Acceptance.

**7-3.11**

**Compensation Adjustments for Price Index Fluctuations.** To the "WHITEBOOK", ADD the following:

3. This Contract is subject to the provisions of The "WHITEBOOK" for Compensation Adjustments for Price Index Fluctuations for paving asphalt.

To the "WHITEBOOK", item 4, DELETE in its entirety and SUBSTITUTE with the following.

4. You may opt out of the payment adjustments for price index fluctuations by submitting a letter with the Bid.

## SECTION 203 – BITUMINOUS MATERIALS

**203-6.3.1 General.** To the “WHITEBOOK”, item 1, DELETE in its entirety and SUBSTITUTE with the following:

1. You shall submit for approval, mix designs for III-C2-PG 64-10 (1/2”) and III-B3-PG 64-10 (3/4”) asphalt concrete. Asphalt concrete mix designs shall be submitted to the City Materials Testing Laboratory for approval.

To the “WHITEBOOK”, ADD the following:

3. Asphalt concrete for Job Mix Formula (JMF) and Mix Designs shall be Type III and shall not exceed 15% RAP.

## SECTION 301 – SUBGRADE PREPARATION, TREATED MATERIALS, AND PLACEMENT OF BASE MATERIALS

**301-1.6 Preparatory Repair Work.** To the “WHITEBOOK”, DELETE in its entirety and SUBSTITUTE with the following:

1. Prior to the application of slurry, the Contractor shall complete all necessary preparation and repair work to the road segment as specified in the Special Provisions and Contract Documents or as directed by the engineer.
2. No preparatory asphalt work shall be done when the atmospheric temperature is below 50 °F or during unsuitable weather.
3. Preparatory Work shall include tree trimming, weed abatement, weed spraying, crack sealing, asphalt repair, base repair, removal of humps and pavement irregularities, raising appurtenances and survey monuments, reconstructing survey monument boxes, adjusting manhole frames & covers, removal of raised pavement markers, removal of pavement markings, and any other work and as specified in the Special Provisions and Contract Documents or as directed by the Engineer.
4. The quantities shown in the appendices are based on a street assessment survey and may vary. The Engineer will designate the limits to be removed and prepared and these designated areas shall be considered to take precedence over the areas shown in an Appendix to the Contract Documents.
5. Most areas of damaged asphalt requiring Asphalt Pavement Repair have been marked out in the field as “MP” or “DO” (mill & pave or dig-out). Mill & Paves shall have a minimum depth of 2”, and dig-outs, also called base repairs, shall have a minimum depth of 10”. Some areas (ie. those uplifted by tree roots) may be marked out in the field as “MP4” and shall have a minimum mill & pave depth of 4”.
6. The minimum repair area shall be 4 feet by 4 feet regardless of mark out.
7. Edges of milled areas shall be cut cleanly

8. Material removed, regardless of removal method, shall be disposed of at a legal site.
9. You shall repair marked out areas of distressed asphalt concrete pavement by milling, grinding, or saw cutting to remove damaged areas of pavement in accordance with 404-1, to expose firm and unyielding pavement, base or native. Unyielding pavement will have no visible cracks and unyielding base or native will be properly compacted, as determined by the Engineer. If cracks are visible, then pavement is not unyielding and shall require additional depth be removed. The Contractor shall prepare subgrade as needed and install a maximum of 5" compacted asphalt concrete pavement over compacted base material to be level with adjacent roadway surface.
10. If, in order to achieve the minimum specified depth, the base material is exposed, then the existing base material, as well as additional base material shall be compacted to 95% relative compaction to a depth 5" below the finished grade (dig-out).
11. Base repairs shall have a minimum depth of 10".
12. Compaction tests shall be made to ensure compliance with the specifications. The Engineer will determine when and where the test will occur. The City will pay for the soils testing required by the Engineer, which meets the required compaction. The Contractor shall reimburse the City for the cost of retesting failing compaction tests. If additional base material is required, the Contractor shall use Crushed Miscellaneous Base in accordance with 200-2.4. The base material shall be prepared conforming to 301-1, "Subgrade Preparation."
13. Recycled base material shall conform to Crushed Miscellaneous Base Material in accordance with 200-2.4, "Crushed Miscellaneous Base."
14. Base repairs shall not exceed 15% RAP in content.
15. Prior to replacing asphalt, the area shall be cleaned by removing all loose and damaged material, moisture, dirt, and other foreign matter and shall be tack coated in accordance with 302-5.4 "Tack Coat."
16. When milling and/or grinding asphalt pavement and the Contractor encounters solid, level unyielding PCC trench caps or appurtenance collars before reaching a minimum depth of 2", then the Contractor shall place enough asphalt concrete pavement to bring the surface to be level with the adjacent roadway.
17. The Contractor shall install new asphalt within the repair area or for patches in accordance with 302-5, "ASPHALT CONCRETE PAVEMENT." Asphalt concrete shall be III-B3-PG 64-10 (3/4") and III-C2-PG 64-10 (1/2") in compliance with 203-6, "ASPHALT CONCRETE."

18. Following the asphalt placement, the Contractor shall roll the entire area of new asphalt in both directions at least twice. The finished patch shall be level and smooth in compliance with 302-5.6.2 "Density and Smoothness."
19. At the end of each day the Contractor shall submit to the Engineer an itemized list of asphalt pavement and base repair work completed. The list shall include the location of the work, the exact square footage of the repair, tons of asphalt placed, and tons of base material placed.

**301-1.6.1 Asphalt Patching.** To the "WHITEBOOK", items 1, 2, and 5, DELETE in their entirety and SUBSTITUTE with the following:

1. Miscellaneous asphalt patching shall consist of patching potholes and skin patching other low spots in the pavement that are deeper than 1/4" per 302-5.6.2 "Density and Smoothness." These areas are generally smaller and more isolated than those areas in need of mill and pave.
2. The areas requiring patching have not been identified in the Contract Documents, nor in the field. The Contractor and/or Engineer shall identify areas that may require patching prior to slurry work to ensure the smoothness and quality of the finished product.
5. You shall remove distressed asphalt pavement either by saw cutting or milling to expose firm and unyielding pavement, prepare subgrade (as needed), and install compacted asphalt concrete pavement over prepared subgrade per 301-1, "Subgrade Preparation."

**301-1.7 Payment.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The payment for the preparatory works shall be included in the Contract Unit Bid Item for which preparation works are performed, unless it is specified as a separate Bid Item.
2. The areas and quantities shown on the road segments and in the appendices are given only for the Contractor's aid in planning the Work and preparing Bids. The Engineer will designate the limits to be removed and prepared and these designated areas shall be considered to take precedent over the areas shown in an Appendix to the Contract Documents. The quantities shown in the appendices are based on a street assessment survey and may vary. No payment shall be made for areas of over excavation as determined by the Engineer.
3. Asphalt pavement repair, including both mill & paves and base repair dig-outs, required for both mill & paves and base repair dig-outs, shall be paid at the Contract unit price per ton for "Asphalt Pavement Repair". No Payment shall be made for areas of over excavation as determined by the Engineer.
4. The payment for preparatory repair asphalt works shall be paid at the Contract Unit Price for "Asphalt Pavement Repair" for each ton placed and includes milling,

grinding, hauling, disposal or saw cutting of existing pavement, tree trimming, tack coating, compaction, and all other necessary work related to asphalt pavement installation.

No additional payment shall be made for milling, grinding, or saw cutting concrete, pavement fabric, rubberized material, steel reinforcement, or any other material.

5. Miscellaneous asphalt patching and tack coat shall be included in the unit price for Bid Item "Asphalt Pavement Repair" and no additional payment shall be made therefore regardless of number and location of patches.

**301-2.4 Measurement and Payment.** To the "GREENBOOK", ADD the following:

The payment for base repair dig-outs shall be paid at the Contract Unit Price for "Crushed Miscellaneous Base", for each ton placed and includes milling, grinding, excavating, hauling, disposal, or saw cutting of existing pavement, and all other necessary work related to asphalt base repair.

## **SECTION 302 – ROADWAY SURFACING**

**302-4.5 Scheduling, Public Convenience and Traffic Control.** To the "GREENBOOK", paragraphs (1) and (2), DELETE in their entirety and SUBSTITUTE with the following:

1. In addition to the requirements of Part 6, you shall comply with the following:
  - a) At least 5 Working Days prior to commencing the Work, you shall submit your proposed Schedule to the Engineer for approval.
  - b) Based upon the approved schedule, you shall notify residents and businesses of the Work and post temporary "No Parking" signs 72 hours in advance.
  - c) Requests for changes in the approved Schedule shall be submitted to the Engineer for approval at least 3 Working Days before the street is scheduled to be sealed.

**302-4.12.2 Application.** To the "WHITEBOOK", item 1, ADD the following:

- c) RPMS shall only be placed when ambient temperature is 50° F or higher.

To the "WHITEBOOK", item 2, subsection "b", ADD the following:

- iii. Where multiple layers of RPMS are specified, the first layer, regardless of Type, shall be placed a minimum of 1' from concrete gutters.



**302-4.12.4 Measurement and Payment.** To the "WHITEBOOK", item 2, DELETE in its entirety and SUBSTITUTE with the following:

2. The payment for RPMS shall be the total square footage used on the project calculated using the method described and shall be paid under the following Bid items:

BID DESCRIPTION	UNIT
Rubber Polymer Modified Slurry (RPMS) Type I (Select Streets)	SF
Rubber Polymer Modified Slurry (RPMS) Type II	SF
Rubber Polymer Modified Slurry (RPMS) Type I Over Type II	SF
Rubber Polymer Modified Slurry (RPMS) Type II Over Type III	SF
Rubber Polymer Modified Slurry (RPMS) Type I (Bike Lane)	SF

The Bid items for RPMS shall include full compensation for the specified surface preparation not included in other Bid items and shall include the Work necessary to construct the RPMS as specified on the Plans. Sweeping, removals, and furnishing the aggregate required for the mix design shall also be included in this Bid item. The removal, replacement, and installation for thermoplastic striping, traffic striping, markers, markings and devices shall be paid under the separate Bid Item for "Remove, Replace & Install Traffic Striping, Markers, Markings & Devices".

**302-15.1 General.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:

1. All cracks in asphalt 1/8 inch or wider but no greater than 1 inch wide shall be sealed prior to the application of slurry. You shall seal only transverse, longitudinal, block, or reflective cracks. You shall not seal alligator (fatigue) cracked areas or cracks in PCC.

**302-15.5 Payment.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following: Crack seal installed will be paid at the Contract unit price per pound for "Crack Seal".

**SECTION 314 – TRAFFIC STRIPING, CURB AND PAVEMENT MARKINGS, AND PAVEMENT MARKERS**

**314-1 GENERAL.** To the "GREENBOOK", ADD the following:

All crosswalks required for this contract shall be in conformance with Standard Drawing SDM-116 for Continental Crosswalks.

The Contractor shall install all traffic striping, pavement markings, pavement markers and devices within 15 working days after the last coat of slurry has been applied in accordance with current standards regardless of the existing conditions and installation will include the proposed striping modifications as identified in the Contract Document. All striping modifications shall be coordinated by the Engineer.

- 314-2.3**      **Payment.** To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:  
See 314-5.7
- 314-3.3**      **Payment.** To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:  
See 314-5.7
- 314-4.3.7**    **Payment.** To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:  
See 314-5.7
- 314-4.4.6**    **Payment.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:  
See 314-5.7
- 314-5.7**      **Payment.** To the "GREENBOOK", DELETE in its entirety and SUBSTITUTE with the following:
1.      All work, materials, labor, costs, and time associated with removing traffic striping, pavement markings and thermoplastics, removal of pavement markers and devices, installing painted traffic striping and markings, installing thermoplastics, installing continental crosswalks, replacement and installation of new pavement markers and devices shall be included in the lump sum bid item for "Remove, Replace & Install Traffic Striping, Markers, Markings & Devices" regardless of amount installed.  
  
This bid item also includes payment for the removal of existing traffic striping, pavement markings, and pavement markers for streets requiring striping modifications as indicated below.
    - a)      Old Carmel Valley Rd from Del Mar Heights to Briarcrest Pl
    - b)      Landsdale Dr from Del Mar Heights to Briarcrest Pl
    - c)      Via Valarta from Camino Playa Cancun to Clairemont Mesa Blvd
    - d)      Antigua Blvd from Santo Rd to Via Valarta
  2.      Payment for the installation of additional new striping for streets requiring striping modifications as indicated below shall be included in the allowance bid item "Striping Modifications":
    - a)      Old Carmel Valley Rd from Del Mar Heights to Briarcrest Pl
    - b)      Landsdale Dr from Del Mar Heights to Briarcrest Pl
    - c)      Via Valarta from Camino Playa Cancun to Clairemont Mesa Blvd
    - d)      Antigua Blvd from Santo Rd to Via Valarta

**SECTION 403 – MANHOLE, SURVEY MONUMENT, AND GATE VALVE FRAMES AND COVERS  
ADJUSTMENT AND RECONSTRUCTION**

- 403-3**      **MANHOLES AND GATE VALVES IN ASPHALT CONCRETE PAVEMENT.** To the "WHITEBOOK", DELETE Item 1 in its entirety, and SUBSTITUTE with the following:
1.      Manhole, sewer, and water valve covers shall be raised to be level with the surrounding pavement surface when such appurtenance are a minimum of one inch (1") below the final surface elevation after the slurry seal has been placed. Engineer to approve location prior to raising.

Appurtenances extending more than one inch (1") above the road surface shall be marked out as a mill & pave and asphalt ramped to smooth transition.

Utility structures projecting less than 2 inches (50 mm) above the subgrade may be paved over and later adjusted to grade.

**403-4 SURVEY MONUMENTS.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The casing and cover for survey monuments shall be adjusted to the new grade using riser rings, when such appurtenances are 1.5" to 3.75" below the surface, in accordance with Standard Drawing M-10B, "Street Survey Monument Overlay Adjustment" and Standard Drawing M-10C, "Street Survey Monument Notes".
2. The Survey Monument Precast Concrete Pipe Box must be reconstructed in accordance with Standard Drawing M-10B for survey monuments that are greater than 0.5" and less than 1.5" below the surface or if the lid has been damaged.
3. The Survey Monument Precast Concrete Pipe Box must be reconstructed in accordance with Standard Drawings M-10A and Standard Drawings M-10B for survey monuments that are greater than 3.75" below the surface.

**403-5 MEASUREMENT AND PAYMENT.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The payment for Raising Appurtenances to Grade, including sewer and water valve covers, all casings, extensions, concrete collars, and any necessary items to complete the work shall be made at the Bid unit "Raise Appurtenance to Grade (Water, Sewer)" for each appurtenance raised.
2. The payment for adjusting existing survey monument, including casing, frame, ring, covers, extensions, grout, brick support, sand base and any other material to grade shall be included in the Contract Bid Unit Price for "Adjust Existing Survey Monument to Grade" for each survey monument raised.
3. The payment for reconstructing the Survey Monument Precast Concrete Pipe Box, monument casing, frame, ring, covers, extensions, grout, brick support, sand base, and any other material required to reconstruct the survey monument precast concrete pipe box shall be included in the Contract Bid Unit Price for "Reconstruct Survey Monument Box" for each the Survey Monument Precast Concrete Pipe box reconstructed.
4. The payment for raising sewer and storm drain Manholes to grade, including casings, rings, extensions, concrete collars, asphalt, and any other materials, shall be made at the Bid unit price for "Adjust Existing Manhole Frame and Cover to Grade" for each manhole adjusted.

## **SECTION 404 – COLD MILLING**

**404-1 GENERAL.** To the "WHITEBOOK", ADD the following:

7. Edges of milled areas shall be cut cleanly. The outside edges of the milled pavement may have a radius transition on the sides parallel to the cutting drum.

8. The presence of roots, pavement fabric, concrete, rubberized material or steel reinforcement within the depth to be cold milled have not been noted, marked out in the field, or quantified.
9. All milling shall be performed in such a manner as to improve drainage, eliminate ponding, and re-establish gravity flow across intersections.
10. Material removed, regardless of removal method, shall be disposed of at a legal site.

**404-6 COLD MILLING OF COMPOSITE PAVEMENTS.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The areas and depths of composite pavement to be cold milled, sawn, or cut have not been identified in the field nor the Contract Documents.
2. Any pavement fabric encountered within the depth to be cold milled shall be disposed of at an approved facility within the jurisdiction of work.

**404-6.1 Cold Milling of Asphalt Concrete with Pavement Fabric Material.** To the "WHITEBOOK", DELETE in its entirety and SUBSTITUTE with the following:

1. The area of pavement containing pavement fabric has not been measured out in the field, quantified, or identified in the Contract Documents.
2. Any pavement fabric encountered within the depth to be cold milled shall be disposed of at an approved facility within the jurisdiction of work.

**404-9 TRAFFIC SIGNAL LOOP DETECTORS.** To the "WHITEBOOK", ADD the following:

6. All damaged traffic detector loop and/or other detection systems located within or adjacent to the limits of work shall be replaced after resurfacing and striping. "Q" loops may be required at bike lanes. "E Modified" loops are required at stop bars. You shall install as many loops as necessary to meet current standards.  
  
Loops may be installed in asphalt, concrete or any other material that may be encountered during the installation.

**404-12 PAYMENT.** To the "WHITEBOOK", item 1 and item 4, DELETE in their entirety and SUBSTITUTE with the following:

1. The payment for installation of traffic detector loops and conduits shall be included in the bid item "Traffic Detector Loop Replacement or Conduit Stub Installed" for each loop or conduit installed. No additional payment shall be made for loop, detector, or conduit type.  
  
No additional payment shall be made for milling grinding, or saw cutting concrete, asphalt pavement fabric, and any other material that may be encountered during the installation.

4. The payment for cold milling of the existing pavement shall be included in the contract bid unit price for which the milling is required ("Asphalt Pavement Repair", "Crushed Miscellaneous Base"), including hauling and disposal of milled material.

No additional payment shall be made for root pruning, milling, grinding, hauling, disposal or saw cutting concrete, and any other material that may be encountered during the installation.

No additional payment shall be made for the milling and grinding of pavement fabric.

To the "WHITEBOOK", ADD the following:

5. The payment for the hauling and disposal of asphalt pavement and fabric shall be included in the bid item "Asphalt Concrete with Pavement Fabric Material" per ton.

Payment for milling, grinding, or saw cutting asphalt pavement fabric shall be included in the contract bid unit price for which the milling is required ("Asphalt Pavement Repair", "Crushed Miscellaneous Base").

## **SECTION 601 - TEMPORARY TRAFFIC CONTROL FOR CONSTRUCTION AND MAINTENANCE WORK ZONES**

**601-2.1.4 Traffic Control for Resurfacing and Slurry Sealing.** To the "WHITEBOOK", item 3, subsection "d", DELETE in its entirety and SUBSTITUTE with the following:

- d) Place "NO PARKING - TOW-AWAY ZONE" signs 72 hours in advance of the scheduled slurry sealing. Reschedule street block segments which are not completed by the last posted Working Day. If a Work delay of 48 hours or more occurs from the originally scheduled Work date, remove the "NO PARKING - TOW-AWAY ZONE" signs for a minimum of 24 hours, then reset and re-post for the appropriate Work date.

**601-3.5.1 General.** To the "WHITEBOOK", item 3, DELETE in its entirety and SUBSTITUTE with the following:

3. Temporary "No Parking" and "No Stopping" signs shall be installed 72 hours before enforcement. Temporary "No Parking" and "No Stopping" signs shall be installed and removed as specified in the Special Provisions. Signs shall indicate specific days, dates, and times of restrictions. If violations occur, call Police Dispatch 619-531-2000 to enforce the Tow-Away notice.

**601-3.6 Channelizing Devices.** To the "WHITEBOOK", item 4, Barricades, ADD the following:

- h) You shall place "OPEN TRENCH" signs (C27(CA)) on Type 3 Barricade within the construction Work zone, ahead of any Work areas with open trenches that are greater than 3 inches in depth, in accordance with California MUTCD SECTION 6F.103 (CA). The barricades shall be placed in a continuous manner and shall prevent pedestrian, vehicular, and cyclist access to the open trench area.

**601-7**            **PAYMENT.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:

1.        The payment for traffic control Working Drawings, permits, traffic control Work including any traffic control devices that may be required by the City, shall be included in Lump Sum Bid Item for "Traffic Control and Working Drawings."
2.        No separate or additional payment shall be made for the following: operation, maintenance, repair, or replacement of Temporary Traffic (TTC) zone devices; all traffic control devices, required signs, notices, and detours; Work Drawings, Traffic Control Plans; labor; and traffic control for asphalt pavement repair, slurry seal, striping, loop installation, raising appurtenances (manholes, monuments, valves), or any other material relating to traffic control work.

### **SECTION 700 – MATERIALS**

**700-5.1**            **Vehicle Detectors.** To the "WHITEBOOK", item 1, DELETE in its entirety and SUBSTITUTE with the following:

1.        Loop wire shall be Type 2. Loop detector lead-in cable shall be Type "B". Slots shall be filled with elastomeric sealant, epoxy sealant, or hot-melt rubberized asphalt sealant, except asphaltic emulsion loop sealant and cold tar loop sealant are acceptable if the pavement surface will receive an asphaltic concrete overlay.

### **SECTION 1001 – CONSTRUCTION BEST MANAGEMENT PRACTICES (BMPs)**

**1001-1**            **GENERAL.** To the "WHITEBOOK", ADD the following:

7.        Based on a preliminary assessment by the City, this Contract is subject to **WPCP**.

**1001-1.11**        **Post-construction Requirement.** To the "WHITEBOOK", ADD the following:

6.        You shall comply with the following post-construction requirement: Storm Drain Inlet Markers.

**1001-4.2**        **Payment.** To the "WHITEBOOK", ADD the following:

4.        All work, materials, labor, costs, and time associated with installing inlet markers shall be paid at the unit bid price "Post-construction Requirements – Inlet Markers" for each marker installed.

**SUPPLEMENTARY SPECIAL PROVISIONS**  
**APPENDICES**

**APPENDIX A**  
**NOTICE OF EXEMPTION**



## NOTICE OF EXEMPTION

TO:   X   Recorder County Clerk  
P.O. Box 1750, MS-A-33  
1600 Pacific Hwy, Room 260  
San Diego, CA 92101-2422

FROM: City of San Diego  
Planning Department  
9485 Aero Drive, MS 413  
San Diego, CA 92123

       Office of Planning and Research  
1400 Tenth Street, Room 121  
Sacramento, CA 95814

PROJECT TITLE: Slurry Seal Group S2023

PROJECT LOCATION-SPECIFIC: See Attachment A: Location List for specific locations. The project is located in the Community Planning Areas of Carmel Valley, Clairemont Mesa, Mira Mesa, Miramar Ranch North, Pacific Highlands Ranch, Rancho Peñsaquitos, Serra Mesa, Scripps Miramar Ranch, Tierrasanta, and University within Council Districts 1, 5, 6, and 7.

PROJECT LOCATION-CITY/COUNTY: San Diego/San Diego

DESCRIPTION OF NATURE AND PURPOSE OF THE PROJECT: The project involves furnishing all labor, materials, equipment, services, and construction related to slurry seal work on existing previous slurry seal paved roadways in various areas throughout the City of San Diego. The work includes; placement of rubber polymer modified slurry (RPMS), crack sealing, removal of humps and pavement irregularities, asphalt mill and pave, and dig outs, pavement base repairs, milling and disposal of pavement fabric, replacing traffic signal detection loops and stub outs, adjusting existing City manhole frames and covers to grade, raising appurtenances to grade (water, sewer), raising survey monuments to grade, reconstructing survey monument boxes, street and sidewalk sweeping, removal and replacement of existing thermoplastic striping and markings/legends, traffic control drawings and permits, weed abatement, storm drain inlet protection, installation of inlet markers, sediment control, and possible night and weekend work. All work would occur within the public right-of-way (paved streets) or previously disturbed non-sensitive areas only, and outside of the City's Multi-Habitat Planning Area (MHPA). No sensitive vegetation would be impacted or removed. Storm Water Best Management Practices (BMPs) for erosion control preventing discharge, as well as Traffic Control Plan (TCP) would be implemented throughout construction.

NAME OF PUBLIC AGENCY APPROVING PROJECT: City of San Diego

NAME OF PERSON OR AGENCY CARRYING OUT PROJECT: City of San Diego - Transportation and Storm Water Department, 2781 Caminito Chollas, San Diego, CA 92105. Contact: Soomin Hwang, Junior Engineer - Civil, (619) 527-8075 / shwang@sandiego.gov

EXEMPT STATUS:

- MINISTERIAL
- DECLARED EMERGENCY
- EMERGENCY PROJECT
- CATEGORICAL EXEMPTION: CEQA Guidelines Section 15301 (Existing Facilities)
- STATUTORY EXEMPTION
- COMMON SENSE EXEMPTION:

REASONS WHY PROJECT IS EXEMPT: The City of San Diego conducted an environmental review and determined the project is exempt from CEQA pursuant to State CEQA Guidelines Section 15301 (Existing Facilities) which consists of the operation, repair, maintenance, permitting, leasing, licensing, or minor alteration of existing public or private structures, facilities, mechanical equipment, or topographical features, involving negligible or no expansion of existing or former use. This includes existing highways and streets, sidewalks, gutters, bicycle and pedestrian trails, and similar facilities (this includes road grading for the purpose of public safety), and other alterations such as the addition of bicycle facilities, including but not limited to bicycle parking, bicycle-share facilities and bicycle lanes, transit improvements such as bus lanes, pedestrian crossings, street trees, and other similar alterations that do not create additional automobile lanes. The exemptions listed in State CEQA Guidelines Section 15300.2 would not apply in that no cumulative impacts were identified, no significant effects on the environment were identified, the project is not adjacent to a scenic highway, and no historical resources would be affected by the action. As to the exception for hazardous materials, there are locations listed on GeoTracker and EnviroStor within 1,000 feet of the public right-of-way. While these locations are listed, the proposed project would not involve ground disturbance which would expose potential hazardous materials, and as such would not preclude the use of a CEQA exemption pursuant to Section 65962.5 of the Government Code.

CONTACT PERSON: Tara Ash-Reynolds, Junior Planner  
City of San Diego - Planning Department  
9485 Aero Drive, MS 413, San Diego, CA 92123

TELEPHONE: 619-533-6492

IF FILED BY APPLICANT:

1. ATTACH CERTIFIED DOCUMENT OF EXEMPTION FINDING
2. HAS A NOTICE OF EXEMPTION BEEN FILED BY THE PUBLIC AGENCY APPROVING THE PROJECT?  
(X) YES ( ) NO

IT IS HEREBY CERTIFIED THAT THE CITY OF SAN DIEGO HAS DETERMINED THE ABOVE ACTIVITY TO BE EXEMPT FROM CEQA.



---

Myra Herrmann, Senior Planner, Planning Department

7/24/2020

DATE

CHECK ONE:

- (X) SIGNED BY LEAD AGENCY    DATE RECEIVED FOR FILING WITH COUNTY CLERK OR OPR:  
( ) SIGNED BY APPLICANT

Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
BERRYFIELD CT	WYNDHAVEN DR	END	1	CARMEL VALLEY
BLACK PINE PL	CHAPARRAL RIDGE RD	END	1	CARMEL VALLEY
BRIARCREST PL	BEGIN	WHITE OAK LN	1	PACIFIC HIGHLANDS RANCH
BRIARCREST PL	VINWOOD CT	FLINTWOOD WY	1	PACIFIC HIGHLANDS RANCH
BRIARCREST PL	WHITE OAK LN	VINWOOD CT	1	PACIFIC HIGHLANDS RANCH
CALLE DE LA SIENA	CAM SANDOVAL	END	1	CARMEL VALLEY
CALLE DE LA SIENA	CTE DE LA SIENA	PASEO MONTANAS	1	CARMEL VALLEY
CALLE DE LA SIENA	PASEO MONTANAS	PLAZA DE LA SIENA	1	CARMEL VALLEY
CALLE DE LA SIENA	PLAZA DE LA SIENA	CAM SANDOVAL	1	CARMEL VALLEY
CAM SANDOVAL	CARMEL CREEK RD	CALLE DE LA SIENA	1	CARMEL VALLEY
CAMARENA RD	CARMEL CENTER RD	CTE FACIL	1	CARMEL VALLEY
CAMARENA RD	CTE FAVOR	KERWOOD CT	1	CARMEL VALLEY
CAMARENA RD	KERWOOD CT	STURGEON CT	1	CARMEL VALLEY
CAMARENA RD	STURGEON CT	GRAYDON RD	1	CARMEL VALLEY
CAMARENA RD	CTE FAMOSA	CTE FAVOR	1	CARMEL VALLEY
CAMARENA RD	CTE FACIL	CTE FAMOSA	1	CARMEL VALLEY
CARMEL CENTER RD	MONTEREY CYPRESS WY	INTERMEZZO WY	1	CARMEL VALLEY
CARMEL CENTER RD	FALCONRIDGE CT	OCEAN VALLEY LN	1	CARMEL VALLEY
CARMEL CENTER RD	CARMEL KNOLLS DR	FALCONRIDGE CT	1	CARMEL VALLEY
CARMEL CENTER RD	CAMARENA RD	CTE AL FRESCO	1	CARMEL VALLEY
CARMEL CENTER RD	CARMEL CREEK RD	CAMARENA RD	1	CARMEL VALLEY
CARMEL CENTER RD	SUNSET BLUFFS WY	MENSHA PL	1	CARMEL VALLEY
CARMEL CENTER RD	INTERMEZZO WY	HERITAGE GLEN LN	1	CARMEL VALLEY
CARMEL CENTER RD	HERITAGE GLEN LN	CARMEL KNOLLS DR	1	CARMEL VALLEY
CARMEL CENTER RD	CTE AL FRESCO	CTE DE LA FONDA	1	CARMEL VALLEY
CARMEL CENTER RD	FOXHOLLOW CT	SUNSET BLUFFS WY	1	CARMEL VALLEY
CARMEL CENTER RD	CTE DE LA FONDA	FUTURA ST	1	CARMEL VALLEY
CARMEL CENTER RD	MENSHA PL	GRAYDON RD	1	CARMEL VALLEY
CARMEL CENTER RD	LUPITA CT	CARMEL MISSION RD	1	CARMEL VALLEY
CARMEL CENTER RD	CARMEL MISSION RD	LONE CYPRESS PL	1	CARMEL VALLEY
CARMEL CENTER RD	FUTURA ST	LUPITA CT	1	CARMEL VALLEY
CARMEL CENTER RD	LONE CYPRESS PL	MONTEREY CYPRESS WY	1	CARMEL VALLEY
CARMEL CENTER RD	OCEAN VALLEY LN	FOXHOLLOW CT	1	CARMEL VALLEY
CARMEL CREEK RD	VIA CANDIDIZ	CARMEL CENTER RD	1	CARMEL VALLEY
CARMEL CREEK RD	CARMEL COUNTRY RD	PASEO MONTANAS	1	CARMEL VALLEY
CARMEL CREEK RD	CARMEL CENTER RD	MC GUIRE DR	1	CARMEL VALLEY
CARMEL CREEK RD	CAM SANDOVAL	VIA CANDIDIZ	1	CARMEL VALLEY
CARMEL CREEK RD	PASEO MONTANAS	CAM SANDOVAL	1	CARMEL VALLEY
CARMEL MISSION RD	CARMEL COUNTRY RD	CARMEL CENTER RD	1	CARMEL VALLEY
CHAMBORD WY	PORTER CREEK RD	GAMAY WY	1	PACIFIC HIGHLANDS RANCH
CHAMBORD WY	RABBIT RIDGE RD	PORTER CREEK RD	1	PACIFIC HIGHLANDS RANCH
CHAMBORD WY	MILL CREEK RD	RABBIT RIDGE RD	1	PACIFIC HIGHLANDS RANCH
CHAMBORD WY	GAMAY WY	SUNSTONE PE	1	PACIFIC HIGHLANDS RANCH
CHAPARRAL RIDGE RD	TIMBER RIDGE RD	WISPERING WOODS CT	1	CARMEL VALLEY
CHAPARRAL RIDGE RD	BEGIN	SUNSET BLUFFS WY	1	CARMEL VALLEY
CHAPARRAL RIDGE RD	BLACK PINE PL	TIMBER RIDGE RD	1	CARMEL VALLEY
CHAPARRAL RIDGE RD	SADDLE MTN CT	BLACK PINE PL	1	CARMEL VALLEY
CHAPARRAL RIDGE RD	SUNSET BLUFFS WY	SADDLE MTN CT	1	CARMEL VALLEY
CLAYMONT CT	GRAYDON RD	END	1	CARMEL VALLEY

Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
CORBETT CT	TIMBER RIDGE RD	END	1	CARMEL VALLEY
CORBETT CT	BEGIN	TIMBER RIDGE RD	1	CARMEL VALLEY
CRISTALLO PL	GRAYDON RD	FEDERMAN LN	1	CARMEL VALLEY
CRISTALLO PL	FEDERMAN LN	END	1	CARMEL VALLEY
CTE AL FRESCO	CARMEL CENTER RD	END	1	CARMEL VALLEY
CTE DE LA FONDA	CARMEL CENTER RD	END	1	CARMEL VALLEY
CTE DE LA SIENA	BEGIN	CALLE DE LA SIENA	1	CARMEL VALLEY
CTE DE LA SIENA	CALLE DE LA SIENA	END	1	CARMEL VALLEY
CTE FACIL	CAMARENA RD	END	1	CARMEL VALLEY
CTE FAMOSA	CAMARENA RD	END	1	CARMEL VALLEY
CTE FAVOR	CAMARENA RD	END	1	CARMEL VALLEY
CYPRESS GLEN PL	MONTEREY CYPRESS WY	END	1	CARMEL VALLEY
DEER PARK WY	RABBIT RIDGE RD	PORTER CREEK RD	1	PACIFIC HIGHLANDS RANCH
DEER PARK WY	PORTER CREEK RD	GAMAY WY	1	PACIFIC HIGHLANDS RANCH
DEER PARK WY	MILL CREEK RD	RABBIT RIDGE RD	1	PACIFIC HIGHLANDS RANCH
FALCONRIDGE CT	CARMEL CENTER RD	END	1	CARMEL VALLEY
FEDERMAN LN	PERCY CT	CRISTALLO PL	1	CARMEL VALLEY
FEDERMAN LN	GRAYDON RD	QUINNEL CT	1	CARMEL VALLEY
FEDERMAN LN	QUINNEL CT	PERCY CT	1	CARMEL VALLEY
FLINTWOOD WY	SONOMA PL	BRIARCREST PL	1	PACIFIC HIGHLANDS RANCH
FOXHOLLOW CT	BEGIN	CARMEL CENTER RD	1	CARMEL VALLEY
FUTURA ST	MISTRAL PL	CARMEL CENTER RD	1	CARMEL VALLEY
FUTURA ST	CARMEL CENTER RD	END	1	CARMEL VALLEY
GAMAY WY	OLD CARMEL VALLEY RD	CHAMBORD WY	1	PACIFIC HIGHLANDS RANCH
GAMAY WY	CHAMBORD WY	SUNSTONE PE	1	PACIFIC HIGHLANDS RANCH
GAMAY WY	SUNSTONE PE	DEER PARK WY	1	PACIFIC HIGHLANDS RANCH
GRAYDON RD	LANSDALE DR	CLAYMONT CT	1	CARMEL VALLEY
GRAYDON RD	TORREY BLUFF DR	FEDERMAN LN	1	CARMEL VALLEY
GRAYDON RD	CRISTALLO PL	LANSDALE DR	1	CARMEL VALLEY
GRAYDON RD	FEDERMAN LN	CAMARENA RD	1	CARMEL VALLEY
GRAYDON RD	CAMARENA RD	CRISTALLO PL	1	CARMEL VALLEY
GRAYDON RD	CLAYMONT CT	CARMEL CENTER RD	1	CARMEL VALLEY
GREENWICH DR	BEGIN	SHOREHAM PL	1	UNIVERSITY
GREENWICH DR	SHOREHAM PL	GOVERNOR DR	1	UNIVERSITY
HALF MILE DR	LANDFAIR RD	EL CAM REAL	1	CARMEL VALLEY
HALF MILE DR	HIGH BLUFF DR	TIVERTON RD	1	CARMEL VALLEY
HALF MILE DR	TIVERTON RD	LANDFAIR RD	1	CARMEL VALLEY
HERITAGE GLEN CT	HERITAGE GLEN LN	END	1	CARMEL VALLEY
HERITAGE GLEN LN	BEGIN	HERITAGE GLEN CT	1	CARMEL VALLEY
HERITAGE GLEN LN	HERITAGE GLEN CT	CARMEL CENTER RD	1	CARMEL VALLEY
KERWOOD CT	CAMARENA RD	END	1	CARMEL VALLEY
KERWOOD CT	BEGIN	CAMARENA RD	1	CARMEL VALLEY
LANDFAIR RD	NEWCREST PT	WINDSWEPT TR	1	CARMEL VALLEY
LANDFAIR RD	HIGH BLUFF DR	NEWCREST PT	1	CARMEL VALLEY
LANDFAIR RD	WINDSWEPT TR	HALF MILE DR	1	CARMEL VALLEY
LANSDALE DR	GRAYDON RD	DEL MAR HEIGHTS RD	1	CARMEL VALLEY
LONE CYPRESS PL	BEGIN	CARMEL CENTER RD	1	CARMEL VALLEY
LUPITA CT	BEGIN	CARMEL CENTER RD	1	CARMEL VALLEY
MC GUIRE DR	CARMEL COUNTRY RD	CARMEL CREEK RD	1	CARMEL VALLEY

Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
MENSHA PL	RALSTON CR	CARMEL CENTER RD	1	CARMEL VALLEY
MENSHA PL	BEGIN	RALSTON CR	1	CARMEL VALLEY
MILL CREEK RD	FLINTWOOD WY	DEER PARK WY	1	PACIFIC HIGHLANDS RANCH
MILL CREEK RD	CHAMBORD WY	FLINTWOOD WY	1	PACIFIC HIGHLANDS RANCH
MILL CREEK RD	OLD CARMEL VALLEY RD	CHAMBORD WY	1	PACIFIC HIGHLANDS RANCH
MISTRAL PL	BEGIN	FUTURA ST	1	CARMEL VALLEY
MISTRAL PL	FUTURA ST	END	1	CARMEL VALLEY
MONTEREY CYPRESS WY	BEGIN	CYPRESS GLEN PL	1	CARMEL VALLEY
MONTEREY CYPRESS WY	CYPRESS GLEN PL	CARMEL CENTER RD	1	CARMEL VALLEY
MONTEREY CYPRESS WY	CARMEL CENTER RD	END	1	CARMEL VALLEY
NEWCREST PT	LANDFAIR RD	END	1	CARMEL VALLEY
OCEAN VALLEY LN	CARMEL CENTER RD	END	1	CARMEL VALLEY
OCEAN VALLEY LN	BEGIN	CARMEL CENTER RD	1	CARMEL VALLEY
OLD CARMEL VALLEY RD	MILL CREEK RD	GAMAY WY	1	CARMEL VALLEY
OLD CARMEL VALLEY RD	SR-56 WB	WHITE OAK LN	1	PACIFIC HIGHLANDS RANCH
OLD CARMEL VALLEY RD	WHITE OAK LN	SANDOWN WY	1	PACIFIC HIGHLANDS RANCH
OLD CARMEL VALLEY RD	GAMAY WY	DEL MAR HEIGHTS RD	1	PACIFIC HIGHLANDS RANCH
OLD CARMEL VALLEY RD	SANDOWN WY	MILL CREEK RD	1	PACIFIC HIGHLANDS RANCH
PASEO MONTANAS	CARMEL CREEK RD	CALLE DE LA SIENA	1	CARMEL VALLEY
PINE MEADOW CT	SUNSET BLUFFS WY	END	1	CARMEL VALLEY
PLAZA DE LA SIENA	CALLE DE LA SIENA	END	1	CARMEL VALLEY
PORTER CREEK RD	CHAMBORD WY	DEER PARK WY	1	PACIFIC HIGHLANDS RANCH
QUARTER MILE DR	LONG RUN DR	EL CAM REAL	1	CARMEL VALLEY
QUINNEL CT	BEGIN	FEDERMAN LN	1	CARMEL VALLEY
RABBIT RIDGE RD	CHAMBORD WY	DEER PARK WY	1	PACIFIC HIGHLANDS RANCH
RALSTON CR	MENSHA PL	END	1	CARMEL VALLEY
SADDLE MTN CT	BEGIN	CHAPARRAL RIDGE RD	1	CARMEL VALLEY
SHOREHAM PL	BEGIN	GREENWICH DR	1	UNIVERSITY
SONOMA PL	WHITE OAK LN	FLINTWOOD WY	1	PACIFIC HIGHLANDS RANCH
STURGEON CT	BEGIN	CAMARENA RD	1	CARMEL VALLEY
STURGEON CT	CAMARENA RD	END	1	CARMEL VALLEY
SUNSET BLUFFS WY	BEGIN	PINE MEADOW CT	1	CARMEL VALLEY
SUNSET BLUFFS WY	CARMEL CENTER RD	CHAPARRAL RIDGE RD	1	CARMEL VALLEY
SUNSET BLUFFS WY	PINE MEADOW CT	CARMEL CENTER RD	1	CARMEL VALLEY
SUNSTONE PE	GAMAY WY	CHAMBORD WY	1	PACIFIC HIGHLANDS RANCH
SUNSTONE PE	CHAMBORD WY	END	1	PACIFIC HIGHLANDS RANCH
TIMBER RIDGE RD	CARMEL CENTER RD	CORBETT CT	1	CARMEL VALLEY
TIMBER RIDGE RD	CORBETT CT	CHAPARRAL RIDGE RD	1	CARMEL VALLEY
TIVERTON RD	WYNDHAVEN DR	HALF MILE DR	1	CARMEL VALLEY
TORREY BLUFF DR	CARMEL CREEK RD	GRAYDON RD	1	CARMEL VALLEY
TORREY RIDGE DR	GRAYDON RD	DEL MAR HEIGHTS RD	1	CARMEL VALLEY
VINWOOD CT	BRIARCREST PL	END	1	PACIFIC HIGHLANDS RANCH
WHITE OAK LN	OLD CARMEL VALLEY RD	SONOMA PL	1	PACIFIC HIGHLANDS RANCH
WHITE OAK LN	SONOMA PL	BRIARCREST PL	1	PACIFIC HIGHLANDS RANCH
WINDSWEPT TR	LANDFAIR RD	END	1	CARMEL VALLEY
WISPERING WOODS CT	CHAPARRAL RIDGE RD	END	1	CARMEL VALLEY
ACCRA LN	TONDINO RD	WEATHERWOOD TR	5	SCRIPPS MIRAMAR RANCH
ANCONA LN	BEGIN	SUNSET RIDGE DR	5	SCRIPPS MIRAMAR RANCH
ARBORLAKE WY	POINTED OAK LN	POINTED OAK LN	5	SCRIPPS MIRAMAR RANCH
BIRCH BLUFF AV	BIRCH BLUFF PL	FIGTREE ST	5	SCRIPPS MIRAMAR RANCH

Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
BIRCH BLUFF AV	FIGTREE ST	END	5	SCRIPPS MIRAMAR RANCH
BIRCH BLUFF PL	BIRCH BLUFF AV	END	5	SCRIPPS MIRAMAR RANCH
BIRCH GLEN CT	BEGIN	PEPPERBROOK LN	5	SCRIPPS MIRAMAR RANCH
BRIGHTON RIDGE CT	HELMER LN	END	5	SCRIPPS MIRAMAR RANCH
CANARYWOOD CT	SUNSET RIDGE DR	END	5	SCRIPPS MIRAMAR RANCH
CHAPARAL VALLEY CT	BEGIN	SYCAMORE RIDGE CT	5	SCRIPPS MIRAMAR RANCH
CHAPARAL VALLEY CT	SYCAMORE RIDGE CT	EDENOAKS ST	5	SCRIPPS MIRAMAR RANCH
EDENOAKS ST	CHAPARAL VALLEY CT	END	5	SCRIPPS MIRAMAR RANCH
EDENOAKS ST	SEMILLON BL	CHAPARAL VALLEY CT	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	OAKFORT CT	SEMILLON BL	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	CAMTO MAGNIFICA	RUE FONTENAY	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	RUE FONTENAY	RUE CHAMBERRY	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	POMERADO RD	CAMTO MAGNIFICA	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	THORNBRUSH CT	WALNUTDALE ST	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	RUE CHANTEMAR	THORNBRUSH CT	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	WALNUTDALE ST	OAKFORT PL	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	OAKFORT PL	OAKFORT CT	5	SCRIPPS MIRAMAR RANCH
FAIRBROOK RD	RUE CHAMBERRY	RUE CHANTEMAR	5	SCRIPPS MIRAMAR RANCH
FIGTREE ST	BEGIN	FIGTREE CT	5	SCRIPPS MIRAMAR RANCH
FIGTREE ST	FIGTREE CT	BIRCH BLUFF AV	5	SCRIPPS MIRAMAR RANCH
FRANK DANIELS WY	BEGIN	HELMER LN	5	SCRIPPS MIRAMAR RANCH
GATEMOORE WY	SCRIPPS CREEK DR	MONTAUBON WY	5	MIRAMAR RANCH NORTH
GATEMOORE WY	SCRIPPS CREEK DR	WALDORF WY	5	MIRAMAR RANCH NORTH
GATEMOORE WY	WALDORF WY	END	5	MIRAMAR RANCH NORTH
GRAINWOOD WY	BEGIN	KINGSPINE AV	5	SCRIPPS MIRAMAR RANCH
HELMER LN	BRIGHTON RIDGE CT	FRANK DANIELS WY	5	SCRIPPS MIRAMAR RANCH
HELMER LN	SUNSET RIDGE DR	BRIGHTON RIDGE CT	5	SCRIPPS MIRAMAR RANCH
KINGSPINE AV	GRAINWOOD WY	SEMILLON BL	5	SCRIPPS MIRAMAR RANCH
KINGSPINE AV	BARRYWOOD WY	GRAINWOOD WY	5	SCRIPPS MIRAMAR RANCH
KINGSPINE AV	SPRUCE GROVE AV	BARRYWOOD WY	5	SCRIPPS MIRAMAR RANCH
LARMIER CR	BEGIN	POCHE PT	5	SCRIPPS MIRAMAR RANCH
LARMIER CR	POCHE PT	SPRING CANYON RD	5	SCRIPPS MIRAMAR RANCH
LIVEWOOD WY	BEGIN	SEMILLON BL	5	SCRIPPS MIRAMAR RANCH
MEADOWDALE LN	WALNUTDALE ST	END	5	SCRIPPS MIRAMAR RANCH
MEADOWDALE LN	PINECASTLE ST	WALNUTDALE ST	5	SCRIPPS MIRAMAR RANCH
MIRA LAGO TR	SCRIPPS LAKE DR	MIRA LAGO WY	5	SCRIPPS MIRAMAR RANCH
MIRA LAGO WY	MIRA LAGO TR	SUNSET RIDGE DR	5	SCRIPPS MIRAMAR RANCH
MONTAUBON CR	MONTAUBON WY	MONTAUBON WY	5	MIRAMAR RANCH NORTH
MONTAUBON WY	MONTAUBON CR	MONTAUBON CR	5	MIRAMAR RANCH NORTH
MONTAUBON WY	WALDORF WY	GATEMOORE WY	5	MIRAMAR RANCH NORTH
MONTAUBON WY	MONTAUBON CR	END	5	MIRAMAR RANCH NORTH
MONTAUBON WY	WALDORF WY	MONTAUBON CR	5	MIRAMAR RANCH NORTH
OAKFORT CT	FAIRBROOK RD	END	5	SCRIPPS MIRAMAR RANCH
OAKFORT PL	BEGIN	FAIRBROOK RD	5	SCRIPPS MIRAMAR RANCH
PEPPERBROOK LN	BIRCH GLEN CT	END	5	SCRIPPS MIRAMAR RANCH
PEPPERBROOK LN	TIMBERLAKE DR	BIRCH GLEN CT	5	SCRIPPS MIRAMAR RANCH
POCHE PT	LARMIER CR	END	5	SCRIPPS MIRAMAR RANCH
POINTED OAK LN	ARBORLAKE WY	ARBORLAKE WY	5	SCRIPPS MIRAMAR RANCH
POINTED OAK LN	ARBORLAKE WY	SCRIPPS TL	5	SCRIPPS MIRAMAR RANCH

Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
POYNTELL CR	TIMBERLAKE DR	END	5	SCRIPPS MIRAMAR RANCH
ROUGEMONT PL	BEGIN	END	5	SCRIPPS MIRAMAR RANCH
ROUGEMONT PL	RUE CHAMONIX	RUE CHANTEMAR	5	SCRIPPS MIRAMAR RANCH
ROUGEMONT PL	BEGIN	RUE CHAMONIX	5	SCRIPPS MIRAMAR RANCH
RUE CHAMBERRY	RUE CHANTEMAR	RUE CHEAUMONT	5	SCRIPPS MIRAMAR RANCH
RUE CHAMONIX	ROUGEMONT PL	END	5	SCRIPPS MIRAMAR RANCH
RUE CHAMONIX	BEGIN	ROUGEMONT PL	5	SCRIPPS MIRAMAR RANCH
RUE CHANTEMAR	RUE MARABELLE	FAIRBROOK RD	5	SCRIPPS MIRAMAR RANCH
RUE CHANTEMAR	ROUGEMONT PL	RUE PARC	5	SCRIPPS MIRAMAR RANCH
RUE CHANTEMAR	RUE PARC	RUE SIENNE NORD	5	SCRIPPS MIRAMAR RANCH
RUE CHANTEMAR	RUE VINCENNES	ROUGEMONT PL	5	SCRIPPS MIRAMAR RANCH
RUE CHANTEMAR	RUE CHAMBERRY	RUE VINCENNES	5	SCRIPPS MIRAMAR RANCH
RUE CHANTEMAR	RUE SIENNE NORD	RUE MARABELLE	5	SCRIPPS MIRAMAR RANCH
RUE FINISTERRE	RUE RIVIERE VERTE	RUE RIVIERE VERTE	5	SCRIPPS MIRAMAR RANCH
RUE FINISTERRE	RUE TOURAINE	RUE PARC	5	SCRIPPS MIRAMAR RANCH
RUE FINISTERRE	RUE PARC	RUE RIVIERE VERTE	5	SCRIPPS MIRAMAR RANCH
RUE FONTENAY	FAIRBROOK RD	RUE FONTENAY CT	5	SCRIPPS MIRAMAR RANCH
RUE FONTENAY	RUE FONTENAY CT	END	5	SCRIPPS MIRAMAR RANCH
RUE FONTENAY CT	BEGINNING	RUE FONTENAY	5	SCRIPPS MIRAMAR RANCH
RUE MARABELLE	RUE CHANTEMAR	END	5	SCRIPPS MIRAMAR RANCH
RUE PARC	RUE TOURAINE	RUE FINISTERRE	5	SCRIPPS MIRAMAR RANCH
RUE PARC	RUE CHANTEMAR	RUE TOURAINE	5	SCRIPPS MIRAMAR RANCH
RUE RIVIERE VERTE	RUE FINISTERRE	RUE FINISTERRE	5	SCRIPPS MIRAMAR RANCH
RUE SIENNE NORD	BEGIN	RUE CHANTEMAR	5	SCRIPPS MIRAMAR RANCH
RUE TOURAINE	RUE PARC	RUE FINISTERRE	5	SCRIPPS MIRAMAR RANCH
SCRIPPS CAPE VISTA PT	BEGIN	SUNSET RIDGE DR	5	SCRIPPS MIRAMAR RANCH
SCRIPPS CREEK DR	GATEMOORE WY	SPRING CANYON RD	5	MIRAMAR RANCH NORTH
SCRIPPS TL	REDFERN CR	POINTED OAK LN	5	SCRIPPS MIRAMAR RANCH
SCRIPPS TL	POINTED OAK LN	WEATHERWOOD TR	5	SCRIPPS MIRAMAR RANCH
SCRIPPS TL	WEATHERWOOD TR	SEMILLON BL	5	SCRIPPS MIRAMAR RANCH
SCRIPPS TL	TIMBERLAKE DR	GLENCREEK CR	5	SCRIPPS MIRAMAR RANCH
SCRIPPS TL	GLENCREEK CR	REDFERN CR	5	SCRIPPS MIRAMAR RANCH
SEMILLON BL	FAIRBROOK RD	BIRCH BLUFF AV	5	SCRIPPS MIRAMAR RANCH
SEMILLON BL	LIVEWOOD WY	KINGSPINE AV	5	SCRIPPS MIRAMAR RANCH
SEMILLON BL	BIRCH BLUFF AV	END	5	SCRIPPS MIRAMAR RANCH
SEMILLON BL	SPRUCE GROVE AV	EDENOAKS ST	5	SCRIPPS MIRAMAR RANCH
SEMILLON BL	POMERADO RD	SPRUCE GROVE AV	5	SCRIPPS MIRAMAR RANCH
SEMILLON BL	KINGSPINE AV	FAIRBROOK RD	5	SCRIPPS MIRAMAR RANCH
SEMILLON BL	EDENOAKS ST	LIVEWOOD WY	5	SCRIPPS MIRAMAR RANCH
SHERRARD WY	WALDORF WY	END	5	MIRAMAR RANCH NORTH
SPRUCE GROVE AV	SPRUCE GROVE PL	SEMILLON BL	5	SCRIPPS MIRAMAR RANCH
SPRUCE GROVE AV	KINGSPINE AV	SPRUCE GROVE PL	5	SCRIPPS MIRAMAR RANCH
SPRUCE GROVE PL	BEGIN	SPRUCE GROVE AV	5	SCRIPPS MIRAMAR RANCH
SUNSET RIDGE DR	ASHLAR PL	ANCONA LN	5	SCRIPPS MIRAMAR RANCH
SUNSET RIDGE DR	HELMER LN	SCRIPPS CAPE VISTA PT	5	SCRIPPS MIRAMAR RANCH
SUNSET RIDGE DR	STEUER WY	ASHLAR PL	5	SCRIPPS MIRAMAR RANCH
SUNSET RIDGE DR	MIRA LAGO WY	STEUER WY	5	SCRIPPS MIRAMAR RANCH
SUNSET RIDGE DR	SCRIPPS CAPE VISTA PT	MIRA LAGO WY	5	SCRIPPS MIRAMAR RANCH
SUNSET RIDGE DR	TIMBERLAKE DR	SCRIPPS LAKE DR	5	SCRIPPS MIRAMAR RANCH



Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
SUNSET RIDGE DR	SCRIPPS LAKE DR	HELMER LN	5	SCRIPPS MIRAMAR RANCH
SUNSET RIDGE DR	ANCONA LN	CANARYWOOD CT	5	SCRIPPS MIRAMAR RANCH
SYCAMORE RIDGE CT	CHAPARAL VALLEY CT	END	5	SCRIPPS MIRAMAR RANCH
THORNBRUSH CT	BEGIN	FAIRBROOK RD	5	SCRIPPS MIRAMAR RANCH
TIMBERLAKE DR	SUMMERWOOD CT	PEPPERBROOK LN	5	SCRIPPS MIRAMAR RANCH
TIMBERLAKE DR	QUAIL SPRINGS CT	SUMMERWOOD CT	5	SCRIPPS MIRAMAR RANCH
TIMBERLAKE DR	PEPPERBROOK LN	SUNSET RIDGE DR	5	SCRIPPS MIRAMAR RANCH
TIMBERLAKE DR	SCRIPPS LAKE DR	QUAIL SPRINGS CT	5	SCRIPPS MIRAMAR RANCH
TIMBERLAKE DR	SUNSET RIDGE DR	POYNTELL CR	5	SCRIPPS MIRAMAR RANCH
TIMBERLAKE DR	POYNTELL CR	SCRIPPS TL	5	SCRIPPS MIRAMAR RANCH
TONDINO CT	BEGIN	TONDINO RD	5	SCRIPPS MIRAMAR RANCH
TONDINO RD	WEATHERWOOD TR	TONDINO CT	5	SCRIPPS MIRAMAR RANCH
TONDINO RD	TONDINO CT	ACCRA LN	5	SCRIPPS MIRAMAR RANCH
TWINLEAF CT	TWINLEAF WY	END	5	MIRAMAR RANCH NORTH
TWINLEAF WY	TWINLEAF CT	MONTAUBON WY	5	MIRAMAR RANCH NORTH
TWINLEAF WY	BEGIN	TWINLEAF CT	5	MIRAMAR RANCH NORTH
WALDORF WY	MONTAUBON WY	SHERRARD WY	5	MIRAMAR RANCH NORTH
WALDORF WY	SHERRARD WY	GATEMOORE WY	5	MIRAMAR RANCH NORTH
WALNUTDALE ST	MEADOWDALE LN	PINECASTLE ST	5	SCRIPPS MIRAMAR RANCH
WALNUTDALE ST	PINECASTLE ST	FAIRBROOK RD	5	SCRIPPS MIRAMAR RANCH
WEATHERWOOD PL	BEGIN	WEATHERWOOD TR	5	SCRIPPS MIRAMAR RANCH
WEATHERWOOD TR	SCRIPPS TL	TONDINO RD	5	SCRIPPS MIRAMAR RANCH
WEATHERWOOD TR	ACCRA LN	ACCRA LN	5	SCRIPPS MIRAMAR RANCH
WEATHERWOOD TR	TONDINO RD	ACCRA LN	5	SCRIPPS MIRAMAR RANCH
WEATHERWOOD TR	ACCRA LN	WEATHERWOOD PL	5	SCRIPPS MIRAMAR RANCH
WEATHERWOOD TR	WEATHERWOOD PL	END	5	SCRIPPS MIRAMAR RANCH
AEGEAN CT	ALONDA WY	ANDASOL ST	6	MIRA MESA
AEGEAN CT	BEGIN	ALONDA WY	6	MIRA MESA
ALONDA CT	ANDASOL ST	ALONDA WY	6	MIRA MESA
ALONDA CT	ROCK CANYON DR	ANDASOL ST	6	MIRA MESA
ALONDA WY	ALONDA CT	AEGEAN CT	6	MIRA MESA
ANASTASIA ST	ARDMORE DR	PETIT ST	6	CLAIREMONT MESA
ANDASOL ST	ALONDA CT	ANGELENO RD	6	MIRA MESA
ANDASOL ST	ANGELENO RD	AEGEAN CT	6	MIRA MESA
ANDASOL ST	BIRDS VIEW CT	ALONDA CT	6	MIRA MESA
ANDASOL ST	BEGIN	BIRDS VIEW CT	6	MIRA MESA
BARON DR	FRIANT ST	HEBRIDES DR	6	MIRA MESA
BARON DR	PAGODA WY	FRIANT ST	6	MIRA MESA
BIDDLE CT	BEGIN	BROADLAWN ST	6	CLAIREMONT MESA
BIDDLE CT	BROADLAWN ST	BIDDLE ST	6	CLAIREMONT MESA
BIDDLE ST	BATISTA ST	BIDDLE CT	6	CLAIREMONT MESA
BIRDS VIEW CT	ANDASOL ST	END	6	MIRA MESA
BROADLAWN ST	BELOIT AV	BIDDLE CT	6	CLAIREMONT MESA
BROADLAWN ST	BATISTA ST	BELOIT AV	6	CLAIREMONT MESA
BROADLAWN ST	BIDDLE CT	PETIT ST	6	CLAIREMONT MESA
CANRIGHT WY	KAUFMAN WY	NORTHRUP DR	6	MIRA MESA
CICADA CT	DORMOUSE RD	END	6	RANCHO PENASQUITOS
DORMOUSE CT	DORMOUSE RD	END	6	RANCHO PENASQUITOS
DORMOUSE RD	DORMOUSE CT	CICADA CT	6	RANCHO PENASQUITOS



Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
DORMOUSE RD	ECLIPSE RD	DORMOUSE CT	6	RANCHO PENASQUITOS
DORMOUSE RD	CICADA CT	RUFUS CT	6	RANCHO PENASQUITOS
DORMOUSE RD	PARK VILLAGE RD	PIPIT PL	6	RANCHO PENASQUITOS
DORMOUSE RD	RUFUS CT	CAM DEL SUR	6	RANCHO PENASQUITOS
DORMOUSE RD	SALVIA WY	ECLIPSE RD	6	RANCHO PENASQUITOS
DORMOUSE RD	PIPIT PL	SALVIA WY	6	RANCHO PENASQUITOS
DORMOUSE RD	BEGIN	SALIX PL	6	RANCHO PENASQUITOS
DORMOUSE RD	SALIX PL	PARK VILLAGE RD	6	RANCHO PENASQUITOS
ECLIPSE PL	BEGIN	ECLIPSE RD	6	RANCHO PENASQUITOS
ECLIPSE RD	ECLIPSE PL	END	6	RANCHO PENASQUITOS
ECLIPSE RD	DORMOUSE RD	ECLIPSE PL	6	RANCHO PENASQUITOS
FRIANT ST	WESTONHILL DR	ISLEWORTH AV	6	MIRA MESA
FRIANT ST	BARON DR	WESTONHILL DR	6	MIRA MESA
GOLDFISH CT	BEGIN	GOLDFISH WY	6	RANCHO PENASQUITOS
GOLDFISH WY	SALVIA WY	GOLDFISH CT	6	RANCHO PENASQUITOS
GOLDFISH WY	ROAN WY	END	6	RANCHO PENASQUITOS
GOLDFISH WY	GOLDFISH CT	ROAN WY	6	RANCHO PENASQUITOS
HATTON ST	FORUM ST	BATISTA ST	6	CLAIREMONT MESA
HATTON ST	BATISTA ST	SALERNO ST	6	CLAIREMONT MESA
HATTON ST	BEGIN	SALIZAR ST	6	CLAIREMONT MESA
HATTON ST	SALERNO ST	AMOROSO ST	6	CLAIREMONT MESA
HATTON ST	SALIZAR ST	FORUM ST	6	CLAIREMONT MESA
ISLEWORTH AV	FRIANT ST	HEBRIDES DR	6	MIRA MESA
ISLEWORTH AV	HEBRIDES DR	FLANDERS DR	6	MIRA MESA
KATYDID CR	SALVIA WY	END	6	RANCHO PENASQUITOS
KAUFMAN WY	CANRIGHT WY	NORTHRUP DR	6	MIRA MESA
LICIA WY	SALIX PL	PARK VILLAGE RD	6	RANCHO PENASQUITOS
LICIA WY	PARK VILLAGE RD	PIPIT PL	6	RANCHO PENASQUITOS
NORTHRUP DR	CANRIGHT WY	PARKDALE AV	6	MIRA MESA
NORTHRUP DR	BEGIN	OSGOOD WY	6	MIRA MESA
NORTHRUP DR	NORTHRUP PT	CANRIGHT WY	6	MIRA MESA
NORTHRUP DR	KAUFMAN WY	NORTHRUP PT	6	MIRA MESA
NORTHRUP DR	OSGOOD WY	KAUFMAN WY	6	MIRA MESA
NORTHRUP PT	BEGIN	NORTHRUP DR	6	MIRA MESA
OSGOOD WY	PARKDALE AV	NORTHRUP DR	6	MIRA MESA
PAGODA WY	WESTONHILL DR	GOLD COAST PL	6	MIRA MESA
PAGODA WY	BELFAST CR	WESTONHILL DR	6	MIRA MESA
PAGODA WY	SAN RAMON DR	BARON DR	6	MIRA MESA
PAGODA WY	BARON DR	BELFAST CR	6	MIRA MESA
PIPIT CT	PIPIT PL	END	6	RANCHO PENASQUITOS
PIPIT PL	PIPIT CT	LICIA WY	6	RANCHO PENASQUITOS
PIPIT PL	SALVIA WY	PIPIT CT	6	RANCHO PENASQUITOS
PIPIT PL	LICIA WY	PIPIT WY	6	RANCHO PENASQUITOS
PIPIT PL	PIPIT WY	END	6	RANCHO PENASQUITOS
PIPIT PL	DORMOUSE RD	SALVIA WY	6	RANCHO PENASQUITOS
PIPIT WY	BEGIN	PIPIT PL	6	RANCHO PENASQUITOS
ROAN RD	ROAN WY	END	6	RANCHO PENASQUITOS
ROAN RD	SALVIA WY	ROAN WY	6	RANCHO PENASQUITOS
ROAN WY	GOLDFISH WY	ROAN RD	6	RANCHO PENASQUITOS

Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
RUFUS CT	BEGIN	DORMOUSE RD	6	RANCHO PENASQUITOS
SALIX CT	BEGIN	SALIX PL	6	RANCHO PENASQUITOS
SALIX PL	SALIX CT	LICIA WY	6	RANCHO PENASQUITOS
SALIX PL	LICIA WY	SALIX WY	6	RANCHO PENASQUITOS
SALIX PL	DORMOUSE RD	SALIX CT	6	RANCHO PENASQUITOS
SALIX WY	BEGIN	SALIX PL	6	RANCHO PENASQUITOS
SALIX WY	SALIX PL	END	6	RANCHO PENASQUITOS
SALVIA WY	ROAN RD	DORMOUSE RD	6	RANCHO PENASQUITOS
SALVIA WY	PIPIT PL	KATYDID CR	6	RANCHO PENASQUITOS
SALVIA WY	KATYDID CR	GOLDFISH WY	6	RANCHO PENASQUITOS
SALVIA WY	GOLDFISH WY	ROAN RD	6	RANCHO PENASQUITOS
SAN RAMON DR	FLANDERS DR	IVORY COAST DR	6	MIRA MESA
SAN RAMON DR	HEBRIDES DR	FLANDERS DR	6	MIRA MESA
SAN RAMON DR	IVORY COAST DR	REAGAN RD	6	MIRA MESA
ADMIRAL AV	BEGIN	EPAULETTE ST	7	SERRA MESA
ADMIRAL AV	AMULET ST	MELBOURNE DR	7	SERRA MESA
ADMIRAL AV	MELBOURNE DR	MISSION VILLAGE DR	7	SERRA MESA
ADMIRAL AV	EPAULETTE ST	AMULET ST	7	SERRA MESA
AMULET ST	SHAWN AV	OVERTON AV	7	SERRA MESA
AMULET ST	FORRESTER CT	FERMI AV	7	SERRA MESA
AMULET ST	FERMI AV	ADMIRAL AV	7	SERRA MESA
AMULET ST	FULLERTON AV	FORRESTER CT	7	SERRA MESA
AMULET ST	IRVINGTON AV	FULLERTON AV	7	SERRA MESA
AMULET ST	OVERTON AV	IRVINGTON AV	7	SERRA MESA
ANTIGUA BL	VILLARRICA WY	CAM PLAYA DE ORO	7	TIERRASANTA
ANTIGUA BL	CALLE MARISELDA	AVNDA PLAYA VERACRUZ	7	TIERRASANTA
ANTIGUA BL	CAM PLAYA ACAPULCO	VILLARRICA WY	7	TIERRASANTA
ANTIGUA BL	CAM PLAYA DE ORO	VIA VALARTA	7	TIERRASANTA
ANTIGUA BL	CAM PLAYA PORTOFINO	CAM PLAYA ACAPULCO	7	TIERRASANTA
ANTIGUA BL	AVNDA PLAYA VERACRUZ	CAM PLAYA PORTOFINO	7	TIERRASANTA
ANTIGUA BL	SANTO RD	CALLE MARISELDA	7	TIERRASANTA
BRONX PL	BEGIN	FULLERTON AV	7	SERRA MESA
CALLE MARISELDA	ANTIGUA BL	END	7	TIERRASANTA
CAM PLAYA ACAPULCO	CTE PLAYA MAZATLAN	ANTIGUA BL	7	TIERRASANTA
CAM PLAYA ACAPULCO	CAM PLAYA MALAGA	CTE PLAYA MAZATLAN	7	TIERRASANTA
CAM PLAYA AZUL	CAM PLAYA CARMEL	CTE PLAYA MERIDA	7	TIERRASANTA
CAM PLAYA CARMEL	VILLARRICA WY	CAM PLAYA AZUL	7	TIERRASANTA
CAM PLAYA CARMEL	CAM PLAYA AZUL	END	7	TIERRASANTA
CAM PLAYA DE ORO	CTE PLAYA MADERA	CTE PLAYA AZTECA	7	TIERRASANTA
CAM PLAYA DE ORO	CTE PLAYA CORONA	CTE PLAYA MADERA	7	TIERRASANTA
CAM PLAYA DE ORO	CAM PLAYA NORTE	CTE PLAYA CORONA	7	TIERRASANTA
CAM PLAYA DE ORO	CTE PLAYA AZTECA	ANTIGUA BL	7	TIERRASANTA
CAM PLAYA MALAGA	AVNDA PLAYA VERACRUZ	CTE PLAYA TOLUCA	7	TIERRASANTA
CAM PLAYA MALAGA	CAM PLAYA ACAPULCO	CTE PLAYA TAMPICO	7	TIERRASANTA
CAM PLAYA MALAGA	CTE PLAYA SOLANA	CAM PLAYA ACAPULCO	7	TIERRASANTA
CAM PLAYA MALAGA	CTE PLAYA TOLUCA	CTE PLAYA SOLANA	7	TIERRASANTA
CAM PLAYA MALAGA	CTE PLAYA DE CASTILA	AVNDA PLAYA VERACRUZ	7	TIERRASANTA
CAM PLAYA MALAGA	CAM PLAYA DE ORO	CTE PLAYA DE CASTILA	7	TIERRASANTA
CAM PLAYA MALAGA	AVNDA PLAYA VERACRUZ	END	7	TIERRASANTA

Street Name	Cross Street 1	Cross Street 2	Council District	Community Planning Area
CAM PLAYA MALAGA	CTE PLAYA TAMPICO	CAM PLAYA DE ORO	7	TIERRASANTA
CAM PLAYA NORTE	CAM PLAYA DE ORO	VIA VALARTA	7	TIERRASANTA
CAM PLAYA PORTOFINO	CTE PLAYA MAJORCA	CTE PLAYA BARCELONA	7	TIERRASANTA
CAM PLAYA PORTOFINO	ANTIGUA BL	CTE PLAYA MAJORCA	7	TIERRASANTA
CTE PLAYA AZTECA	CAM PLAYA DE ORO	END	7	TIERRASANTA
CTE PLAYA BARCELONA	VILLARRICA WY	CAM PLAYA PORTOFINO	7	TIERRASANTA
CTE PLAYA BARCELONA	CAM PLAYA PORTOFINO	END	7	TIERRASANTA
CTE PLAYA DE CASTILA	BEGIN	CAM PLAYA MALAGA	7	TIERRASANTA
CTE PLAYA MADERA	CAM PLAYA DE ORO	END	7	TIERRASANTA
CTE PLAYA MAJORCA	BEGIN	CAM PLAYA PORTOFINO	7	TIERRASANTA
CTE PLAYA MAZATLAN	CAM PLAYA ACAPULCO	END	7	TIERRASANTA
CTE PLAYA MERIDA	CAM PLAYA AZUL	END	7	TIERRASANTA
CTE PLAYA MERIDA	BEGIN	CAM PLAYA AZUL	7	TIERRASANTA
CTE PLAYA TAMPICO	CAM PLAYA MALAGA	END	7	TIERRASANTA
EPAULETTE ST	HUNTINGTON AV	ADMIRAL AV	7	SERRA MESA
EPAULETTE ST	IRVINGTON AV	HUNTINGTON AV	7	SERRA MESA
FERMI AV	MARATHON DR	MARTINDALE CT	7	SERRA MESA
FERMI AV	MISSION VILLAGE DR	MARATHON DR	7	SERRA MESA
FERMI AV	AMULET ST	FORRESTER CT	7	SERRA MESA
FERMI AV	MARTINDALE CT	MONARCH ST	7	SERRA MESA
FERMI AV	MELBOURNE DR	MISSION VILLAGE DR	7	SERRA MESA
FERMI AV	FORRESTER CT	MELBOURNE DR	7	SERRA MESA
FORRESTER CT	AMULET ST	END	7	SERRA MESA
FORRESTER CT	BEGIN	FERMI AV	7	SERRA MESA
FORRESTER CT	BEGIN	END	7	SERRA MESA
FULLERTON AV	MELBOURNE DR	MISSION VILLAGE DR	7	SERRA MESA
FULLERTON AV	BRONX PL	MELBOURNE DR	7	SERRA MESA
FULLERTON AV	AMULET ST	BRONX PL	7	SERRA MESA
HUNTINGTON AV	WILBEE CT	EPAULETTE ST	7	SERRA MESA
IRVINGTON AV	EPAULETTE ST	AMULET ST	7	SERRA MESA
IRVINGTON AV	AMULET ST	MELBOURNE DR	7	SERRA MESA
IRVINGTON AV	WILBEE CT	EPAULETTE ST	7	SERRA MESA
MARATHON DR	FULLERTON AV	FERMI AV	7	SERRA MESA
MARTINDALE CT	FULLERTON AV	FERMI AV	7	SERRA MESA
MELBOURNE DR	FULLERTON AV	FERMI AV	7	SERRA MESA
MELBOURNE DR	FERMI AV	ADMIRAL AV	7	SERRA MESA
OVERTON AV	WILBEE CT	AMULET ST	7	SERRA MESA
VIA VALARTA	VIA DOMINIQUE	COLLEGIO DR	7	TIERRASANTA
VIA VALARTA	CAM PLAYA NORTE	AVNDA PLAYA CANCUN	7	TIERRASANTA
VIA VALARTA	CLAIREMONT MESA BL	VIA DOMINIQUE	7	TIERRASANTA
VIA VALARTA	AVNDA PLAYA CANCUN	ANTIGUA BL	7	TIERRASANTA
VIA VALARTA	VIA PLAYA DE CORTES	CAM PLAYA NORTE	7	TIERRASANTA
VIA VALARTA	COLLEGIO DR	VIA PLAYA DE CORTES	7	TIERRASANTA
VIA VALARTA	ANTIGUA BL	CAM PLAYA CANCUN	7	TIERRASANTA
VILLARRICA WY	CTE PLAYA BARCELONA	PORTOBELO DR	7	TIERRASANTA
VILLARRICA WY	ANTIGUA BL	CAM PLAYA CARMEL	7	TIERRASANTA
VILLARRICA WY	CAM PLAYA CARMEL	CTE PLAYA BARCELONA	7	TIERRASANTA
WILBEE CT	OVERTON AV	IRVINGTON AV	7	SERRA MESA
WILBEE CT	IRVINGTON AV	HUNTINGTON AV	7	SERRA MESA

**APPENDIX B**  
**FIRE HYDRANT METER PROGRAM**

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 1 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

1. **PURPOSE**

- 1.1 To establish a Departmental policy and procedure for issuance, proper usage and charges for fire hydrant meters.

2. **AUTHORITY**

- 2.1 All authorities and references shall be current versions and revisions.
- 2.2 San Diego Municipal Code (NC) Chapter VI, Article 7, Sections 67.14 and 67.15
- 2.3 Code of Federal Regulations, Safe Drinking Water Act of 1986
- 2.4 California Code of Regulations, Titles 17 and 22
- 2.5 California State Penal Code, Section 498B.0
- 2.6 State of California Water Code, Section 110, 500-6, and 520-23
- 2.7 Water Department Director

**Reference**

- 2.8 State of California Guidance Manual for Cross Connection Programs
- 2.9 American Water Works Association Manual M-14, Recommended Practice for Backflow Prevention
- 2.10 American Water Works Association Standards for Water Meters
- 2.11 U.S.C. Foundation for Cross Connection Control and Hydraulic Research Manual

3. **DEFINITIONS**

- 3.1 **Fire Hydrant Meter:** A portable water meter which is connected to a fire hydrant for the purpose of temporary use. (These meters are sometimes referred to as Construction Meters.)

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 2 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

- 3.2 **Temporary Water Use:** Water provided to the customer for no longer than twelve (12) months.
- 3.3 **Backflow Preventor:** A Reduced Pressure Principal Assembly connected to the outlet side of a Fire Hydrant Meter.

4. **POLICY**

- 4.1 The Water Department shall collect a deposit from every customer requiring a fire hydrant meter and appurtenances prior to providing the meter and appurtenances (see Section 7.1 regarding the Fees and Deposit Schedule). The deposit is refundable upon the termination of use and return of equipment and appurtenances in good working condition.
- 4.2 Fire hydrant meters will have a 2 ½" swivel connection between the meter and fire hydrant. The meter shall not be connected to the 4" port on the hydrant. All Fire Hydrant Meters issued shall have a Reduced Pressure Principle Assembly (RP) as part of the installation. Spanner wrenches are the only tool allowed to turn on water at the fire hydrant.
- 4.3 The use of private hydrant meters on City hydrants is prohibited, with exceptions as noted below. All private fire hydrant meters are to be phased out of the City of San Diego. All customers who wish to continue to use their own fire hydrant meters must adhere to the following conditions:
  - a. Meters shall meet all City specifications and American Water Works Association (AWWA) standards.
  - b. Customers currently using private fire hydrant meters in the City of San Diego water system will be allowed to continue using the meter under the following conditions:
    - 1. The customer must submit a current certificate of accuracy and calibration results for private meters and private backflows annually to the City of San Diego, Water Department, Meter Shop.

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 3 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

2. The meter must be properly identifiable with a clearly labeled serial number on the body of the fire hydrant meter. The serial number shall be plainly stamped on the register lid and the main casing. Serial numbers shall be visible from the top of the meter casing and the numbers shall be stamped on the top of the inlet casing flange.
3. All meters shall be locked to the fire hydrant by the Water Department, Meter Section (see Section 4.7).
4. All meters shall be read by the Water Department, Meter Section (see Section 4.7).
5. All meters shall be relocated by the Water Department, Meter Section (see Section 4.7).
6. These meters shall be tested on the anniversary of the original test date and proof of testing will be submitted to the Water Department, Meter Shop, on a yearly basis. If not tested, the meter will not be allowed for use in the City of San Diego.
7. All private fire hydrant meters shall have backflow devices attached when installed.
8. The customer must maintain and repair their own private meters and private backflows.
9. The customer must provide current test and calibration results to the Water Department, Meter Shop after any repairs.
10. When private meters are damaged beyond repair, these private meters will be replaced by City owned fire hydrant meters.

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 4 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

11. When a private meter malfunctions, the customer will be notified and the meter will be removed by the City and returned to the customer for repairs. Testing and calibration results shall be given to the City prior to any re-installation.
  12. The register shall be hermetically sealed straight reading and shall be readable from the inlet side. Registration shall be in hundred cubic feet.
  13. The outlet shall have a 2 ½ “National Standards Tested (NST) fire hydrant male coupling.
  14. Private fire hydrant meters shall not be transferable from one contracting company to another (i.e. if a company goes out of business or is bought out by another company).
- 4.4 All fire hydrant meters and appurtenances shall be installed, relocated and removed by the City of San Diego, Water Department. All City owned fire hydrant meters and appurtenances shall be maintained by the City of San Diego, Water Department, Meter Services.
- 4.5 If any fire hydrant meter is used in violation of this Department Instruction, the violation will be reported to the Code Compliance Section for investigation and appropriate action. Any customer using a fire hydrant meter in violation of the requirements set forth above is subject to fines or penalties pursuant to the Municipal Code, Section 67.15 and Section 67.37.
- 4.6 Conditions and Processes for Issuance of a Fire Hydrant Meter**
- Process for Issuance
- a. Fire hydrant meters shall only be used for the following purposes:
    1. Temporary irrigation purposes not to exceed one year.



<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 5 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

2. Construction and maintenance related activities (see Tab 2).
  - b. No customer inside or outside the boundaries of the City of San Diego Water Department shall resell any portion of the water delivered through a fire hydrant by the City of San Diego Water Department.
  - c. The City of San Diego allows for the issuance of a temporary fire hydrant meter for a period not to exceed 12 months (365 days). An extension can only be granted in writing from the Water Department Director for up to 90 additional days. A written request for an extension by the consumer must be submitted at least 30 days prior to the 12 month period ending. No extension shall be granted to any customer with a delinquent account with the Water Department. No further extensions shall be granted.
  - d. Any customer requesting the issuance of a fire hydrant meter shall file an application with the Meter Section. The customer must complete a "Fire Hydrant Meter Application" (Tab 1) which includes the name of the company, the party responsible for payment, Social Security number and/or California ID, requested location of the meter (a detailed map signifying an exact location), local contact person, local phone number, a contractor's license (or a business license), description of specific water use, duration of use at the site and full name and address of the person responsible for payment.
  - e. At the time of the application the customer will pay their fees according to the schedule set forth in the Rate Book of Fees and Charges, located in the City Clerk's Office. All fees must be paid by check, money order or cashiers check, made payable to the City Treasurer. Cash will not be accepted.
  - f. No fire hydrant meters shall be furnished or relocated for any customer with a delinquent account with the Water Department.
  - g. After the fees have been paid and an account has been created, the

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 6 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

meter shall be installed within 48 hours (by the second business day). For an additional fee, at overtime rates, meters can be installed within 24 hours (within one business day).

#### 4.7 Relocation of Existing Fire Hydrant Meters

- a. The customer shall call the Fire Hydrant Meter Hotline (herein referred to as “Hotline”), a minimum of 24 hours in advance, to request the relocation of a meter. A fee will be charged to the existing account, which must be current before a work order is generated for the meter’s relocation.
- b. The customer will supply in writing the address where the meter is to be relocated (map page, cross street, etc). The customer must update the original Fire Hydrant Meter Application with any changes as it applies to the new location.
- c. Fire hydrant meters shall be read on a monthly basis. While fire hydrant meters and backflow devices are in service, commodity, base fee and damage charges, if applicable, will be billed to the customer on a monthly basis. If the account becomes delinquent, the meter will be removed.

#### 4.8 Disconnection of Fire Hydrant Meter

- a. After ten (10) months a “Notice of Discontinuation of Service” (Tab 3) will be issued to the site and the address of record to notify the customer of the date of discontinuance of service. An extension can only be granted in writing from the Water Department Director for up to 90 additional days (as stated in Section 4.6C) and a copy of the extension shall be forwarded to the Meter Shop Supervisor. If an extension has not been approved, the meter will be removed after twelve (12) months of use.
- b. Upon completion of the project the customer will notify the Meter Services office via the Hotline to request the removal of the fire hydrant meter and appurtenances. A work order will be generated

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 7 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

for removal of the meter.

- c. Meter Section staff will remove the meter and backflow prevention assembly and return it to the Meter Shop. Once returned to the Meter Shop the meter and backflow will be tested for accuracy and functionality.
- d. Meter Section Staff will contact and notify Customer Services of the final read and any charges resulting from damages to the meter and backflow or its appurtenance. These charges will be added on the customer's final bill and will be sent to the address of record. Any customer who has an outstanding balance will not receive additional meters.
- e. Outstanding balances due may be deducted from deposits and any balances refunded to the customer. Any outstanding balances will be turned over to the City Treasurer for collection. Outstanding balances may also be transferred to any other existing accounts.

5. **EXCEPTIONS**

- 5.1 Any request for exceptions to this policy shall be presented, in writing, to the Customer Support Deputy Director, or his/her designee for consideration.

6. **MOBILE METER**

- 6.1 Mobile meters will be allowed on a case by case basis. All mobile meters will be protected by an approved backflow assembly and the minimum requirement will be a Reduced Pressure Principal Assembly. The two types of Mobile Meters are vehicle mounted and floating meters. Each style of meters has separate guidelines that shall be followed for the customer to retain service and are described below:

- a) **Vehicle Mounted Meters:** Customer applies for and receives a City owned Fire Hydrant Meter from the Meter Shop. The customer mounts the meter on the vehicle and brings it to the Meter Shop for

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 8 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

inspection. After installation is approved by the Meter Shop the vehicle and meter shall be brought to the Meter Shop on a monthly basis for meter reading and on a quarterly basis for testing of the backflow assembly. Meters mounted at the owner's expense shall have the one year contract expiration waived and shall have meter or backflow changed if either fails.

b) **Floating Meters:** Floating Meters are meters that are not mounted to a vehicle. **(Note: All floating meters shall have an approved backflow assembly attached.)** The customer shall submit an application and a letter explaining the need for a floating meter to the Meter Shop. The Fire Hydrant Meter Administrator, after a thorough review of the needs of the customer, (i.e. number of jobsites per day, City contract work, lack of mounting area on work vehicle, etc.), may issue a floating meter. At the time of issue, it will be necessary for the customer to complete and sign the "Floating Fire Hydrant Meter Agreement" which states the following:

- 1) The meter will be brought to the Meter Shop at 2797 Caminito Chollas, San Diego on the third week of each month for the monthly read by Meter Shop personnel.
- 2) Every other month the meter will be read and the backflow will be tested. This date will be determined by the start date of the agreement.

If any of the conditions stated above are not met the Meter Shop has the right to cancel the contract for floating meter use and close the account associated with the meter. The Meter Shop will also exercise the right to refuse the issuance of another floating meter to the company in question.

Any Fire Hydrant Meter using reclaimed water shall not be allowed use again with any potable water supply. The customer shall incur the cost of replacing the meter and backflow device in this instance.

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 9 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

7. **FEE AND DEPOSIT SCHEDULES**

7.1 **Fees and Deposit Schedules:** The fees and deposits, as listed in the Rate Book of Fees and Charges, on file with the Office of the City Clerk, are based on actual reimbursement of costs of services performed, equipment and materials. These deposits and fees will be amended, as needed, based on actual costs. Deposits, will be refunded at the end of the use of the fire hydrant meter, upon return of equipment in good working condition and all outstanding balances on account are paid. Deposits can also be used to cover outstanding balances.

All fees for equipment, installation, testing, relocation and other costs related to this program are subject to change without prior notification. The Mayor and Council will be notified of any future changes.

8. **UNAUTHORIZED USE OF WATER FROM A HYDRANT**

8.1 Use of water from any fire hydrant without a properly issued and installed fire hydrant meter is theft of City property. Customers who use water for unauthorized purposes or without a City of San Diego issued meter will be prosecuted.

8.2 If any unauthorized connection, disconnection or relocation of a fire hydrant meter, or other connection device is made by anyone other than authorized Water Department personnel, the person making the connection will be prosecuted for a violation of San Diego Municipal Code, Section 67.15. In the case of a second offense, the customer's fire hydrant meter shall be confiscated and/or the deposit will be forfeited.

8.3 Unauthorized water use shall be billed to the responsible party. Water use charges shall be based on meter readings, or estimates when meter readings are not available.

8.4 In case of unauthorized water use, the customer shall be billed for all applicable charges as if proper authorization for the water use had been obtained, including but not limited to bi-monthly service charges, installation charges and removal charges.

<b>CITY OF SAN DIEGO CALIFORNIA DEPARTMENT INSTRUCTIONS</b>	<b>NUMBER DI 55.27</b>	<b>DEPARTMENT Water Department</b>
<b>SUBJECT  FIRE HYDRANT METER PROGRAM (FORMERLY: CONSTRUCTION METER PROGRAM)</b>	<b>PAGE 10 OF 10</b>	<b>EFFECTIVE DATE  October 15, 2002</b>
	<b>SUPERSEDES DI 55.27</b>	<b>DATED April 21, 2000</b>

- 8.5 If damage occurs to Water Department property (i.e. fire hydrant meter, backflow, various appurtenances), the cost of repairs or replacements will be charged to the customer of record (applicant).

**Water Department Director**

- Tabs: 1. Fire Hydrant Meter Application  
2. Construction & Maintenance Related Activities With No Return To Sewer  
3. Notice of Discontinuation of Service

#### APPENDIX

**Administering Division:** Customer Support Division

**Subject Index:** Construction Meters  
Fire Hydrant  
Fire Hydrant Meter Program  
Meters, Floating or Vehicle Mounted  
Mobile Meter  
Program, Fire Hydrant Meter

**Distribution:** DI Manual Holders



# Application for Fire Hydrant Meter (EXHIBIT A)

(For Office Use Only)

NS REQ	FAC#
DATE	BY

METER SHOP (619) 527-7449

## Meter Information

Application Date	Requested Install Date:
------------------	-------------------------

Fire Hydrant Location: (Attach Detailed Map//Thomas Bros. Map Location or Construction drawing.) <u>Zip:</u>	T.B.	G.B. (CITY USE)
Specific Use of Water:		
Any Return to Sewer or Storm Drain, if so, explain:		
Estimated Duration of Meter Use: <input type="text"/>	<input type="checkbox"/>	Check Box if Reclaimed Water

## Company Information

Company Name:			
Mailing Address:			
City:	State:	Zip:	Phone: ( )
*Business license#		*Contractor license#	
A Copy of the Contractor's license OR Business License is required at the time of meter issuance.			
Name and Title of Billing Agent: <small>(PERSON IN ACCOUNTS PAYABLE)</small>			Phone: ( )
Site Contact Name and Title:			Phone: ( )
Responsible Party Name:			Title:
Cal ID#			Phone: ( )
Signature:		Date:	
<small>Guarantees Payment of all Charges Resulting from the use of this Meter. Insures that employees of this Organization understand the proper use of Fire Hydrant Meter</small>			

<b>Fire Hydrant Meter Removal Request</b>	Requested Removal Date:
Provide Current Meter Location if Different from Above:	
Signature:	Title:      Date:
Phone: ( )	Pager: ( )

<input type="checkbox"/> City Meter	<input type="checkbox"/> Private Meter	
Contract Acct #:	Deposit Amount: <b>\$ 936.00</b>	Fees Amount: <b>\$ 62.00</b>
Meter Serial #	Meter Size: <b>05</b>	Meter Make and Style: <b>6-7</b>
Backflow #	Backflow Size:	Backflow Make and Style:
Name:	Signature:	Date:

**WATER USES WITHOUT ANTICIPATED CHARGES FOR RETURN TO SEWER**

Auto Detailing  
Backfilling  
Combination Cleaners (Vactors)  
Compaction  
Concrete Cutters  
Construction Trailers  
Cross Connection Testing  
Dust Control  
Flushing Water Mains  
Hydro Blasting  
Hydro Seeing  
Irrigation (for establishing irrigation only; not continuing irrigation)  
Mixing Concrete  
Mobile Car Washing  
Special Events  
Street Sweeping  
Water Tanks  
Water Trucks  
Window Washing

**Note:**

1. If there is any return to sewer or storm drain, then sewer and/or storm drain fees will be charges.



Date

Name of Responsible Party  
Company Name and Address  
Account Number: \_\_\_\_\_

Subject:           Discontinuation of Fire Hydrant Meter Service

Dear Water Department Customer:

The authorization for use of Fire Hydrant Meter # \_\_\_\_\_, located at *(Meter Location Address)* ends in 60 days and will be removed on or after *(Date Authorization Expires)*. Extension requests for an additional 90 days must be submitted in writing for consideration 30 days prior to the discontinuation date. If you require an extension, please contact the Water Department, or mail your request for an extension to:

City of San Diego  
Water Department  
Attention: Meter Services  
2797 Caminito Chollas  
San Diego, CA 92105-5097

Should you have any questions regarding this matter, please call the Fire Hydrant Hotline at (619) \_\_\_\_\_ - \_\_\_\_\_.

Sincerely,

Water Department

## **APPENDIX C**

### **MATERIALS TYPICALLY ACCEPTED BY CERTIFICATE OF COMPLIANCE**

## **MATERIALS TYPICALLY ACCEPTED BY CERTIFICATE OF COMPLIANCE**

1. Soil amendment
2. Fiber mulch
3. PVC or PE pipe up to 16 inch diameter
4. Stabilizing emulsion
5. Lime
6. Preformed elastomeric joint seal
7. Plain and fabric reinforced elastomeric bearing pads
8. Steel reinforced elastomeric bearing pads
9. Waterstops (Special Condition)
10. Epoxy coated bar reinforcement
11. Plain and reinforcing steel
12. Structural steel
13. Structural timber and lumber
14. Treated timber and lumber
15. Lumber and timber
16. Aluminum pipe and aluminum pipe arch
17. Corrugated steel pipe and corrugated steel pipe arch
18. Structural metal plate pipe arches and pipe arches
19. Perforated steel pipe
20. Aluminum underdrain pipe
21. Aluminum or steel entrance tapers, pipe downdrains, reducers, coupling bands and slip joints
22. Metal target plates
23. Paint (traffic striping)
24. Conductors
25. Painting of electrical equipment
26. Electrical components
27. Engineering fabric
28. Portland Cement
29. PCC admixtures
30. Minor concrete, asphalt
31. Asphalt (oil)
32. Liquid asphalt emulsion
33. Epoxy

**APPENDIX D**

**SAMPLE CITY INVOICE WITH CASH FLOW FORECAST**



WBS #:	B18108
Date Submitted:	10/10/2018
NTP Date:	3/23/2018
Final Statement of WD Date:	5/23/2020
Contract #:	K-XX-XXXX-XXX-X
Contract Amount:	\$5,617,000

## Construction Cash Flow Forecast

"Sewer and Water Group Job 965 (W)"

Year	January	February	March	April	May	June	July	August	September	October	November	December
2018				15,000	25,000	52,000	52,000	100,000	10,000	100,000	100,000	100,000
2019	10,000	10,000	85,000	58,000	100,000	100,000	100,000	100,000	100,000	100,000	1,000,000	1,000,000
2020	100,000	100,000	100,000	1,000,000	1,000,000							
2021												
2022												
2023												
2024												
2025												

SAMPLE REFERENCE

## **APPENDIX E**

### **SAMPLE CONTRACTOR'S DAILY QUALITY CONTROL INSPECTION REPORT**

**Appendix E**

City of San Diego  
Asphalt Concrete Overlay

**Contractor's Daily Quality Control Inspection Report**

Project Title: \_\_\_\_\_ Date: \_\_\_\_\_

Locations: 1. \_\_\_\_\_  
2. \_\_\_\_\_  
3. \_\_\_\_\_

Asphalt Mix Specification: Attached Supplier: \_\_\_\_\_

Dig out Locations: 1. \_\_\_\_\_  
2. \_\_\_\_\_  
3. \_\_\_\_\_

Tack Coat Application Rate @ Locations:  
1. \_\_\_\_\_  
2. \_\_\_\_\_  
3. \_\_\_\_\_

Asphalt Temperature at Placement @ Locations:  
1. \_\_\_\_\_  
2. \_\_\_\_\_  
3. \_\_\_\_\_

Asphalt Depth @Locations:  
1. \_\_\_\_\_  
2. \_\_\_\_\_  
3. \_\_\_\_\_

Compaction Test Result @Locations:  
1. \_\_\_\_\_  
2. \_\_\_\_\_  
3. \_\_\_\_\_



Location and nature of defects:

1. \_\_\_\_\_
2. \_\_\_\_\_
3. \_\_\_\_\_

Remedial and Corrective Actions taken or proposed for Engineer's approval:

1. \_\_\_\_\_
2. \_\_\_\_\_
3. \_\_\_\_\_

Date's City Laboratory representative was present:

1. \_\_\_\_\_
2. \_\_\_\_\_
3. \_\_\_\_\_

Verified the following:

1. Proper Storage of Materials & Equipment
2. Proper Operation of Equipment
3. Adherence to Plans and Specs
4. Review of QC Tests
5. Safety Inspection

Initials:

- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_
- \_\_\_\_\_

Deviations from QCP \_\_\_\_\_ (see attached)

Quality Control Plan Administrator's Signature:

Date Signed:

\_\_\_\_\_

\_\_\_\_\_

City of San Diego  
Rubber Polymer Modified Slurry  
**Contractor's Daily Quality Control Inspection Report**

Project Title: \_\_\_\_\_ Date: \_\_\_\_\_

Ambient Temperature (Start of Work): \_\_\_\_\_ Time: \_\_\_\_\_

Environmental Considerations: \_\_\_\_\_

Locations (Address Range/Cross Streets):

1. \_\_\_\_\_
2. \_\_\_\_\_
3. \_\_\_\_\_

Approved Mix Design: \_\_\_\_\_

Material Suppliers: \_\_\_\_\_

RPMS Type(s): \_\_\_\_\_

Slurry Machine #'s: \_\_\_\_\_

Estimated Cure Time (Break) of Slurry: \_\_\_\_\_

Pre-Mix (Per 100 Counts)

Gate Setting/Emulsion %: \_\_\_\_\_

Aggregate Weight: \_\_\_\_\_

Cement % (by weight of aggregate): \_\_\_\_\_

Crumb Rubber % (by volume of cement): \_\_\_\_\_

Machine Inspection

Leaks: \_\_\_\_\_

Sprayers: \_\_\_\_\_

Emulsion Filter: \_\_\_\_\_

Carbon Black: \_\_\_\_\_

Spreader Box Inspection

Cleanliness: \_\_\_\_\_

Augers: \_\_\_\_\_

Rubbers: \_\_\_\_\_

Fabric: \_\_\_\_\_

Runners: \_\_\_\_\_

City of San Diego  
Rubber Polymer Modified Slurry  
**Contractor's Daily Quality Control Inspection Report**

Project Conditions

Crack Fill: \_\_\_\_\_

Asphalt Deficiencies: \_\_\_\_\_

Cleanliness: \_\_\_\_\_

Impediments/Other: \_\_\_\_\_

Communication to Client/ Resident Engineer

Crack Fill: \_\_\_\_\_

Asphalt Deficiencies: \_\_\_\_\_

Cleanliness: \_\_\_\_\_

Impediments/Other: \_\_\_\_\_

Test Lab

Tech: \_\_\_\_\_ Time on Site: \_\_\_\_\_

Notes

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

QCP Administrator Signature:

Date Signed:

\_\_\_\_\_

\_\_\_\_\_

**APPENDIX F**  
**SAMPLE OF PUBLIC NOTICE**



CONSTRUCTION NOTICE

PROJECT TITLE

Work on your street will begin within one week to replace the existing water mains servicing your community.

The work will consist of:

- Saw-cutting and trench work on Ingulf Street from Morena Boulevard to Galveston Street to install new water mains, water laterals and fire hydrants.
• Streets where trenching takes place will be resurfaced and curb ramps will be upgraded to facilitate access for persons with disabilities where required.
• This work is anticipated to be complete in your community by December 2016.

How your neighborhood may be impacted:

- Water service to some properties during construction will be provided by a two-inch highline pipe that will run along the curb. To report a highline leak call 619-515-3525.
• Temporary water service disruptions are planned. If planned disruptions impact your property, you will receive advance notice.
• Parking restrictions will exist because of the presence of construction equipment and materials.
• "No Parking" signs will be displayed 72 hours in advance of the work.
• Cars parked in violation of signs will be TOWED.

Hours and Days of Operation:

Monday through Friday X:XX AM to X:XX PM.

City of San Diego Contractor:

Company Name, XXX-XXX-XXXX



CONSTRUCTION NOTICE

PROJECT TITLE

Work on your street will begin within one week to replace the existing water mains servicing your community.

The work will consist of:

- Saw-cutting and trench work on Ingulf Street from Morena Boulevard to Galveston Street to install new water mains, water laterals and fire hydrants.
• Streets where trenching takes place will be resurfaced and curb ramps will be upgraded to facilitate access for persons with disabilities where required.
• This work is anticipated to be complete in your community by December 2016.

How your neighborhood may be impacted:

- Water service to some properties during construction will be provided by a two-inch highline pipe that will run along the curb. To report a highline leak call 619-515-3525.
• Temporary water service disruptions are planned. If planned disruptions impact your property, you will receive advance notice.
• Parking restrictions will exist because of the presence of construction equipment and materials.
• "No Parking" signs will be displayed 72 hours in advance of the work.
• Cars parked in violation of signs will be TOWED.

Hours and Days of Operation:

Monday through Friday X:XX AM to X:XX PM.

City of San Diego Contractor:

Company Name, XXX-XXX-XXXX

To contact the City of San Diego: SD Public Works 619-533-4207 | engineering@sandiego.gov | sandiego.gov/CIP

To contact the City of San Diego: SD Public Works 619-533-4207 | engineering@sandiego.gov | sandiego.gov/CIP

**APPENDIX G**  
**LIST OF PROPOSED WORK**

Slurry Seal Group 2023 - Scope of Work  
 IO: 21004779

Work Order Number	Segment ID	Street Name	Cross Street 1	Cross Street 2	Council District	TB Map Page	Trash Day	Community Planning Area	Functional Classification	Survey Length (FT)	Survey Width (FT)	Survey Area (SF)	Crack Seal (LBS)	Base Repair (TONS)	Mill / Pave (TONS)	Hump Removal (LF)	Inlet Marker (EA)	Inlet Protection (EA)	Traffic Loops (EA)	Traffic Loops Location	Survey Monument	Comments
S2023	SS-001660	ACCRA LN	TONDINO RD	WEATHERWOOD TR	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	560	27	15120	233	0	2.43							TYPE I/II.
S2023	SS-001811	ADMIRAL AV	BEGIN	EPAULETTE ST	7	1249-E6	Friday	SERRA MESA	Residential	194	40	7760	119		2.11							TYPE I/II.
S2023	SS-001809	ADMIRAL AV	AMULET ST	MELBOURNE DR	7	1249-E5	Friday	SERRA MESA	Residential	1175	37	43475	669					1	2			TYPE I/II.
S2023	SS-001808	ADMIRAL AV	MELBOURNE DR	MISSION VILLAGE DR	7	1249-E5	Friday	SERRA MESA	Residential	345	37	12765	196									TYPE I/II.
S2023	SS-001810	ADMIRAL AV	EPAULETTE ST	AMULET ST	7	1249-E6	Friday	SERRA MESA	Residential	380	33	12540	193									TYPE I/II.
S2023	SS-001833	AEGEAN CT	ALONDA WY	ANDASOL ST	6	1209-A2	Tuesday	MIRA MESA	Residential	230	34	7820	120		7.71							TYPE I/II.
S2023	SS-001832	AEGEAN CT	BEGIN	ALONDA WY	6	1209-A2	Tuesday	MIRA MESA	Residential	553	34	18802	289		8.79							TYPE I/II.
S2023	SS-002186	ALONDA CT	ANDASOL ST	ALONDA WY	6	1209-A2	Tuesday	MIRA MESA	Residential	207	34	7038	108		3.7							TYPE I/II.
S2023	SS-002187	ALONDA CT	ROCK CANYON DR	ANDASOL ST	6	1209-A2	Tuesday	MIRA MESA	Residential	226	34	7684	118		3.7							TYPE I/II.
S2023	SS-002189	ALONDA WY	ALONDA CT	AEGEAN CT	6	1209-A2	Tuesday	MIRA MESA	Residential	658	34	22372	344		14.69							TYPE I/II.
S2023	SS-002406	AMULET ST	SHAWN AV	OVERTON AV	7	1249-E6	Friday	SERRA MESA	Residential	225	37	8325										TYPE I/II. NO CRACK SEAL.
S2023	SS-002403	AMULET ST	FORRESTER CT	FERMI AV	7	1249-E6	Friday	SERRA MESA	Residential	255	37	9435	145									TYPE I/II.
S2023	SS-002402	AMULET ST	FERMI AV	ADMIRAL AV	7	1249-E5	Friday	SERRA MESA	Residential	225	37	8325										TYPE I/II. NO CRACK SEAL.
S2023	SS-002404	AMULET ST	FULLERTON AV	FORRESTER CT	7	1249-E6	Friday	SERRA MESA	Residential	218	37	8066	124									TYPE I/II.
S2023	SS-002407	AMULET ST	IRVINGTON AV	FULLERTON AV	7	1249-E6	Friday	SERRA MESA	Residential	815	37	30155	464									TYPE I/II.
S2023	SS-002405	AMULET ST	OVERTON AV	IRVINGTON AV	7	1249-E6	Friday	SERRA MESA	Residential	266	37	9842										TYPE I/II. RAISE 1 WATER VALVE. NO CRACK SEAL.
S2023	SS-002420	ANCONA LN	BEGIN	SUNSET RIDGE DR	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	665	31	20615	317		74.76							TYPE I/II.
S2023	SS-002429	ANDASOL ST	ALONDA CT	ANGELENO RD	6	1209-A2	Tuesday	MIRA MESA	Residential	670	37	24790	381		17.03						1	TYPE I/II. RAISE 1 MANHOLE. RECONSTRUCT 1 SURVEY MONUMENT.
S2023	SS-002427	ANDASOL ST	ANGELENO RD	AEGEAN CT	6	1209-A2	Tuesday	MIRA MESA	Residential	408	37	15096	232	3.78	4.75							TYPE I/II. RAISE 2 MANHOLE.
S2023	SS-002428	ANDASOL ST	BIRDS VIEW CT	ALONDA CT	6	1208-J2	Tuesday	MIRA MESA	Residential	280	37	10360	159		2.85							TYPE I/II.
S2023	SS-002430	ANDASOL ST	BEGIN	BIRDS VIEW CT	6	1208-J2	Tuesday	MIRA MESA	Residential	173	27	4671	72		1.32							TYPE I/II.
S2023	SS-002527	ANTIGUA BL	VILLARRICA WY	CAM PLAYA DE ORO	7	1229-J7	Friday	TIERRASANTA	Major	1357	74	100418	1545		72.49							TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 2 WATER VALVES. RAISE 5 MANHOLE. NEAR SCHOOL.
S2023	SS-002513	ANTIGUA BL	CALLE MARISELDA	AVNDA PLAYA VERACRUZ	7	1229-H7	Friday	TIERRASANTA	Major	547	74	40478	623								1	TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 1 MANHOLE. RECONSTRUCT 1 SURVEY MONUMENT.
S2023	SS-002528	ANTIGUA BL	CAM PLAYA ACAPULCO	VILLARRICA WY	7	1229-J7	Friday	TIERRASANTA	Major	370	74	27380	421									TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 3 WATER VALVES.
S2023	SS-002505	ANTIGUA BL	CAM PLAYA DE ORO	VIA VALARTA	7	1229-J7	Friday	TIERRASANTA	Major	714	74	52836	813		28.78						1	TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 1 SURVEY MONUMENT. RAISE 2 MANHOLE.
S2023	SS-002506	ANTIGUA BL	CAM PLAYA PORTOFINO	CAM PLAYA ACAPULCO	7	1229-J7	Friday	TIERRASANTA	Major	740	74	54760	842									TYPE II/III WITH TYPE I OVER BIKE LANE.
S2023	SS-002507	ANTIGUA BL	AVNDA PLAYA VERACRUZ	CAM PLAYA PORTOFINO	7	1229-H7	Friday	TIERRASANTA	Major	308	74	22792	351									TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 1 WATER VALVE.
S2023	SS-002529	ANTIGUA BL	SANTO RD	CALLE MARISELDA	7	1229-H7	Friday	TIERRASANTA	Major	1220	74	90280	1389		2.59							TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 6 WATER VALVES.
S2023	SS-002622	ARBORLAKE WY	POINTED OAK LN	POINTED OAK LN	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	700	33	23100	355		26.88							TYPE I/II.
S2023	SS-003600	BARON DR	FRIANT ST	HEBRIDES DR	6	1209-C4	Tuesday	MIRA MESA	Residential	215	33	7095	109									TYPE I/II.
S2023	SS-003601	BARON DR	PAGODA WY	FRIANT ST	6	1209-C4	Tuesday	MIRA MESA	Residential	387	33	12771	196	2.02								TYPE I/II.
S2023	SS-004107	BERRYFIELD CT	WYNDHAVEN DR	END	1	1188-A5	Monday	CARMEL VALLEY	Residential	505	33	16665	256									TYPE I/II.
S2023	SS-004255	BIRCH GLEN CT	BEGIN	PEPPERBROOK LN	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	285	36	10260	158		9.24							TYPE I/II.
S2023	SS-004288	BIRDS VIEW CT	ANDASOL ST	END	6	1208-J2	Tuesday	MIRA MESA	Residential	135	27	3645	56		1.82							TYPE I/II.
S2023	SS-004373	BLACK PINE PL	CHAPARRAL RIDGE RD	END	1	1188-C5	Monday	CARMEL VALLEY	Residential	100	41	4100	63									TYPE I/II.
S2023	SS-031642	BRIARCREST PL	BEGIN	WHITE OAK LN	1	1188-E6	Monday	PACIFIC HIGHLANDS RANCH	Residential	190	38	7220	111									TYPE I/II.
S2023	SS-031644	BRIARCREST PL	VINWOOD CT	FLINTWOOD WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	600	31	18600	286									TYPE I/II.
S2023	SS-031643	BRIARCREST PL	WHITE OAK LN	VINWOOD CT	1	1188-E6	Monday	PACIFIC HIGHLANDS RANCH	Residential	339	31	10509	162									TYPE I/II.
S2023	SS-004890	BRIGHTON RIDGE CT	HELMER LN	END	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	177	36	6372	98		3.96							TYPE I/II.
S2023	SS-004984	BRONX PL	BEGIN	FULLERTON AV	7	1249-E5	Friday	SERRA MESA	Residential	157	38	5966	92									TYPE I/II.
S2023	SS-005488	CALLE DE LA SIENA	CAM SANDOVAL	END	1	1188-B6	Monday	CARMEL VALLEY	Residential	511	32	16352	252									TYPE I/II.
S2023	SS-005491	CALLE DE LA SIENA	CTE DE LA SIENA	PASEO MONTANAS	1	1188-B6	Monday	CARMEL VALLEY	Residential	295	30	8850	136									TYPE I/II.
S2023	SS-005490	CALLE DE LA SIENA	PASEO MONTANAS	PLAZA DE LA SIENA	1	1188-B6	Monday	CARMEL VALLEY	Residential	300	33	9900	152									TYPE I/II.
S2023	SS-005489	CALLE DE LA SIENA	PLAZA DE LA SIENA	CAM SANDOVAL	1	1188-B6	Monday	CARMEL VALLEY	Residential	420	33	13860	213									TYPE I/II.
S2023	SS-005566	CALLE MARISELDA	ANTIGUA BL	END	7	1229-H7	Friday	TIERRASANTA	Local	880	37	32560	501	8.08								TYPE I/II.
S2023	SS-005841	CAM PLAYA ACAPULCO	CTE PLAYA MAZATLAN	ANTIGUA BL	7	1229-J7	Friday	TIERRASANTA	Local	165	33	5445	84									TYPE I/II.
S2023	SS-005842	CAM PLAYA ACAPULCO	CAM PLAYA MALAGA	CTE PLAYA MAZATLAN	7	1229-J7	Friday	TIERRASANTA	Local	410	33	13530	208									TYPE I/II.
S2023	SS-005843	CAM PLAYA AZUL	CAM PLAYA CARMEL	CTE PLAYA MERIDA	7	1229-J7	Friday	TIERRASANTA	Local	250	33	8250	127									TYPE I/II.
S2023	SS-005847	CAM PLAYA CARMEL	VILLARRICA WY	CAM PLAYA AZUL	7	1229-J7	Friday	TIERRASANTA	Local	335	33	11055	170		3.25							TYPE I/II.
S2023	SS-005846	CAM PLAYA CARMEL	CAM PLAYA AZUL	END	7	1229-J7	Friday	TIERRASANTA	Local	440	36	15840	244									TYPE I/II.
S2023	SS-005852	CAM PLAYA DE ORO	CTE PLAYA MADERA	CTE PLAYA AZTECA	7	1229-J7	Friday	TIERRASANTA	Local	230	33	7590	117									TYPE I/II.
S2023	SS-005853	CAM PLAYA DE ORO	CTE PLAYA CORONA	CTE PLAYA MADERA	7	1229-J7	Friday	TIERRASANTA	Local	270	33	8910	137									TYPE I/II.
S2023	SS-005854	CAM PLAYA DE ORO	CAM PLAYA NORTE	CTE PLAYA CORONA	7	1229-J7	Friday	TIERRASANTA	Local	270	33	8910	137		7.6							TYPE I/II.
S2023	SS-005857	CAM PLAYA DE ORO	CTE PLAYA AZTECA	ANTIGUA BL	7	1229-J7	Friday	TIERRASANTA	Local	245	33	8085	124									TYPE I/II.
S2023	SS-005862	CAM PLAYA MALAGA	AVNDA PLAYA VERACRUZ	CTE PLAYA TOLUCA	7	1229-J7	Friday	TIERRASANTA	Local	236	33	7788	120		4.44							TYPE I/II.
S2023	SS-005860	CAM PLAYA MALAGA	CAM PLAYA ACAPULCO	CTE PLAYA TAMPICO	7	1229-J7	Friday	TIERRASANTA	Local	301	33	9933	153		9.13							TYPE I/II.
S2023	SS-005859	CAM PLAYA MALAGA	CTE PLAYA SOLANA	CAM PLAYA ACAPULCO	7	1229-J7	Friday	TIERRASANTA	Local	298	33	9834	151		3.17							TYPE I/II.
S2023	SS-005858	CAM PLAYA MALAGA	CTE PLAYA TOLUCA	CTE PLAYA SOLANA	7	1229-J7	Friday	TIERRASANTA	Local	295	33	9735	150		5.86							TYPE I/II.
S2023	SS-005864	CAM PLAYA MALAGA	CAM PLAYA MALAGA	AVNDA PLAYA VERACRUZ	7	1229-J7	Friday	TIERRASANTA	Local	295	33	9735	150		4.96							TYPE I/II.
S2023	SS-005863	CAM PLAYA MALAGA	CAM PLAYA DE ORO	CTE PLAYA DE CASTILA	7	1229-J7	Friday	TIERRASANTA	Local	260	33	8580	132		2.53							TYPE I/II.
S2023	SS-005865	CAM PLAYA MALAGA	AVNDA PLAYA VERACRUZ	END	7	1229-J7	Friday	TIERRASANTA	Local	370												





Slurry Seal Group 2023 - Scope of Work  
 IO: 21004779

Work Order Number	Segment ID	Street Name	Cross Street 1	Cross Street 2	Council District	TB Map Page	Trash Day	Community Planning Area	Functional Classification	Survey Length (FT)	Survey Width (FT)	Survey Area (SF)	Crack Seal (LBS)	Base Repair (TONS)	Mill / Pave (TONS)	Hump Removal (LF)	Inlet Marker (EA)	Inlet Protection (EA)	Traffic Loops (EA)	Traffic Loops Location	Survey Monument	Comments
S2023	SS-031702	GAMAY WY	OLD CARMEL VALLEY RD	CHAMBORD WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	150	37	5550	85									TYPE I/II.
S2023	SS-031703	GAMAY WY	CHAMBORD WY	SUNSTONE PE	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	420	31	13020	200									TYPE I/II.
S2023	SS-031707	GAMAY WY	SUNSTONE PE	DEER PARK WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	163	31	5053	78									TYPE I/II.
S2023	SS-011913	GATEMOORE WY	SCRIPPS CREEK DR	MONTAUBON WY	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	700	30	21000	323			40						TYPE I/II.
S2023	SS-011914	GATEMOORE WY	SCRIPPS CREEK DR	WALDORF WY	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	260	30	7800	120									TYPE I/II.
S2023	SS-011915	GATEMOORE WY	WALDORF WY	END	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	777	31	24087	371									TYPE I/II.
S2023	SS-012376	GOLDFISH CT	BEGIN	GOLDFISH WY	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	240	34	8160	126									TYPE I/II.
S2023	SS-012378	GOLDFISH WY	SALVIA WY	GOLDFISH CT	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	228	28	6384	98									TYPE I/II.
S2023	SS-012379	GOLDFISH WY	ROAN WY	END	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	418	32	13376	206			85						TYPE I/II.
S2023	SS-012377	GOLDFISH WY	GOLDFISH CT	ROAN WY	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	415	27	11205	172									TYPE I/II.
S2023	SS-012463	GRAINWOOD WY	BEGIN	KINGSPINE AV	5	1210-B4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	846	37	31302	482									TYPE I/II.
S2023	SS-012582	GRAYDON RD	LANSDALE DR	CLAYMONT CT	1	1188-B5	Monday	CARMEL VALLEY	Major	490	37	18130	279									TYPE I/II. RAISE 1 WATER VALVE.
S2023	SS-012580	GRAYDON RD	TORREY BLUFF DR	FEDERMAN LN	1	1188-B5	Monday	CARMEL VALLEY	Major	190	37	7030	108									TYPE I/II.
S2023	SS-012581	GRAYDON RD	CRISTALLO PL	LANSDALE DR	1	1188-B5	Monday	CARMEL VALLEY	Major	313	37	11581	178									TYPE I/II.
S2023	SS-012583	GRAYDON RD	FEDERMAN LN	CAMARENA RD	1	1188-B5	Monday	CARMEL VALLEY	Major	534	37	19758	304									TYPE I/II.
S2023	SS-012584	GRAYDON RD	CAMARENA RD	CRISTALLO PL	1	1188-B5	Monday	CARMEL VALLEY	Major	480	37	17760	273									TYPE I/II.
S2023	SS-012585	GRAYDON RD	CLAYMONT CT	CARMEL CENTER RD	1	1188-C5	Monday	CARMEL VALLEY	Major	350	37	12950	199									TYPE I/II. RAISE 2 WATER VALVES.
S2023	SS-012915	HALF MILE DR	LANDFAIR RD	EL CAM REAL	1	1188-A4	Monday	CARMEL VALLEY	Major	215	48	10320	159									TYPE I/II. RAISE 2 WATER VALVES.
S2023	SS-012918	HALF MILE DR	HIGH BLUFF DR	TIVERTON RD	1	1188-A4	Monday	CARMEL VALLEY	Major	275	37	10175	157									TYPE I/II.
S2023	SS-012916	HALF MILE DR	TIVERTON RD	LANDFAIR RD	1	1188-A4	Monday	CARMEL VALLEY	Major	420	44	18480	284									TYPE I/II.
S2023	SS-013307	HELMER LN	BRIGHTON RIDGE CT	FRANK DANIELS WY	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	275	33	9075	140									TYPE I/II.
S2023	SS-013308	HELMER LN	SUNSET RIDGE DR	BRIGHTON RIDGE CT	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	790	32	25280	389									TYPE I/II.
S2023	SS-013360	HERITAGE GLEN CT	HERITAGE GLEN LN	END	1	1188-C6	Monday	CARMEL VALLEY	Residential	142	39	5538	85									TYPE I/II.
S2023	SS-013361	HERITAGE GLEN LN	BEGIN	HERITAGE GLEN CT	1	1188-B6	Monday	CARMEL VALLEY	Residential	695	35	24325	374									TYPE I/II.
S2023	SS-013362	HERITAGE GLEN LN	HERITAGE GLEN CT	CARMEL CENTER RD	1	1188-C6	Monday	CARMEL VALLEY	Residential	171	29	4959	76									TYPE I/II.
S2023	SS-013893	HUNTINGTON AV	WILBEE CT	EPAULETTE ST	7	1249-E6	Friday	SERRA MESA	Residential	800	33	26400	406									TYPE I/II.
S2023	SS-014258	IRVINGTON AV	EPAULETTE ST	AMULET ST	7	1249-E6	Friday	SERRA MESA	Residential	263	33	8679										TYPE I/II. NO CRACK SEAL.
S2023	SS-014257	IRVINGTON AV	AMULET ST	MELBOURNE DR	7	1249-E6	Friday	SERRA MESA	Residential	272	33	8976	138									TYPE I/II.
S2023	SS-014259	IRVINGTON AV	WILBEE CT	EPAULETTE ST	7	1249-E6	Friday	SERRA MESA	Residential	980	33	32340	498									TYPE I/II.
S2023	SS-014315	ISLEWORTH AV	FRIANT ST	HEBRIDES DR	6	1209-D4	Tuesday	MIRA MESA	Residential	765	33	25245	388									TYPE I/II.
S2023	SS-014314	ISLEWORTH AV	HEBRIDES DR	FLANDERS DR	6	1209-D4	Tuesday	MIRA MESA	Residential	227	33	7491	115									TYPE I/II.
S2023	SS-014935	KATYDID CR	SALVIA WY	END	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	892	35	31220	480									TYPE I/II.
S2023	SS-014936	KAUFMAN WY	CANRIGHT WY	NORTHURP DR	6	1209-A5	Tuesday	MIRA MESA	Residential	664	31	20584	317									TYPE I/II.
S2023	SS-015163	KERWOOD CT	CAMARENA RD	END	1	1188-B5	Monday	CARMEL VALLEY	Residential	624	35	21840	336									TYPE I/II.
S2023	SS-015162	KERWOOD CT	BEGIN	CAMARENA RD	1	1188-B5	Monday	CARMEL VALLEY	Residential	420	31	13020	200									TYPE I/II.
S2023	SS-015252	KINGSPINE AV	GRAINWOOD WY	SEMILLON BL	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	320	33	10560	162									TYPE I/II.
S2023	SS-015254	KINGSPINE AV	BARRYWOOD WY	GRAINWOOD WY	5	1210-B4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	2335	33	77055	1185									TYPE I/II.
S2023	SS-015253	KINGSPINE AV	SPRUCE GROVE AV	BARRYWOOD WY	5	1210-B4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	428	37	15836	244									TYPE I/II.
S2023	SS-015962	LANDFAIR RD	NEWCREST PT	WINDSWEEP TR	1	1187-J4	Monday	CARMEL VALLEY	Residential	176	29	5104	79									TYPE I/II.
S2023	SS-015963	LANDFAIR RD	HIGH BLUFF DR	NEWCREST PT	1	1187-J4	Monday	CARMEL VALLEY	Residential	640	28	17920	276									TYPE I/II.
S2023	SS-015967	LANDFAIR RD	WINDSWEEP TR	HALF MILE DR	1	1188-A4	Monday	CARMEL VALLEY	Residential	768	29	22272	343									TYPE I/II. INCLUDE CUL-DE-SAC.
S2023	SS-016040	LANSDALE DR	GRAYDON RD	DEL MAR HEIGHTS RD	1	1188-B5	Monday	CARMEL VALLEY	Major	375	36	13500	208									TYPE I/II.
S2023	SS-016087	LARMIER CR	BEGIN	POCHE PT	5	1209-J2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	252	44	11088	171									TYPE I/II.
S2023	SS-016088	LARMIER CR	POCHE PT	SPRING CANYON RD	5	1209-J2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	560	28	15680	241									TYPE I/II.
S2023	SS-016370	LICIA WY	LICIA WY	PARK VILLAGE RD	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	246	33	8118	125									TYPE I/II.
S2023	SS-016369	LICIA WY	PARK VILLAGE RD	PIPIT PL	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	174	33	5742	88									TYPE I/II.
S2023	SS-016619	LIVEWOOD WY	BEGIN	SEMILLON BL	5	1210-B4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	927	34	31518	485									TYPE I/II.
S2023	SS-016809	LONE CYPRESS PL	BEGIN	CARMEL CENTER RD	1	1188-B6	Monday	CARMEL VALLEY	Residential	143	37	5291	81									TYPE I/II.
S2023	SS-017011	LUPITA CT	BEGIN	CARMEL CENTER RD	1	1188-B6	Monday	CARMEL VALLEY	Residential	280	33	9240	142									TYPE I/II.
S2023	SS-017449	MARATHON DR	FULLERTON AV	FERMI AV	7	1249-E5	Friday	SERRA MESA	Residential	650	33	21450	330									TYPE I/II.
S2023	SS-017694	MARTINDALE CT	FULLERTON AV	FERMI AV	7	1249-E5	Friday	SERRA MESA	Residential	650	33	21450	330									TYPE I/II.
S2023	SS-017853	MC GUIRE DR	CARMEL COUNTRY RD	CARMEL CREEK RD	1	1188-B5	Monday	CARMEL VALLEY	Prime	567	37	20979	323									TYPE I/II.
S2023	SS-017960	MEADOWDALE LN	WALNUTDALE ST	END	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	373	31	11563	178									TYPE I/II.
S2023	SS-017961	MEADOWDALE LN	PINECASTLE ST	WALNUTDALE ST	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	303	33	9999	154									TYPE I/II.
S2023	SS-018006	MELBOURNE DR	FULLERTON AV	FERMI AV	7	1249-E5	Friday	SERRA MESA	Residential	645	33	21285	327									TYPE I/II.
S2023	SS-018005	MELBOURNE DR	FERMI AV	ADMIRAL AV	7	1249-E5	Friday	SERRA MESA	Residential	275	33	9075										TYPE I/II. NO CRACK SEAL.
S2023	SS-018074	MENSHA PL	RALSTON CR	CARMEL CENTER RD	1	1188-C5	Monday	CARMEL VALLEY	Residential	212	29	6148	95									TYPE I/II.
S2023	SS-018075	MENSHA PL	BEGIN	RALSTON CR	1	1188-B5	Monday	CARMEL VALLEY	Residential	428	32	13696	211									TYPE I/II.
S2023	SS-031695	MILL CREEK RD	FLINTWOOD WY	DEER PARK WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	115	31	3565	55									TYPE I/II.
S2023	SS-031694	MILL CREEK RD	CHAMBORD WY	FLINTWOOD WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	425	31	13175	203									TYPE I/II.
S2023	SS-031693	MILL CREEK RD	OLD CARMEL VALLEY RD	CHAMBORD WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	165	36	5940	91									TYPE I/II.
S2023	SS-018363	MIRA LAGO TR	SCRIPPS LAKE DR	MIRA LAGO WY	5	1209-J3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	1480	34	50320	774									TYPE I/II.
S2023	SS-018364	MIRA LAGO WY	MIRA LAGO TR	SUNSET RIDGE DR	5	1209-J3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	820	33	27060	416									TYPE I/II.
S2023	SS-018670	MISTRAL PL	BEGIN	FUTURA ST	1	1188-B6	Monday	CARMEL VALLEY	Residential	265	32	8480	130									TYPE I/II.
S2023	SS-018669	MISTRAL PL	FUTURA ST	END	1	1188-B6	Monday	CARMEL VALLEY	Residential	405	33.5	13568	209									TYPE I/II.
S2023	SS-018829	MONTAUBON CR	MONTAUBON WY	MONTAUBON WY	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	272	27	7344	113									TYPE I/II.
S2023	SS-018831	MONTAUBON WY	MONTAUBON CR	MONTAUBON CR	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	155	29	4495	69									TYPE I/II.
S2023	SS-018833	MONTAUBON WY	WALDORF WY	GATEMOORE WY	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	680	29	19720	303									TYPE I/II.
S2023	SS-018832	MONTAUBON WY	MONTAUBON CR	END	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	200	27	5400	83									TYPE I/II.
S2023	SS-018830	MONTAUBON WY	WALDORF WY	MONTAUBON CR	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	305	29	8845	136									TYPE I/II.
S2023	SS-018881	MONTEREY CYPRESS WY	BEGIN	CYPRESS GLEN PL	1	1188-C6	Monday	CARMEL VALLEY	Residential	355	34	12070	186									TYPE I/II.
S2023	SS-018880	MONTEREY CYPRESS WY	C																			

Slurry Seal Group 2023 - Scope of Work  
 IO: 21004779


Work Order Number	Segment ID	Street Name	Cross Street 1	Cross Street 2	Council District	TB Map Page	Trash Day	Community Planning Area	Functional Classification	Survey Length (FT)	Survey Width (FT)	Survey Area (SF)	Crack Seal (LBS)	Base Repair (TONS)	Mill / Pave (TONS)	Hump Removal (LF)	Inlet Marker (EA)	Inlet Protection (EA)	Traffic Loops (EA)	Traffic Loops Location	Survey Monument	Comments
S2023	SS-020987	PAGODA WY	BELFAST CR	WESTONHILL DR	6	1209-C4	Tuesday	MIRA MESA	Residential	400	33	13200	203		0.63							TYPE I/II.
S2023	SS-020990	PAGODA WY	SAN RAMON DR	BARON DR	6	1209-C5	Tuesday	MIRA MESA	Residential	550	33	18150	279		3.17							TYPE I/II.
S2023	SS-020989	PAGODA WY	BARON DR	BELFAST CR	6	1209-C5	Tuesday	MIRA MESA	Residential	220	33	7260	112		4.44							TYPE I/II.
S2023	SS-021451	PASEO MONTANAS	CARMEL CREEK RD	CALLE DE LA SIENA	1	1188-B6	Monday	CARMEL VALLEY	Residential	280	33	9240	142			20						TYPE I/II.
S2023	SS-021641	PEPPERBROOK LN	BIRCH GLEN CT	END	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	225	34	7650	118		20.33							TYPE I/II.
S2023	SS-021642	PEPPERBROOK LN	TIMBERLAKE DR	BIRCH GLEN CT	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	205	29	5945	91		22.18			2				TYPE I/II.
S2023	SS-021813	PINE MEADOW CT	SUNSET BLUFFS WY	END	1	1188-C5	Monday	CARMEL VALLEY	Residential	325	33	10725	165									TYPE I/II.
S2023	SS-021858	PIBIT CT	PIBIT PL	END	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	164	37	6068	93									TYPE I/II.
S2023	SS-021861	PIBIT PL	PIBIT CT	LICIA WY	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	545	33	17985	277									TYPE I/II.
S2023	SS-021862	PIBIT PL	SALVIA WY	PIBIT CT	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	586	33	19338	298		1.58	35			2			TYPE I/II.
S2023	SS-021860	PIBIT PL	LICIA WY	PIBIT WY	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	162	33	5346	82									TYPE I/II.
S2023	SS-021859	PIBIT PL	PIBIT WY	END	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	495	31	15345	236		2.38					2		TYPE I/II.
S2023	SS-021863	PIBIT PL	DORMOUSE RD	SALVIA WY	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	310	33	10230	157									TYPE I/II.
S2023	SS-021864	PIBIT WY	BEGIN	PIBIT PL	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	101	36	3636	56									TYPE I/II.
S2023	SS-021933	PLAZA DE LA SIENA	CALLE DE LA SIENA	END	1	1188-B6	Monday	CARMEL VALLEY	Residential	215	32	6880	106									TYPE I/II.
S2023	SS-022039	POCHE PT	LARMIER CR	END	5	1209-J2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	340	33	11220	173		1.58							TYPE I/II.
S2023	SS-022088	POINTED OAK LN	ARBORLAKE WY	ARBORLAKE WY	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	725	33	23925	368		10.22			1				TYPE I/II.
S2023	SS-022087	POINTED OAK LN	ARBORLAKE WY	SCRIPPS TL	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	120	33	3960	61		3.17							TYPE I/II.
S2023	SS-031704	PORTER CREEK RD	CHAMBOARD WY	DEER PARK WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	580	31	17980	277					2		2	1	TYPE I/II. REPLACE 1 SURVEY MONUMENT LID.
S2023	SS-022320	POYNTELL CR	TIMBERLAKE DR	END	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	288	34	9792	151		21.12							TYPE I/II.
S2023	SS-022481	QUARTER MILE DR	LONG RUN DR	EL CAM REAL	1	1188-A5	Monday	CARMEL VALLEY	Major	590	65	38350	590		30.1			1		1	10	@ EL CAM REAL
S2023	SS-022553	QUINNEL CT	BEGIN	FEDERMAN LN	1	1188-B5	Monday	CARMEL VALLEY	Residential	152	37	5624	87		0.48							TYPE I/II.
S2023	SS-031705	RABBIT RIDGE RD	CHAMBOARD WY	DEER PARK WY	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	555	31	17205	265					2		2		TYPE I/II.
S2023	SS-022653	RALSTON CR	MENSHA PL	END	1	1188-C5	Monday	CARMEL VALLEY	Residential	645	33	21285	327		2.53					2		TYPE I/II.
S2023	SS-023298	ROAN RD	ROAN WY	END	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	416	34	14144	218		0.53							TYPE I/II.
S2023	SS-023297	ROAN RD	SALVIA WY	ROAN WY	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	753	30	22590	348									TYPE I/II.
S2023	SS-023299	ROAN WY	GOLDFISH WY	ROAN RD	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	250	29	7250	112									TYPE I/II.
S2023	SS-023644	ROUGEMONT PL	BEGIN	END	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	345	28	9660	149		2.06							TYPE I/II.
S2023	SS-023643	ROUGEMONT PL	RUE CHAMONIX	RUE CHANTEMAR	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	150	36	5400	83		12.59					2		TYPE I/II.
S2023	SS-023642	ROUGEMONT PL	BEGIN	RUE CHAMONIX	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	698	30	20940	322		9.5					4		TYPE I/II.
S2023	SS-023697	RUE CHAMONIX	ROUGEMONT PL	END	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	215	36	7740	119									TYPE I/II.
S2023	SS-023698	RUE CHAMONIX	BEGIN	ROUGEMONT PL	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	285	38	10830	167		4.8							TYPE I/II.
S2023	SS-023699	RUE CHANTEMAR	RUE MARABELLE	FAIRBROOK RD	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	325	38	12350	190		2.96					95		TYPE I/II.
S2023	SS-023706	RUE CHANTEMAR	ROUGEMONT PL	RUE PARC	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	390	38	14820	228		4.75							TYPE I/II.
S2023	SS-023701	RUE CHANTEMAR	RUE PARC	RUE SIENNE NORD	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	628	38	23864	367		4.01							TYPE I/II. RAISE 1 MANHOLES. RAISE 1 WATER VALVE.
S2023	SS-023702	RUE CHANTEMAR	RUE VINCENNES	ROUGEMONT PL	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	250	37	9250	142		3.43					2		TYPE I/II.
S2023	SS-023703	RUE CHANTEMAR	RUE CHAMBERRY	RUE VINCENNES	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	825	38	31350	482		6.23							TYPE I/II.
S2023	SS-023700	RUE CHANTEMAR	RUE SIENNE NORD	RUE MARABELLE	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	250	38	9500	146		1.85					1		TYPE I/II.
S2023	SS-023725	RUE FINISTERRE	RUE RIVIERE VERTE	RUE RIVIERE VERTE	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	630	30	18900	291		34.48					1		TYPE I/II.
S2023	SS-023724	RUE FINISTERRE	RUE TOURAINE	RUE PARC	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	170	30	5100	78		3.38							TYPE I/II.
S2023	SS-023723	RUE FINISTERRE	RUE PARC	RUE RIVIERE VERTE	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	295	32	9440	145		12.94						1	TYPE I/II.
S2023	SS-023311	RUE FONTENAY	FAIRBROOK RD	RUE FONTENAY CT	5	1210-B4	Tuesday	SCRIPPS MIRAMAR RANCH	Local	445	37	16465	253							2		TYPE I/II.
S2023	SS-023312	RUE FONTENAY	RUE FONTENAY CT	END	5	1210-B4	Tuesday	SCRIPPS MIRAMAR RANCH	Local	250	49	12250	188									TYPE I/II.
S2023	SS-023313	RUE FONTENAY CT	BEGINNING	RUE FONTENAY	5	1210-B4	Tuesday	SCRIPPS MIRAMAR RANCH	Local	270	49	13230	204							1		TYPE I/II.
S2023	SS-023730	RUE MARABELLE	RUE CHANTEMAR	END	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	91	60	5460	84		2.06							TYPE I/II.
S2023	SS-023736	RUE PARC	RUE TOURAINE	RUE FINISTERRE	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	250	37	9250	142		2.8							TYPE I/II.
S2023	SS-023735	RUE PARC	RUE CHANTEMAR	RUE TOURAINE	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	140	37	5180	80		12.67						2	TYPE I/II.
S2023	SS-023737	RUE RIVIERE VERTE	RUE FINISTERRE	RUE FINISTERRE	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	645	30	19350	298		9.03							TYPE I/II.
S2023	SS-023739	RUE SIENNE NORD	BEGIN	RUE CHANTEMAR	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	246	37	9102	140		29.62							TYPE I/II.
S2023	SS-023745	RUE TOURAINE	RUE PARC	RUE FINISTERRE	5	1210-C5	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	355	34	12070	186		15.31							TYPE I/II.
S2023	SS-023802	RUFFUS CT	BEGIN	DORMOUSE RD	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	175	37	6475	100		1.37							TYPE I/II.
S2023	SS-023876	SADDLE MTN CT	BEGIN	CHAPARRAL RIDGE RD	1	1188-C6	Monday	CARMEL VALLEY	Residential	495	30	14850	228									TYPE I/II.
S2023	SS-023910	SALIX CT	BEGIN	SALIX PL	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	138	39	5382	83									TYPE I/II.
S2023	SS-023911	SALIX PL	SALIX CT	LICIA WY	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	570	33	18810	289							1		TYPE I/II.
S2023	SS-023912	SALIX PL	LICIA WY	LICIA WY	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	173	30	5190	80									TYPE I/II.
S2023	SS-023913	SALIX PL	DORMOUSE RD	SALIX CT	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	572	32	18304	282									TYPE I/II.
S2023	SS-023915	SALIX WY	BEGIN	SALIX PL	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	484	31	15004	231									TYPE I/II.
S2023	SS-023914	SALIX WY	SALIX PL	END	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	285	33	9405	145			25						TYPE I/II.
S2023	SS-023949	SALVIA WY	ROAN RD	DORMOUSE RD	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	270	33	8910	137							1		TYPE I/II.
S2023	SS-023952	SALVIA WY	PIBIT PL	KATYDID CR	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	222	33	7326	113		0.53							TYPE I/II.
S2023	SS-023951	SALVIA WY	KATYDID CR	GOLDFISH WY	6	1189-A7	Tuesday	RANCHO PENASQUITOS	Residential	661	33	21813	336			55				1		TYPE I/II.
S2023	SS-023950	SALVIA WY	GOLDFISH WY	ROAN RD	6	1189-A6	Tuesday	RANCHO PENASQUITOS	Residential	270	33	8910	137			35				1		TYPE I/II.
S2023	SS-024145	SAN RAMON DR	FLANDERS DR	IVORY COAST DR	6	1209-C4	Tuesday	MIRA MESA	Residential	227	37	8399	129		3.17							TYPE I/II.
S2023	SS-024146	SAN RAMON DR	HEBRIDES DR	FLANDERS DR	6	1209-C4	Tuesday	MIRA MESA	Residential	266	37	9842	151		20.7							TYPE I/II.
S2023	SS-024144	SAN RAMON DR	IVORY COAST DR	REAGAN RD	6	1209-C4	Tuesday	MIRA MESA	Residential	247	37	9139	141		11.4					50		TYPE I/II. NEAR SCHOOL.
S2023	SS-024508	SCRIPPS CAPE VISTA PT	BEGIN	SUNSET RIDGE DR	5	1209-J3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	660	36	23760	366		33.63							TYPE I/II.
S2023	SS-024520	SCRIPPS CREEK DR	GATEMOORE WY	SPRING CANYON RD	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	50	75	3750	58									TYPE I/II.
S2023	SS-024573	SCRIPPS TL	REDFERN CR	POINTED OAK LN	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Collector	203	37	7511	116		3.17					150		TYPE I/II.
S2023	SS-024572	SCRIPPS TL	POINTED OAK LN	WEATHERWOOD TR	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Collector	335	37	12395	191		30.31					20		TYPE I/II.
S2023	SS-024571	SCRIPPS TL	WEATHERWOOD TR	SEMILLON BL	5	1210-A3	Tuesday	SCRIPPS MIR														

Slurry Seal Group 2023 - Scope of Work  
 IO: 21004779

Work Order Number	Segment ID	Street Name	Cross Street 1	Cross Street 2	Council District	TB Map Page	Trash Day	Community Planning Area	Functional Classification	Survey Length (FT)	Survey Width (FT)	Survey Area (SF)	Crack Seal (LBS)	Base Repair (TONS)	Mill / Pave (TONS)	Hump Removal (LF)	Inlet Marker (EA)	Inlet Protection (EA)	Traffic Loops (EA)	Traffic Loops Location	Survey Monument	Comments
S2023	SS-025940	SUNSET RIDGE DR	MIRA LAGO WY	STUEER WY	5	1209-J2	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	210	40	8400	129		41.98							TYPE I/II.
S2023	SS-025941	SUNSET RIDGE DR	SCRIPPS CAPE VISTA PT	MIRA LAGO WY	5	1209-J3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	205	37	7585	117		20.86							TYPE I/II.
S2023	SS-025944	SUNSET RIDGE DR	TIMBERLAKE DR	SCRIPPS LAKE DR	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	800	37	29600	455		6.02							TYPE I/II.
S2023	SS-025943	SUNSET RIDGE DR	SCRIPPS LAKE DR	HELMER LN	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	406	36	14616	225		2.69							TYPE I/II.
S2023	SS-025937	SUNSET RIDGE DR	ANCONA LN	CANARYWOOD CT	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	295	38	11210	172		33.9							TYPE I/II.
S2023	SS-031708	SUNSTONE PE	GAMAY WY	CHAMBORD WY	1	1188-E4	Monday	PACIFIC HIGHLANDS RANCH	Residential	545	31	16895	260				2	2				TYPE I/II.
S2023	SS-031929	SUNSTONE PE	CHAMBORD WY	END	1	1188-E4	Monday	PACIFIC HIGHLANDS RANCH	Residential	420	40	16800	258									TYPE I/II.
S2023	SS-026052	SYCAMORE RIDGE CT	CHAPARAL VALLEY CT	END	5	1210-C3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	490	34	16660	256		1.06							TYPE I/II.
S2023	SS-026453	THORNBRUSH CT	BEGIN	FAIRBROOK RD	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	200	35	7000	108		4.12							TYPE I/II.
S2023	SS-026511	TIMBER RIDGE RD	CARMEL CENTER RD	CORBETT CT	1	1188-C5	Monday	CARMEL VALLEY	Residential	325	32	10400	160				2	2				TYPE I/II.
S2023	SS-026510	TIMBER RIDGE RD	CORBETT CT	CHAPARRAL RIDGE RD	1	1188-C5	Monday	CARMEL VALLEY	Residential	184	32	5888	91		7.39							TYPE I/II. RAISE 2 WATER VALVES.
S2023	SS-026516	TIMBERLAKE DR	SUMMERWOOD CT	PEPPERBROOK LN	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	340	37	12580	194		16.84							TYPE I/II.
S2023	SS-026517	TIMBERLAKE DR	QUAIL SPRINGS CT	SUMMERWOOD CT	5	1209-J3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	690	37	25530	393		12.04							TYPE I/II.
S2023	SS-026515	TIMBERLAKE DR	PEPPERBROOK LN	SUNSET RIDGE DR	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	325	37	12025	185		15.95							TYPE I/II.
S2023	SS-026518	TIMBERLAKE DR	SCRIPPS LAKE DR	QUAIL SPRINGS CT	5	1209-J3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	760	37	28120	433		3.43			2				TYPE I/II. RAISE 2 MANHOLE.
S2023	SS-026514	TIMBERLAKE DR	SUNSET RIDGE DR	POYNTELL CR	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	715	37	26455	407		63.84			1				TYPE I/II.
S2023	SS-026513	TIMBERLAKE DR	POYNTELL CR	SCRIPPS TL	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Prime	205	37	7585	117		8.87			1				TYPE I/II.
S2023	SS-026549	TIVERTON RD	WYNDHAVEN DR	HALF MILE DR	1	1188-A4	Monday	CARMEL VALLEY	Residential	1395	22	30690	472		14.26		10	10				TYPE I/II.
S2023	SS-026598	TONDINO CT	BEGIN	TONDINO RD	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	101	31	3131	48		1.27							TYPE I/II.
S2023	SS-026600	TONDINO RD	WEATHERWOOD TR	TONDINO CT	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	401	27	10827	167		3.06		50					TYPE I/II.
S2023	SS-026599	TONDINO RD	TONDINO CT	ACCRA LN	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	290	28	8120	125		0.32		90					TYPE I/II.
S2023	SS-026657	TORREY BLUFF DR	CARMEL CREEK RD	GRAYDON RD	1	1188-B5	Monday	CARMEL VALLEY	Major	915	37	33855	521		18.72							TYPE I/II.
S2023	SS-026693	TORREY RIDGE DR	GRAYDON RD	DEL MAR HEIGHTS RD	1	1188-B5	Monday	CARMEL VALLEY	Major	480	37	17760	273		12.43			8			DEL MAR HIGHTS RD & TORREY RIDGE RD	TYPE I/II.
S2023	SS-027025	TWINLEAF CT	TWINLEAF WY	END	5	1209-H2	Tuesday	MIRAMAR RANCH NORTH	Residential	240	34	8160	126		1.58							TYPE I/II.
S2023	SS-027027	TWINLEAF WY	TWINLEAF CT	MONTAUBON WY	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	640	29	18560	286						2			TYPE I/II.
S2023	SS-027028	TWINLEAF WY	BEGIN	TWINLEAF CT	5	1209-H2	Tuesday	MIRAMAR RANCH NORTH	Residential	465	32	14880	229				1	1				TYPE I/II.
S2023	SS-027923	VIA VALARTA	VIA DOMINIQUE	COLLEGIO DR	7	1250-A1	Friday	TIERRASANTA	Collector	865	60	51900	798		23.34						1	TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 1 WATER VALVE. RAISE 1 MANHOLE. RAISE 1 SURVEY MONUMENT.
S2023	SS-027920	VIA VALARTA	CAM PLAYA NORTE	AVNDA PLAYA CANCUN	7	1230-A7	Friday	TIERRASANTA	Collector	200	60	12000	185									TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 1 MANHOLE.
S2023	SS-027924	VIA VALARTA	CLAIREMONT MESA BL	VIA DOMINIQUE	7	1250-A1	Friday	TIERRASANTA	Collector	425	60	25500	392		18.06							TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 1 WATER VALVE.
S2023	SS-027919	VIA VALARTA	AVNDA PLAYA CANCUN	ANTIGUA BL	7	1230-A7	Friday	TIERRASANTA	Collector	835	60	50100	771		16.53						1	TYPE II/III WITH TYPE I OVER BIKE LANE. RECONSTRUCT 1 SURVEY MONUMENT. RAISE 2 MANHOLE.
S2023	SS-027921	VIA VALARTA	VIA PLAYA DE CORTES	CAM PLAYA NORTE	7	1230-A7	Friday	TIERRASANTA	Collector	491	60	29460	453						2			TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 2 MANHOLE. RAISE 5 WATER VALVES.
S2023	SS-027922	VIA VALARTA	COLLEGIO DR	VIA PLAYA DE CORTES	7	1250-A1	Friday	TIERRASANTA	Collector	910	60	54600	840		60.56		74	1	2			TYPE II/III WITH TYPE I OVER BIKE LANE. RAISE 8 WATER VALVES. RAISE 2 MANHOLE.
S2023	SS-027925	VIA VALARTA	ANTIGUA BL	CAM PLAYA CANCUN	7	1230-A7	Friday	TIERRASANTA	Collector	900	62	55800	858		4.86		56		2			TYPE II/III WITH TYPE I OVER BIKE LANE.
S2023	SS-027995	VILLARRICA WY	CTE PLAYA BARCELONA	PORTOBELLO DR	7	1229-J7	Friday	TIERRASANTA	Local	650	38	24700	380		7.13			1	2			TYPE I/II. RAISE 1 MANHOLE.
S2023	SS-027994	VILLARRICA WY	ANTIGUA BL	CAM PLAYA CARMEL	7	1229-J7	Friday	TIERRASANTA	Local	315	38	11970	184									TYPE I/II.
S2023	SS-027993	VILLARRICA WY	CAM PLAYA CARMEL	CTE PLAYA BARCELONA	7	1229-J7	Friday	TIERRASANTA	Local	470	38	17860	275		1.06		50		2			TYPE I/II.
S2023	SS-031647	WINWOOD CT	BRIARCREST PL	END	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	135	33	4455	69									TYPE I/II.
S2023	SS-028189	WALDORF WY	MONTAUBON WY	SHERRARD WY	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	240	30	7200	111						2			TYPE I/II.
S2023	SS-028188	WALDORF WY	SHERRARD WY	GATEMOORE WY	5	1209-J2	Tuesday	MIRAMAR RANCH NORTH	Residential	272	29	7888	121	8.82								TYPE I/II.
S2023	SS-028221	WALNUTDALE ST	MEADOWDALE LN	PINECASTLE ST	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	970	32	31040	478		12.72				2			TYPE I/II.
S2023	SS-028220	WALNUTDALE ST	PINECASTLE ST	FAIRBROOK RD	5	1210-C4	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	270	34	9180	141		1.48							TYPE I/II.
S2023	SS-028351	WEATHERWOOD PL	BEGIN	WEATHERWOOD TR	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	165	37	6105	94		1.16							TYPE I/II.
S2023	SS-028356	WEATHERWOOD TR	SCRIPPS TL	TONDINO RD	5	1210-A3	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	106	31	3286	51		0.84			2	2			TYPE I/II.
S2023	SS-028354	WEATHERWOOD TR	ACCRA LN	ACCRA LN	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	385	32	12320	190		4.75			1	2			TYPE I/II.
S2023	SS-028355	WEATHERWOOD TR	TONDINO RD	ACCRA LN	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	640	32	20480	315		2.64			1	1			TYPE I/II.
S2023	SS-028353	WEATHERWOOD TR	ACCRA LN	WEATHERWOOD PL	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	220	31	6820	105		5.49							TYPE I/II.
S2023	SS-028352	WEATHERWOOD TR	WEATHERWOOD PL	END	5	1210-A2	Tuesday	SCRIPPS MIRAMAR RANCH	Residential	275	33	9075	140		8.61							TYPE I/II.
S2023	SS-031640	WHITE OAK LN	OLD CARMEL VALLEY RD	SONOMA PL	1	1188-E5	Monday	PACIFIC HIGHLANDS RANCH	Residential	165	31	5115	79					1	1			TYPE I/II.
S2023	SS-031641	WHITE OAK LN	SONOMA PL	BRIARCREST PL	1	1188-E6	Monday	PACIFIC HIGHLANDS RANCH	Residential	270	31	8370	129					1	1			TYPE I/II.
S2023	SS-028768	WILBEE CT	OVERTON AV	IRVINGTON AV	7	1249-E6	Friday	SERRA MESA	Residential	220	33	7260										TYPE I/II. NO CRACK SEAL.
S2023	SS-028767	WILBEE CT	IRVINGTON AV	HUNTINGTON AV	7	1249-E6	Friday	SERRA MESA	Residential	248	33	8184										TYPE I/II. NO CRACK SEAL.
S2023	SS-028933	WINDSWEEP TR	LANDFAIR RD	END	1	1188-A4	Monday	CARMEL VALLEY	Residential	330	31	10230	157		14.89							TYPE I/II.
S2023	SS-029010	WISPERING WOODS CT	CHAPARRAL RIDGE RD	END	1	1188-C5	Monday	CARMEL VALLEY	Residential	350	32	11200	172									TYPE I/II.

**APPENDIX H**  
**OVERALL LOCATION MAP**



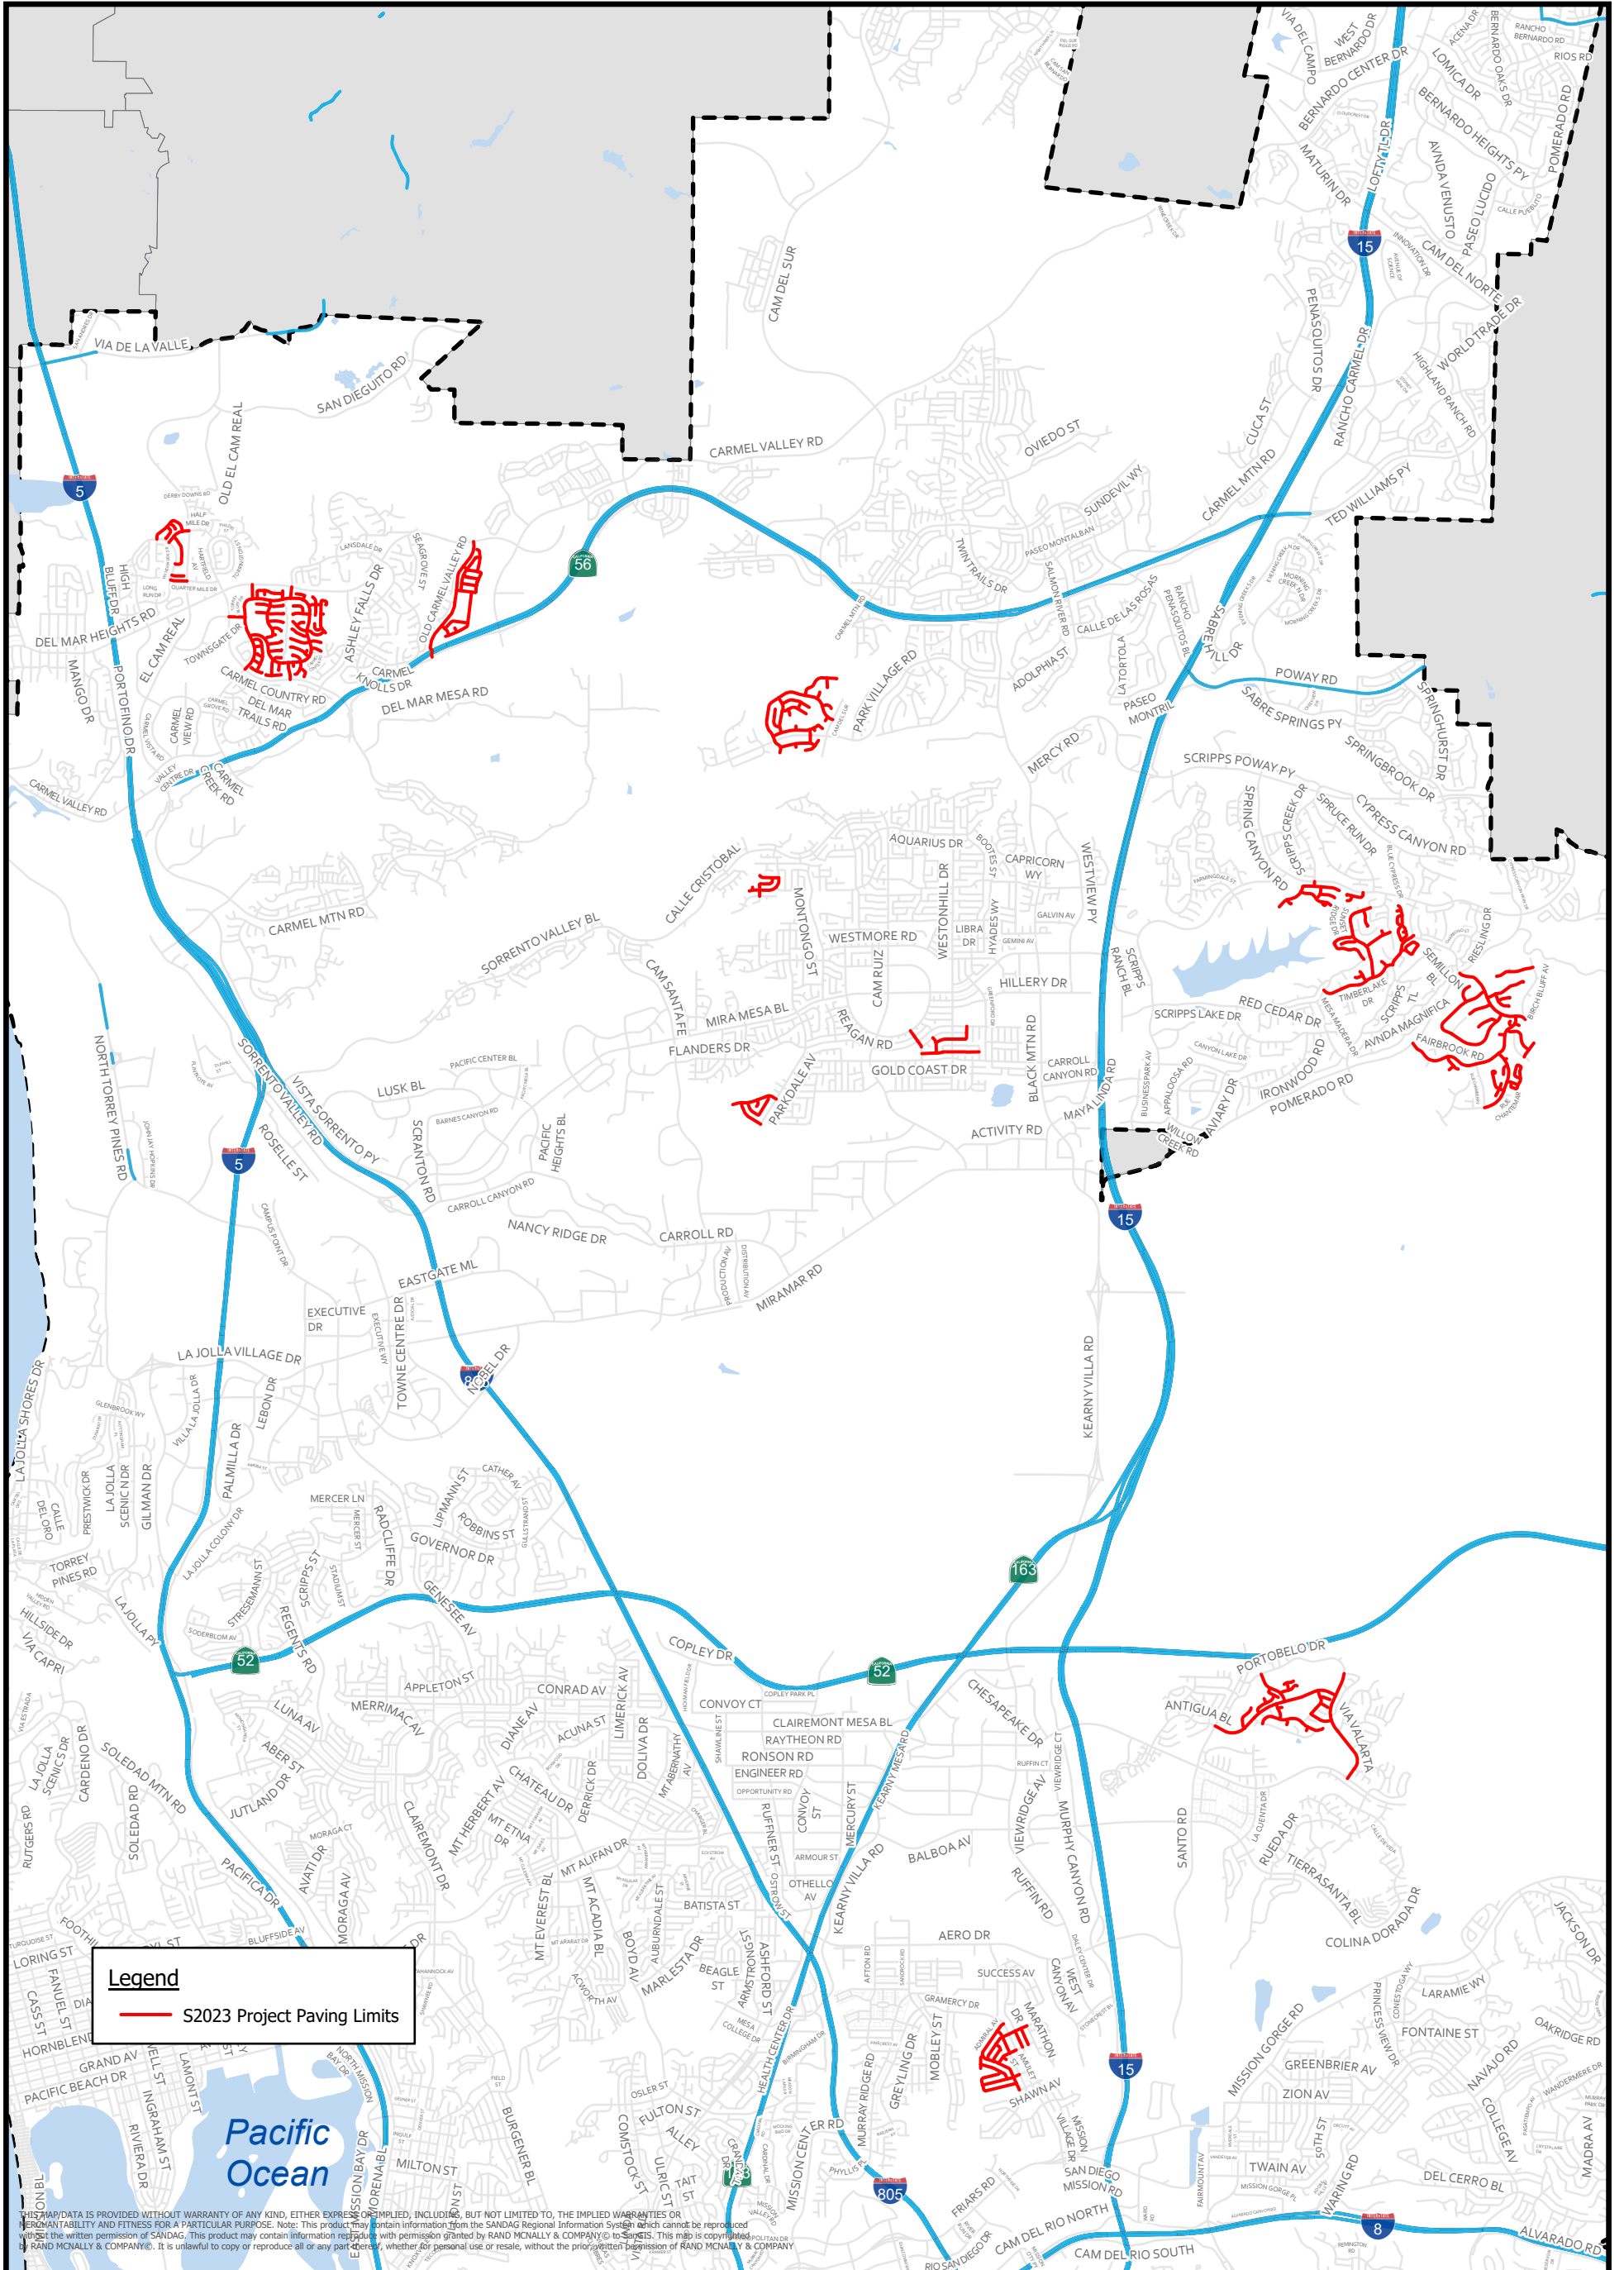




**APPENDIX I**  
**RESURFACING LIMIT MAPS**



Slurry Seal Group 2023

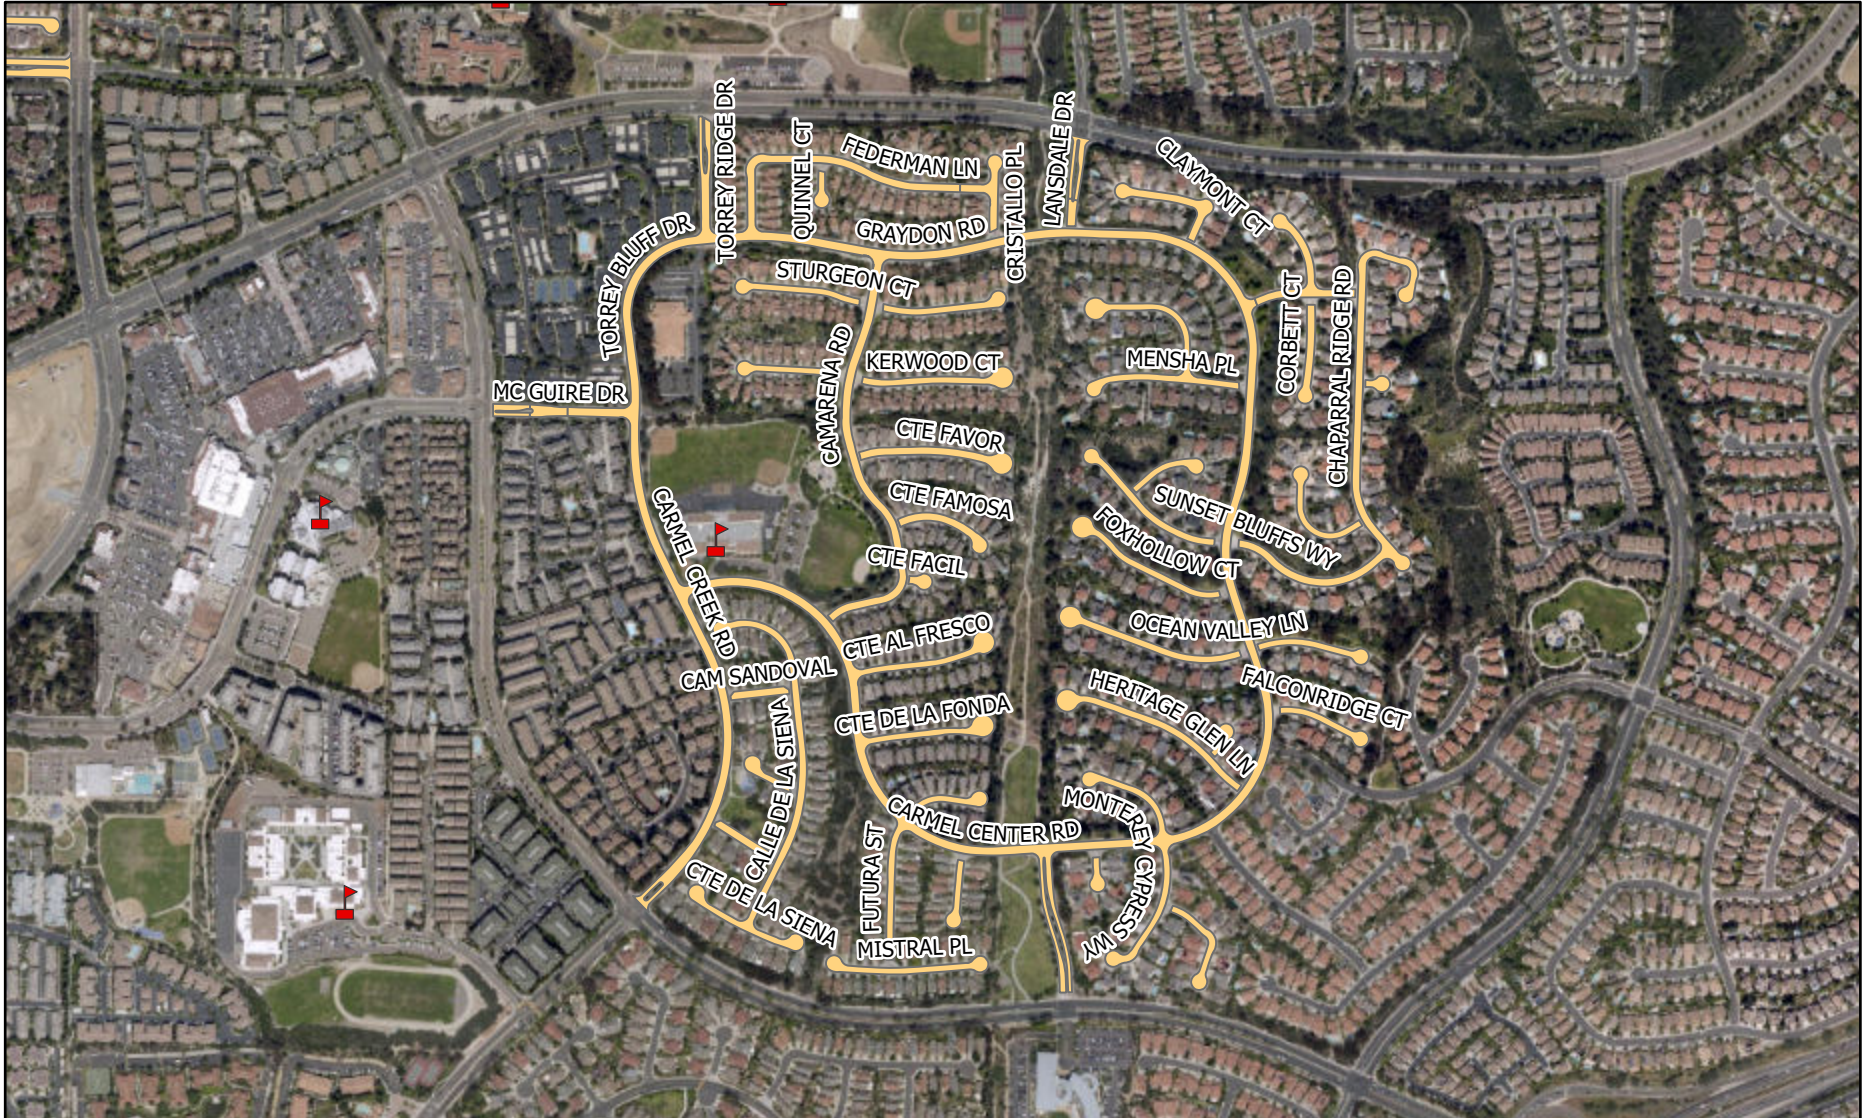COMMUNITY: CARMEL VALLEY



-  Schools
-  S2023 Resurfacing Limits



THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.



Slurry Seal Group 2023

COMMUNITY: MIRA MESA



Schools



S2023 Resurfacing Limits





THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.




Slurry Seal Group 2023

COMMUNITY: MIRA MESA



-  Schools
-  S2023 Resurfacing Limits





THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.



Slurry Seal Group 2023

COMMUNITY: MIRA MESA



-  Schools
-  S2023 Resurfacing Limits





THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.




**Slurry Seal Group 2023**

COMMUNITY: TIERRASANTA



-  Schools
-  S2023 Resurfacing Limits






THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.



Slurry Seal Group 2023

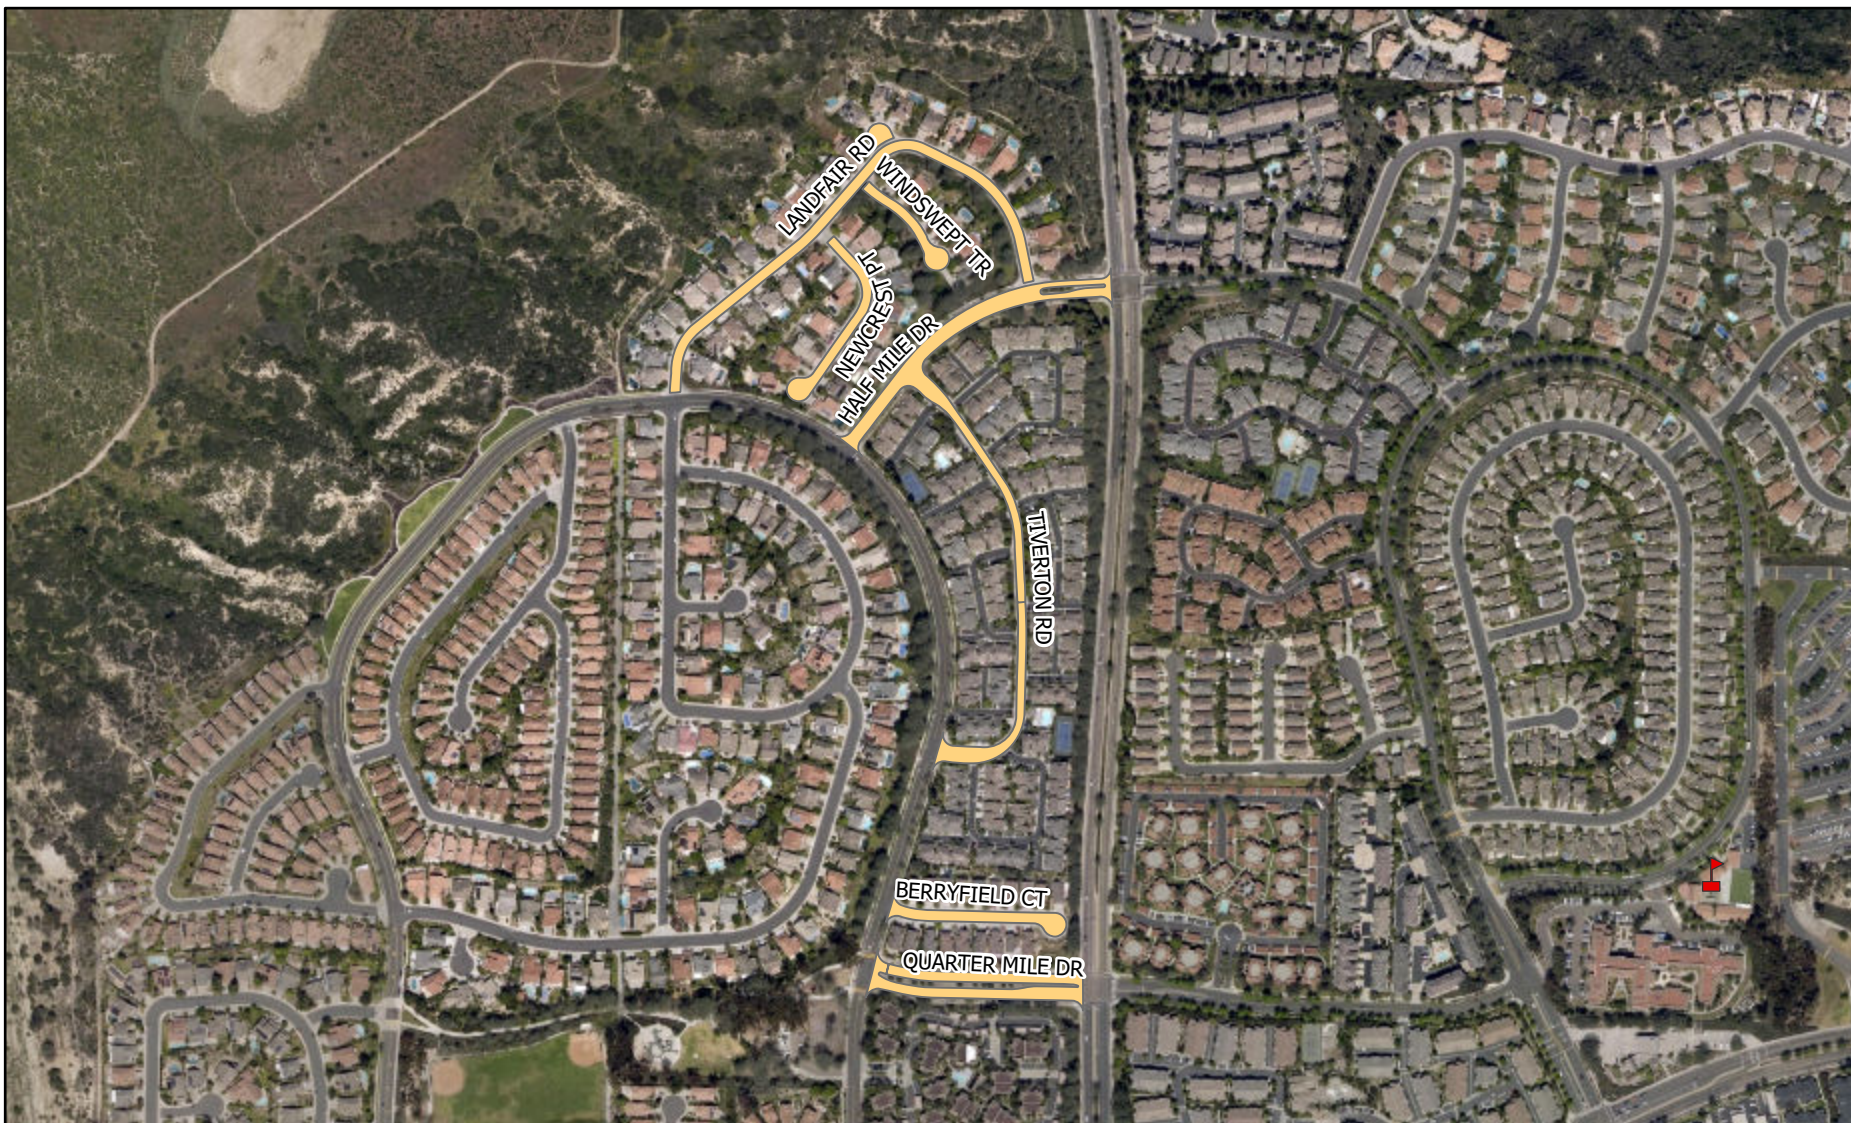COMMUNITY: CARMEL VALLEY



-  Schools
-  S2023 Resurfacing Limits






THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.




**Slurry Seal Group 2023**

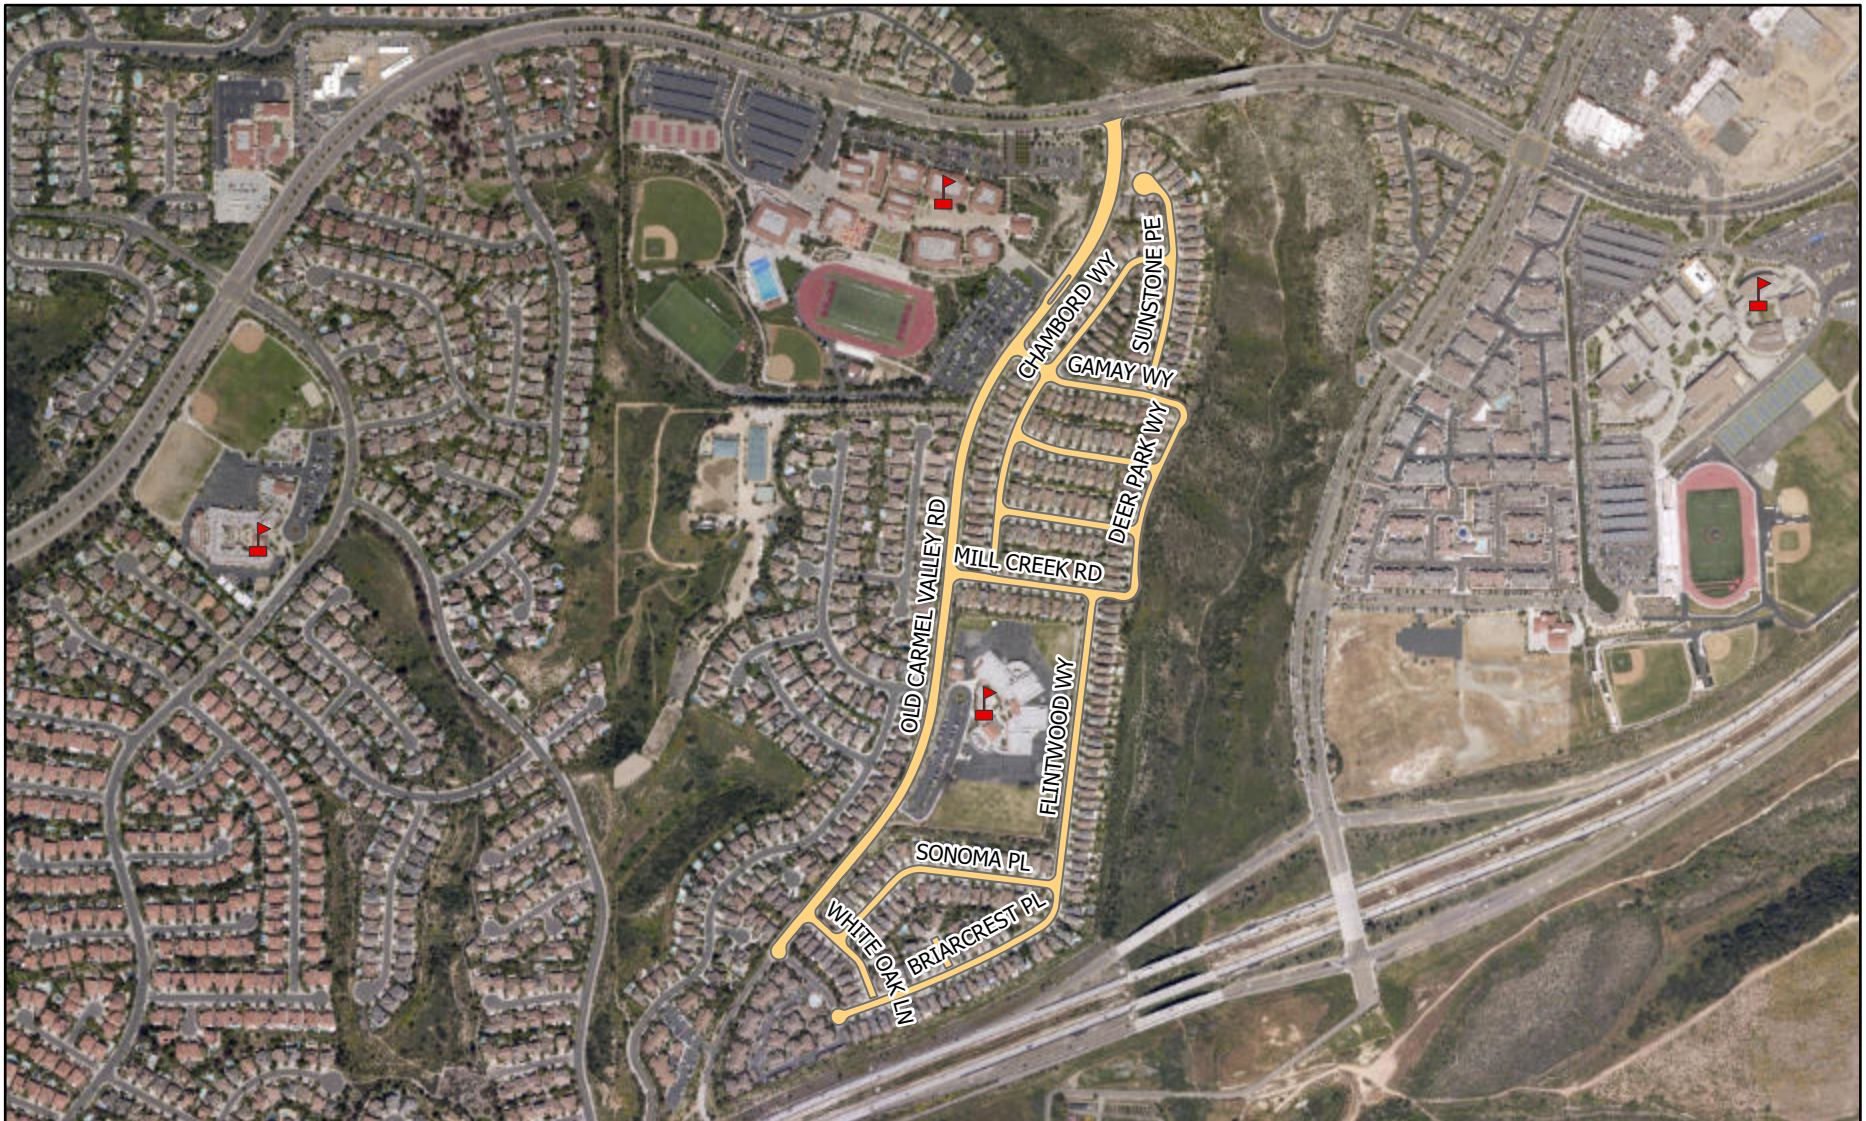COMMUNITY: CARMEL VALLEY



-  Schools
-  S2023 Resurfacing Limits






THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.




Slurry Seal Group 2023

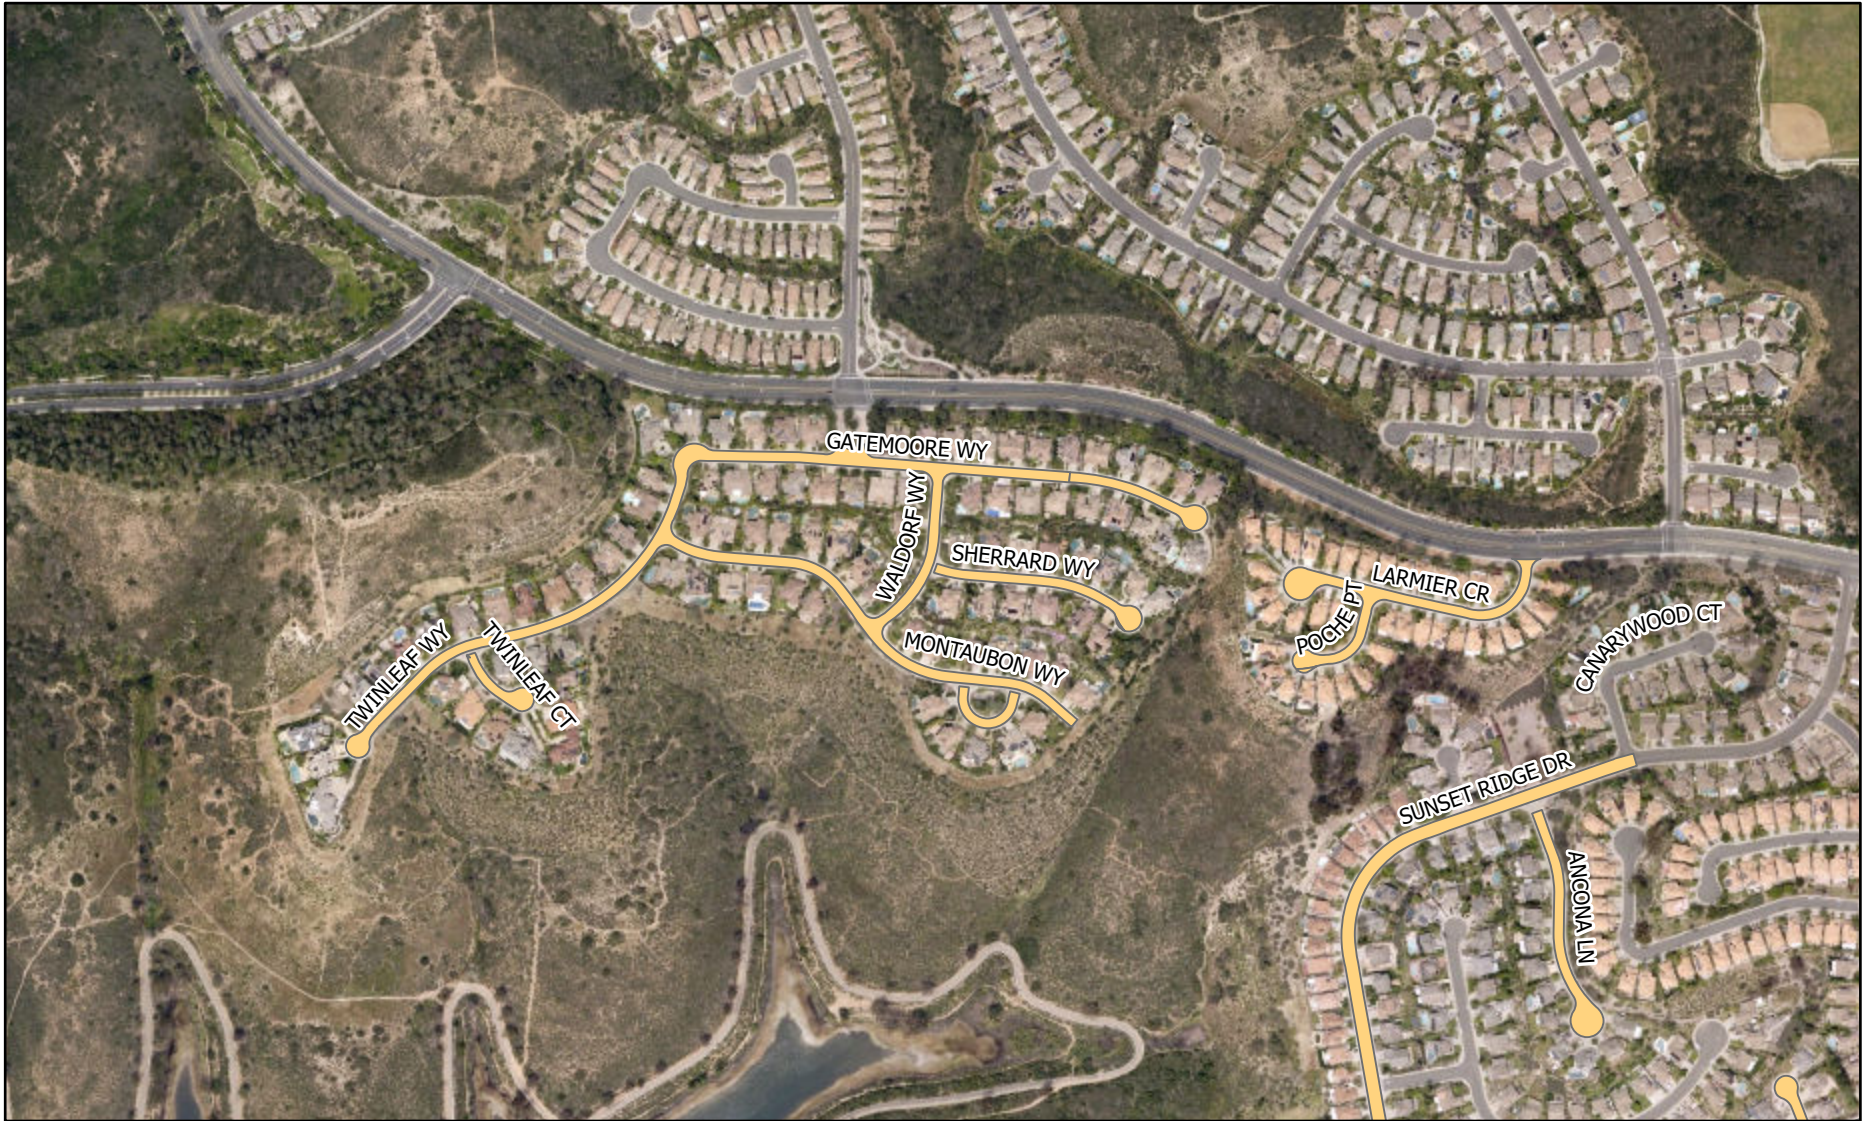COMMUNITY: SCRIPPS MIRAMAR RANCH



-  Schools
-  S2023 Resurfacing Limits





THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.




Slurry Seal Group 2023

COMMUNITY: SERRA MESA



-  Schools
-  S2023 Resurfacing Limits






THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.




**Slurry Seal Group 2023**

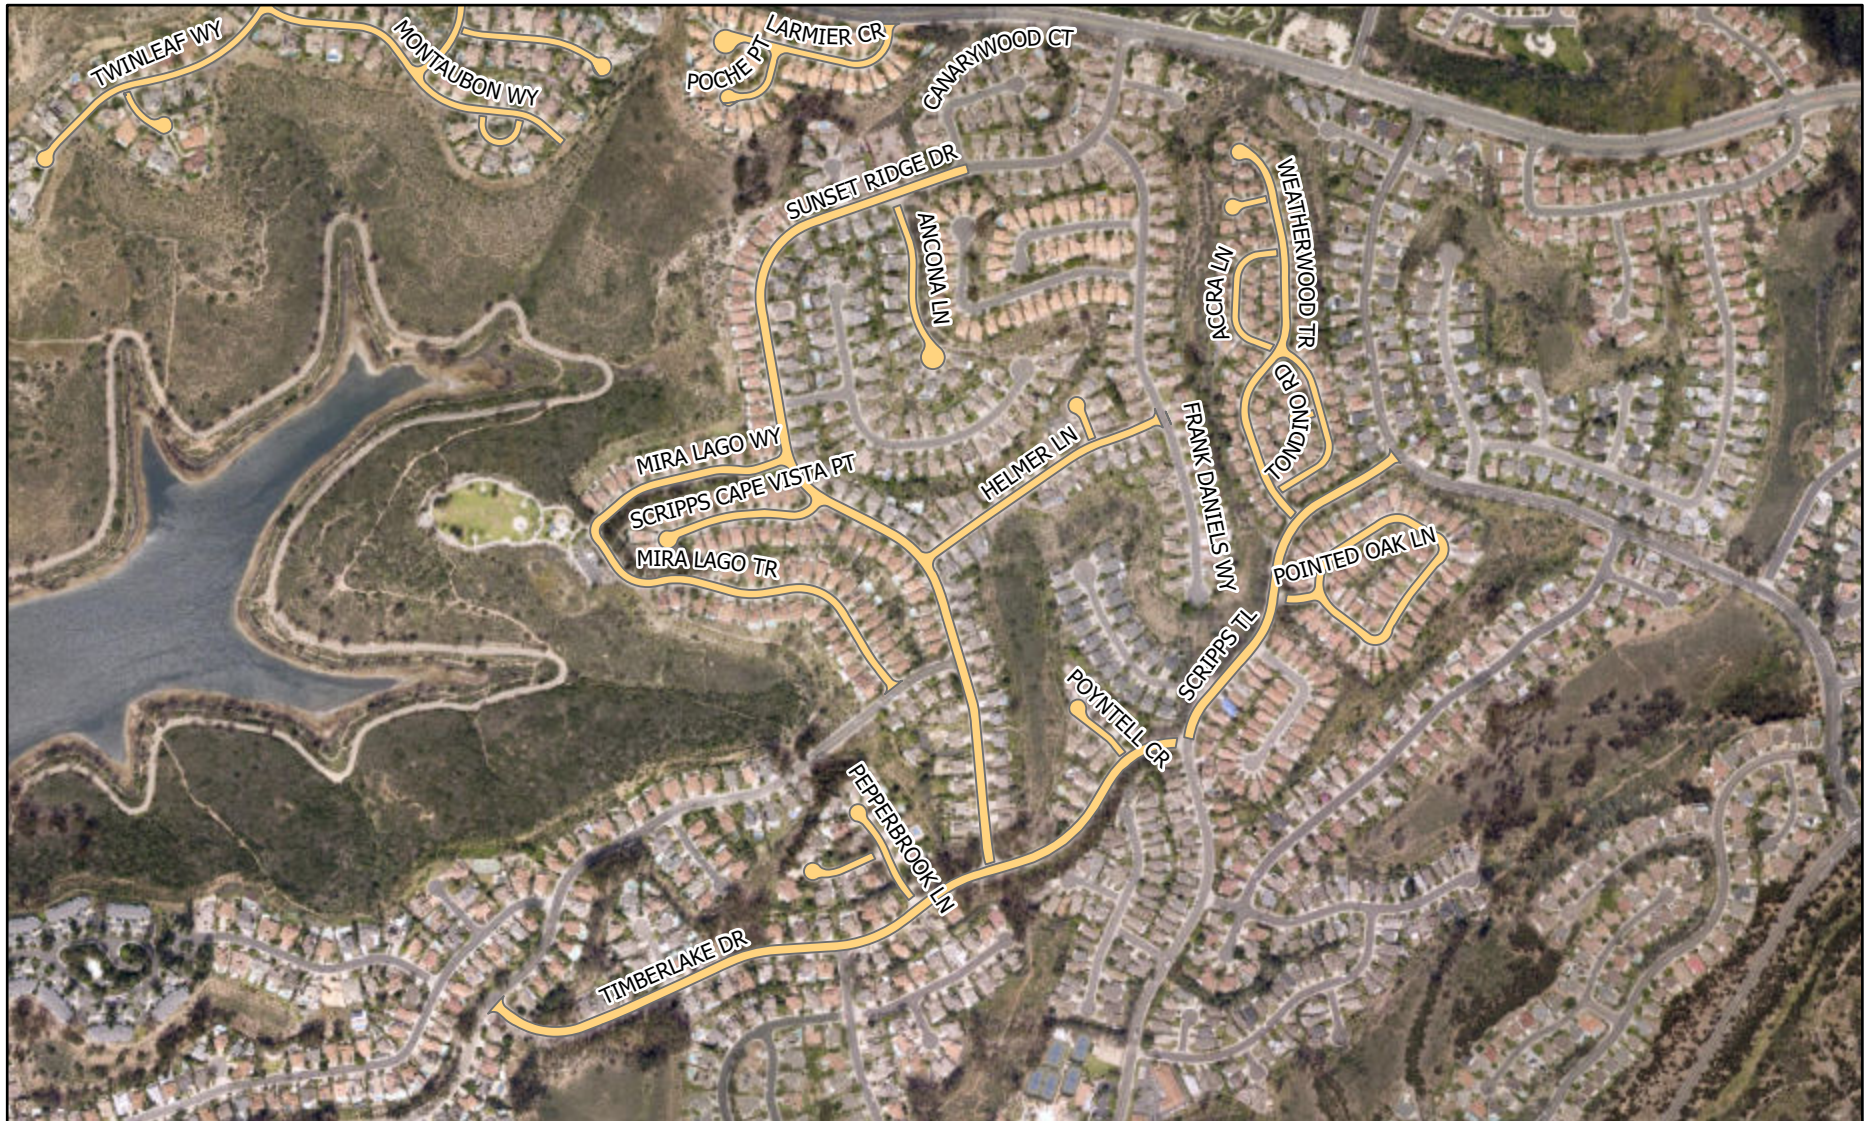COMMUNITY: SCRIPPS MIRAMAR RANCH



-  Schools
-  S2023 Resurfacing Limits





THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.



**Slurry Seal Group 2023**

COMMUNITY: RANCHO PENASQUITOS



-  Schools
-  S2023 Resurfacing Limits





THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.



**Slurry Seal Group 2023**

COMMUNITY: MILITARY FACILITIES



-  Schools
-  S2023 Resurfacing Limits






THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.




Slurry Seal Group 2023

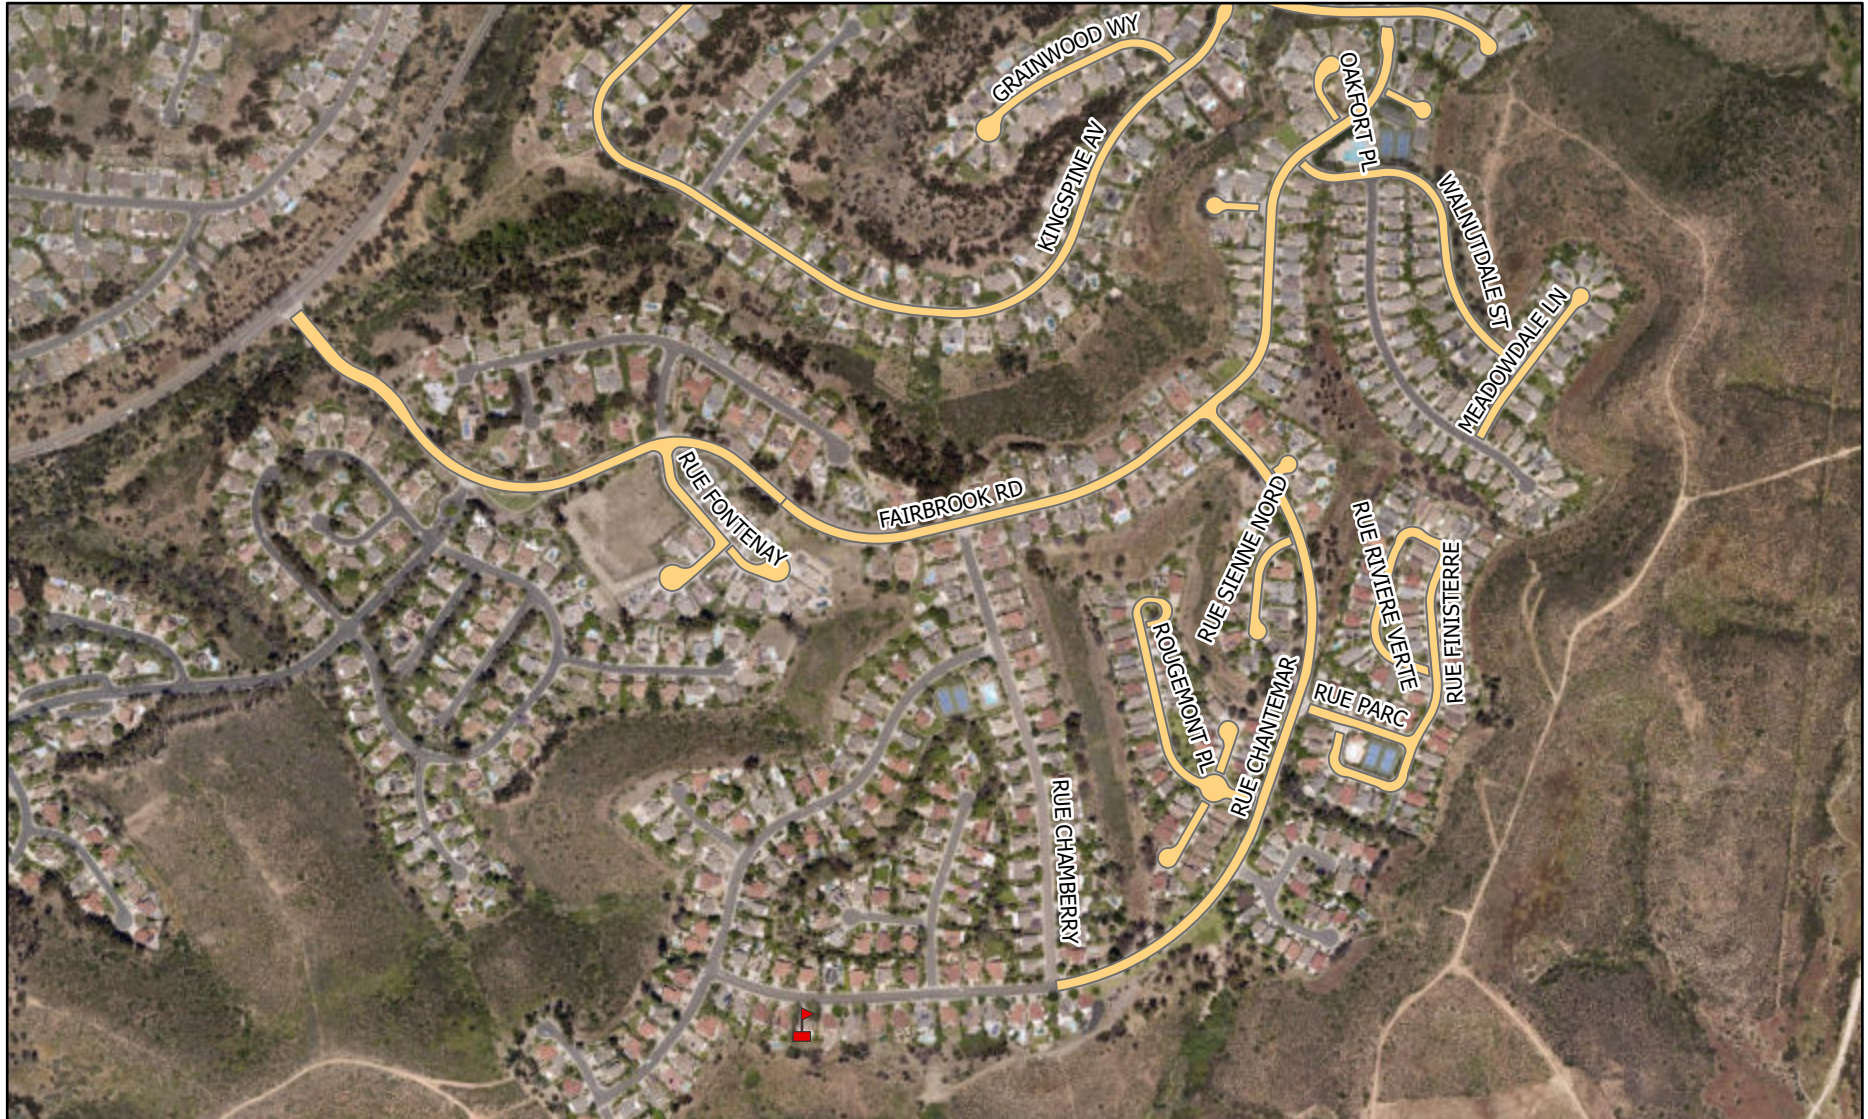COMMUNITY: MILITARY FACILITIES



-  Schools
-  S2023 Resurfacing Limits



THIS MAP/DATA IS PROVIDED WITHOUT WARRANTY OF ANY KIND, EITHER EXPRESS OR IMPLIED, INCLUDING, BUT NOT LIMITED TO, THE IMPLIED WARRANTIES OR MERCHANTABILITY AND FITNESS FOR A PARTICULAR PURPOSE. Note: This product may contain information reproduced with permission granted by RAND MCNALLY & COMPANY to SanGIS. This map is copyrighted by RAND MCNALLY & COMPANY. It is unlawful to copy or reproduce all or any part thereof, whether for personal use or resale, without the prior, written permission of RAND MCNALLY & COMPANY.

**APPENDIX J**  
**PROJECT STREET LIST**

**Slurry Seal Group 2023  
Project Street List**

Segment ID	Street Name	Cross Street 1	Cross Street 2	CD	TB Map	Community Planning Area	Functional Classification
SS-001660	ACCRA LN	TONDINO RD	WEATHERWOOD TR	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-001811	ADMIRAL AV	BEGIN	EPAULETTE ST	7	1249-E6	SERRA MESA	Residential
SS-001809	ADMIRAL AV	AMULET ST	MELBOURNE DR	7	1249-E5	SERRA MESA	Residential
SS-001808	ADMIRAL AV	MELBOURNE DR	MISSION VILAGE DR	7	1249-E5	SERRA MESA	Residential
SS-001810	ADMIRAL AV	EPAULETTE ST	AMULET ST	7	1249-E6	SERRA MESA	Residential
SS-001833	AEGEAN CT	ALONDA WY	ANDASOL ST	6	1209-A2	MIRA MESA	Residential
SS-001832	AEGEAN CT	BEGIN	ALONDA WY	6	1209-A2	MIRA MESA	Residential
SS-002186	ALONDA CT	ANDASOL ST	ALONDA WY	6	1209-A2	MIRA MESA	Residential
SS-002187	ALONDA CT	ROCK CANYON DR	ANDASOL ST	6	1209-A2	MIRA MESA	Residential
SS-002189	ALONDA WY	ALONDA CT	AEGEAN CT	6	1209-A2	MIRA MESA	Residential
SS-002406	AMULET ST	SHAWN AV	OVERTON AV	7	1249-E6	SERRA MESA	Residential
SS-002403	AMULET ST	FORRESTER CT	FERMI AV	7	1249-E6	SERRA MESA	Residential
SS-002402	AMULET ST	FERMI AV	ADMIRAL AV	7	1249-E5	SERRA MESA	Residential
SS-002404	AMULET ST	FULLERTON AV	FORRESTER CT	7	1249-E6	SERRA MESA	Residential
SS-002407	AMULET ST	IRVINGTON AV	FULLERTON AV	7	1249-E6	SERRA MESA	Residential
SS-002405	AMULET ST	OVERTON AV	IRVINGTON AV	7	1249-E6	SERRA MESA	Residential
SS-002420	ANCONA LN	BEGIN	SUNSET RIDGE DR	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-002429	ANDASOL ST	ALONDA CT	ANGELENO RD	6	1209-A2	MIRA MESA	Residential
SS-002427	ANDASOL ST	ANGELENO RD	AEGEAN CT	6	1209-A2	MIRA MESA	Residential
SS-002428	ANDASOL ST	BIRDS VIEW CT	ALONDA CT	6	1208-J2	MIRA MESA	Residential
SS-002430	ANDASOL ST	BEGIN	BIRDS VIEW CT	6	1208-J2	MIRA MESA	Residential
SS-002527	ANTIGUA BL	VILLARRICA WY	CAM PLAYA DE ORO	7	1229-J7	TIERRASANTA	Major
SS-002513	ANTIGUA BL	CALLE MARISELDA	AVNDA PLAYA VERACRUZ	7	1229-H7	TIERRASANTA	Major
SS-002528	ANTIGUA BL	CAM PLAYA ACAPULCO	VILLARRICA WY	7	1229-J7	TIERRASANTA	Major
SS-002505	ANTIGUA BL	CAM PLAYA DE ORO	VIA VALARTA	7	1229-J7	TIERRASANTA	Major
SS-002506	ANTIGUA BL	CAM PLAYA PORTOFINO	CAM PLAYA ACAPULCO	7	1229-J7	TIERRASANTA	Major
SS-002507	ANTIGUA BL	AVNDA PLAYA VERACRUZ	CAM PLAYA PORTOFINO	7	1229-H7	TIERRASANTA	Major
SS-002529	ANTIGUA BL	SANTO RD	CALLE MARISELDA	7	1229-H7	TIERRASANTA	Major
SS-002622	ARBORLAKE WY	POINTED OAK LN	POINTED OAK LN	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-003600	BARON DR	FRIANT ST	HEBRIDES DR	6	1209-C4	MIRA MESA	Residential
SS-003601	BARON DR	PAGODA WY	FRIANT ST	6	1209-C4	MIRA MESA	Residential
SS-004107	BERRYFIELD CT	WYNDHAVEN DR	END	1	1188-A5	CARMEL VALLEY	Residential
SS-004255	BIRCH GLEN CT	BEGIN	PEPPERBROOK LN	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-004288	BIRDS VIEW CT	ANDASOL ST	END	6	1208-J2	MIRA MESA	Residential
SS-004373	BLACK PINE PL	CHAPARRAL RIDGE RD	END	1	1188-C5	CARMEL VALLEY	Residential
SS-031642	BRIARCREST PL	BEGIN	WHITE OAK LN	1	1188-E6	PACIFIC HIGHLANDS RANCH	Residential
SS-031644	BRIARCREST PL	VINWOOD CT	FLINTWOOD WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031643	BRIARCREST PL	WHITE OAK LN	VINWOOD CT	1	1188-E6	PACIFIC HIGHLANDS RANCH	Residential
SS-004890	BRIGHTON RIDGE CT	HELMER LN	END	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-004984	BRONX PL	BEGIN	FULLERTON AV	7	1249-E5	SERRA MESA	Residential
SS-005488	CALLE DE LA SIENA	CAM SANDOVAL	END	1	1188-B6	CARMEL VALLEY	Residential
SS-005491	CALLE DE LA SIENA	CTE DE LA SIENA	PASEO MONTANAS	1	1188-B6	CARMEL VALLEY	Residential
SS-005490	CALLE DE LA SIENA	PASEO MONTANAS	PLAZA DE LA SIENA	1	1188-B6	CARMEL VALLEY	Residential
SS-005489	CALLE DE LA SIENA	PLAZA DE LA SIENA	CAM SANDOVAL	1	1188-B6	CARMEL VALLEY	Residential
SS-005566	CALLE MARISELDA	ANTIGUA BL	END	7	1229-H7	TIERRASANTA	Local
SS-005841	CAM PLAYA ACAPULCO	CTE PLAYA MAZATLAN	ANTIGUA BL	7	1229-J7	TIERRASANTA	Local
SS-005842	CAM PLAYA ACAPULCO	CAM PLAYA MALAGA	CTE PLAYA MAZATLAN	7	1229-J7	TIERRASANTA	Local
SS-005843	CAM PLAYA AZUL	CAM PLAYA CARMEL	CTE PLAYA MERIDA	7	1229-J7	TIERRASANTA	Local
SS-005847	CAM PLAYA CARMEL	VILLARRICA WY	CAM PLAYA AZUL	7	1229-J7	TIERRASANTA	Local
SS-005846	CAM PLAYA CARMEL	CAM PLAYA AZUL	END	7	1229-J7	TIERRASANTA	Local
SS-005852	CAM PLAYA DE ORO	CTE PLAYA MADERA	CTE PLAYA AZTECA	7	1229-J7	TIERRASANTA	Local
SS-005853	CAM PLAYA DE ORO	CTE PLAYA CORONA	CTE PLAYA MADERA	7	1229-J7	TIERRASANTA	Local
SS-005854	CAM PLAYA DE ORO	CAM PLAYA NORTE	CTE PLAYA CORONA	7	1229-J7	TIERRASANTA	Local
SS-005857	CAM PLAYA DE ORO	CTE PLAYA AZTECA	ANTIGUA BL	7	1229-J7	TIERRASANTA	Local
SS-005862	CAM PLAYA MALAGA	AVNDA PLAYA VERACRUZ	CTE PLAYA TOLUCA	7	1229-J7	TIERRASANTA	Local
SS-005860	CAM PLAYA MALAGA	CAM PLAYA ACAPULCO	CTE PLAYA TAMPICO	7	1229-J7	TIERRASANTA	Local
SS-005859	CAM PLAYA MALAGA	CTE PLAYA SOLANA	CAM PLAYA ACAPULCO	7	1229-J7	TIERRASANTA	Local
SS-005858	CAM PLAYA MALAGA	CTE PLAYA TOLUCA	CTE PLAYA SOLANA	7	1229-J7	TIERRASANTA	Local
SS-005864	CAM PLAYA MALAGA	CTE PLAYA DE CASTILA	AVNDA PLAYA VERACRUZ	7	1229-J7	TIERRASANTA	Local
SS-005863	CAM PLAYA MALAGA	CAM PLAYA DE ORO	CTE PLAYA DE CASTILA	7	1229-J7	TIERRASANTA	Local
SS-005865	CAM PLAYA MALAGA	AVNDA PLAYA VERACRUZ	END	7	1229-J7	TIERRASANTA	Local
SS-005861	CAM PLAYA MALAGA	CTE PLAYA TAMPICO	CAM PLAYA DE ORO	7	1229-J7	TIERRASANTA	Local
SS-005866	CAM PLAYA NORTE	CAM PLAYA DE ORO	VIA VALARTA	7	1229-J7	TIERRASANTA	Local
SS-005867	CAM PLAYA PORTOFINO	CTE PLAYA MAJORCA	CTE PLAYA BARCELONA	7	1229-J7	TIERRASANTA	Local
SS-005868	CAM PLAYA PORTOFINO	ANTIGUA BL	CTE PLAYA MAJORCA	7	1229-H7	TIERRASANTA	Local
SS-005911	CAM SANDOVAL	CARMEL CREEK RD	CALLE DE LA SIENA	1	1188-B6	CARMEL VALLEY	Residential
SS-005943	CAMARENA RD	CARMEL CENTER RD	CTE FACIL	1	1188-B6	CARMEL VALLEY	Major
SS-005940	CAMARENA RD	CTE FAVOR	KERWOOD CT	1	1188-B5	CARMEL VALLEY	Major
SS-005939	CAMARENA RD	KERWOOD CT	STURGEON CT	1	1188-B5	CARMEL VALLEY	Major
SS-005938	CAMARENA RD	STURGEON CT	GRAYDON RD	1	1188-B5	CARMEL VALLEY	Major
SS-005941	CAMARENA RD	CTE FAMOSA	CTE FAVOR	1	1188-B6	CARMEL VALLEY	Major
SS-005942	CAMARENA RD	CTE FACIL	CTE FAMOSA	1	1188-B6	CARMEL VALLEY	Major
SS-006153	CANRIGHT WY	KAUFMAN WY	NORTHTRUP DR	6	1209-A5	MIRA MESA	Residential
SS-006362	CARMEL CENTER RD	MONTREY CYPRESS WY	INTERMEZZO WY	1	1188-C6	CARMEL VALLEY	Major
SS-006356	CARMEL CENTER RD	FALCONRIDGE CT	OCEAN VALLEY LN	1	1188-C6	CARMEL VALLEY	Major
SS-006358	CARMEL CENTER RD	CARMEL KNOLLS DR	FALCONRIDGE CT	1	1188-C6	CARMEL VALLEY	Major
SS-006355	CARMEL CENTER RD	CAMARENA RD	CTE AL FRESCO	1	1188-B6	CARMEL VALLEY	Major
SS-006353	CARMEL CENTER RD	CARMEL CREEK RD	CAMARENA RD	1	1188-B6	CARMEL VALLEY	Major
SS-006366	CARMEL CENTER RD	SUNSET BLUFFS WY	MENSHA PL	1	1188-C5	CARMEL VALLEY	Major



**Slurry Seal Group 2023  
Project Street List**

Segment ID	Street Name	Cross Street 1	Cross Street 2	CD	TB Map	Community Planning Area	Functional Classification
SS-006360	CARMEL CENTER RD	INTERMEZZO WY	HERITAGE GLEN LN	1	1188-C6	CARMEL VALLEY	Major
SS-006359	CARMEL CENTER RD	HERITAGE GLEN LN	CARMEL KNOLLS DR	1	1188-C6	CARMEL VALLEY	Major
SS-006357	CARMEL CENTER RD	CTE AL FRESCO	CTE DE LA FONDA	1	1188-B6	CARMEL VALLEY	Major
SS-006352	CARMEL CENTER RD	FOXHOLLOW CT	SUNSET BLUFFS WY	1	1188-C6	CARMEL VALLEY	Major
SS-006361	CARMEL CENTER RD	CTE DE LA FONDA	FUTURA ST	1	1188-B6	CARMEL VALLEY	Major
SS-006351	CARMEL CENTER RD	MENSHA PL	GRAYDON RD	1	1188-C5	CARMEL VALLEY	Major
SS-006367	CARMEL CENTER RD	LUPITA CT	CARMEL MISSION RD	1	1188-B6	CARMEL VALLEY	Major
SS-006364	CARMEL CENTER RD	CARMEL MISSION RD	LONE CYPRESS PL	1	1188-B6	CARMEL VALLEY	Major
SS-006365	CARMEL CENTER RD	FUTURA ST	LUPITA CT	1	1188-B6	CARMEL VALLEY	Major
SS-006363	CARMEL CENTER RD	LONE CYPRESS PL	MONTEREY CYPRESS WY	1	1188-B6	CARMEL VALLEY	Major
SS-006354	CARMEL CENTER RD	OCEAN VALLEY LN	FOXHOLLOW CT	1	1188-C6	CARMEL VALLEY	Major
SS-006380	CARMEL CREEK RD	VIA CANDIDIZ	CARMEL CENTER RD	1	1188-B6	CARMEL VALLEY	Major
SS-006382	CARMEL CREEK RD	CARMEL COUNTRY RD	PASEO MONTANAS	1	1188-B6	CARMEL VALLEY	Major
SS-006387	CARMEL CREEK RD	CARMEL CENTER RD	MC GUIRE DR	1	1188-B6	CARMEL VALLEY	Major
SS-006381	CARMEL CREEK RD	CAM SANDOVAL	VIA CANDIDIZ	1	1188-B6	CARMEL VALLEY	Major
SS-006388	CARMEL CREEK RD	PASEO MONTANAS	CAM SANDOVAL	1	1188-B6	CARMEL VALLEY	Major
SS-006410	CARMEL MISSION RD	CARMEL COUNTRY RD	CARMEL CENTER RD	1	1188-B6	CARMEL VALLEY	Major
SS-031701	CHAMBORD WY	PORTER CREEK RD	GAMAY WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031700	CHAMBORD WY	RABBIT RIDGE RD	PORTER CREEK RD	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031699	CHAMBORD WY	MILL CREEK RD	RABBIT RIDGE RD	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031706	CHAMBORD WY	GAMAY WY	SUNSTONE PE	1	1188-E4	PACIFIC HIGHLANDS RANCH	Residential
SS-006934	CHAPARAL VALLEY CT	BEGIN	SYCAMORE RIDGE CT	5	1210-C3	SCRIPPS MIRAMAR RANCH	Residential
SS-006933	CHAPARAL VALLEY CT	SYCAMORE RIDGE CT	EDENOAKS ST	5	1210-C3	SCRIPPS MIRAMAR RANCH	Residential
SS-006935	CHAPARRAL RIDGE RD	TIMBER RIDGE RD	WISPERING WOODS CT	1	1188-C5	CARMEL VALLEY	Residential
SS-006938	CHAPARRAL RIDGE RD	BEGIN	SUNSET BLUFFS WY	1	1188-C6	CARMEL VALLEY	Residential
SS-006936	CHAPARRAL RIDGE RD	BLACK PINE PL	TIMBER RIDGE RD	1	1188-C5	CARMEL VALLEY	Residential
SS-006939	CHAPARRAL RIDGE RD	SADDLE MTN CT	BLACK PINE PL	1	1188-C5	CARMEL VALLEY	Residential
SS-006937	CHAPARRAL RIDGE RD	SUNSET BLUFFS WY	SADDLE MTN CT	1	1188-C6	CARMEL VALLEY	Residential
SS-007204	CICADA CT	DORMOUSE RD	END	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-007358	CLAYMONT CT	GRAYDON RD	END	1	1188-C5	CARMEL VALLEY	Residential
SS-007928	CORBETT CT	TIMBER RIDGE RD	END	1	1188-C5	CARMEL VALLEY	Residential
SS-007929	CORBETT CT	BEGIN	TIMBER RIDGE RD	1	1188-C5	CARMEL VALLEY	Residential
SS-008268	CRISTALLO PL	GRAYDON RD	FEDERMAN LN	1	1188-B5	CARMEL VALLEY	Residential
SS-008267	CRISTALLO PL	FEDERMAN LN	END	1	1188-B5	CARMEL VALLEY	Residential
SS-008327	CTE AL FRESCO	CARMEL CENTER RD	END	1	1188-B6	CARMEL VALLEY	Residential
SS-008343	CTE DE LA FONDA	CARMEL CENTER RD	END	1	1188-B6	CARMEL VALLEY	Residential
SS-008344	CTE DE LA SIENA	BEGIN	CALLE DE LA SIENA	1	1188-B6	CARMEL VALLEY	Residential
SS-008345	CTE DE LA SIENA	CALLE DE LA SIENA	END	1	1188-B6	CARMEL VALLEY	Residential
SS-008351	CTE FACIL	CAMARENA RD	END	1	1188-B6	CARMEL VALLEY	Residential
SS-008352	CTE FAMOSA	CAMARENA RD	END	1	1188-B6	CARMEL VALLEY	Residential
SS-008353	CTE FAVOR	CAMARENA RD	END	1	1188-B5	CARMEL VALLEY	Residential
SS-008374	CTE PLAYA AZTECA	CAM PLAYA DE ORO	END	7	1229-J7	TIERRASANTA	Local
SS-008375	CTE PLAYA BARCELONA	VILLARRICA WY	CAM PLAYA PORTOFINO	7	1229-J7	TIERRASANTA	Local
SS-008376	CTE PLAYA BARCELONA	CAM PLAYA PORTOFINO	END	7	1229-J7	TIERRASANTA	Local
SS-008382	CTE PLAYA DE CASTILA	BEGIN	CAM PLAYA MALAGA	7	1229-J7	TIERRASANTA	Local
SS-008388	CTE PLAYA MADERA	CAM PLAYA DE ORO	END	7	1229-J7	TIERRASANTA	Local
SS-008389	CTE PLAYA MAJORCA	BEGIN	CAM PLAYA PORTOFINO	7	1229-J7	TIERRASANTA	Local
SS-008390	CTE PLAYA MAZATLAN	CAM PLAYA ACAPULCO	END	7	1229-J7	TIERRASANTA	Local
SS-008391	CTE PLAYA MERIDA	CAM PLAYA AZUL	END	7	1229-J7	TIERRASANTA	Local
SS-008392	CTE PLAYA MERIDA	BEGIN	CAM PLAYA AZUL	7	1229-J7	TIERRASANTA	Local
SS-008397	CTE PLAYA TAMPICO	CAM PLAYA MALAGA	END	7	1229-J7	TIERRASANTA	Local
SS-008542	CYPRESS GLEN PL	MONTEREY CYPRESS WY	END	1	1188-C6	CARMEL VALLEY	Residential
SS-031697	DEER PARK WY	RABBIT RIDGE RD	PORTER CREEK RD	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031698	DEER PARK WY	PORTER CREEK RD	GAMAY WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031696	DEER PARK WY	MILL CREEK RD	RABBIT RIDGE RD	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-009380	DORMOUSE CT	DORMOUSE RD	END	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009383	DORMOUSE RD	DORMOUSE CT	CICADA CT	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009382	DORMOUSE RD	ECLIPSE RD	DORMOUSE CT	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009384	DORMOUSE RD	CICADA CT	RUFUS CT	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009387	DORMOUSE RD	PARK VILLAGE RD	PIPIT PL	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-009385	DORMOUSE RD	RUFUS CT	CAM DEL SUR	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-009381	DORMOUSE RD	SALVIA WY	ECLIPSE RD	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009386	DORMOUSE RD	PIPIT PL	SALVIA WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-009389	DORMOUSE RD	BEGIN	SALIX PL	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-009388	DORMOUSE RD	SALIX PL	PARK VILLAGE RD	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-009870	ECLIPSE PL	BEGIN	ECLIPSE RD	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009871	ECLIPSE RD	ECLIPSE PL	END	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009872	ECLIPSE RD	DORMOUSE RD	ECLIPSE PL	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-009883	EDENOAKS ST	CHAPARAL VALLEY CT	END	5	1210-C3	SCRIPPS MIRAMAR RANCH	Residential
SS-009884	EDENOAKS ST	SEMILLON BL	CHAPARAL VALLEY CT	5	1210-C3	SCRIPPS MIRAMAR RANCH	Residential
SS-010399	EPAULETTE ST	HUNTINGTON AV	ADMIRAL AV	7	1249-E6	SERRA MESA	Residential
SS-010400	EPAULETTE ST	IRVINGTON AV	HUNTINGTON AV	7	1249-E6	SERRA MESA	Residential
SS-010759	FAIRBROOK RD	OAKFORT CT	SEMILLON BL	5	1210-C4	SCRIPPS MIRAMAR RANCH	Prime
SS-031972	FAIRBROOK RD	CAMTO MAGNIFICA	RUE FONTENAY	5	1210-B4	SCRIPPS MIRAMAR RANCH	Prime
SS-010766	FAIRBROOK RD	FAIRBROOK RD	RUE CHAMBERY	5	1210-B4	SCRIPPS MIRAMAR RANCH	Prime
SS-010765	FAIRBROOK RD	POMERADO RD	CAMTO MAGNIFICA	5	1210-B4	SCRIPPS MIRAMAR RANCH	Prime
SS-010762	FAIRBROOK RD	THORNBRUSH CT	WALNUTDALE ST	5	1210-C4	SCRIPPS MIRAMAR RANCH	Major
SS-010763	FAIRBROOK RD	RUE CHANTEMAR	THORNBRUSH CT	5	1210-C4	SCRIPPS MIRAMAR RANCH	Major
SS-010761	FAIRBROOK RD	WALNUTDALE ST	OAKFORT PL	5	1210-C4	SCRIPPS MIRAMAR RANCH	Prime

**Slurry Seal Group 2023  
Project Street List**

Segment ID	Street Name	Cross Street 1	Cross Street 2	CD	TB Map	Community Planning Area	Functional Classification
SS-010760	FAIRBROOK RD	OAKFORT PL	OAKFORT CT	5	1210-C4	SCRIPPS MIRAMAR RANCH	Prime
SS-010764	FAIRBROOK RD	RUE CHAMBERRY	RUE CHANTEMAR	5	1210-C4	SCRIPPS MIRAMAR RANCH	Major
SS-010848	FALCONRIDGE CT	CARMEL CENTER RD	END	1	1188-C6	CARMEL VALLEY	Residential
SS-010964	FEDERMAN LN	PERCY CT	CRISTALLO PL	1	1188-B5	CARMEL VALLEY	Residential
SS-010965	FEDERMAN LN	GRAYDON RD	QUINNEL CT	1	1188-B5	CARMEL VALLEY	Residential
SS-010963	FEDERMAN LN	QUINNEL CT	PERCY CT	1	1188-B5	CARMEL VALLEY	Residential
SS-011042	FERMI AV	MARATHON DR	MARTINDALE CT	7	1249-E5	SERRA MESA	Residential
SS-011043	FERMI AV	MISSION VILLAGE DR	MARATHON DR	7	1249-E5	SERRA MESA	Residential
SS-011046	FERMI AV	AMULET ST	FORRESTER CT	7	1249-E5	SERRA MESA	Residential
SS-011040	FERMI AV	MARTINDALE CT	MONARCH ST	7	1249-E5	SERRA MESA	Residential
SS-011044	FERMI AV	MELBOURNE DR	MISSION VILLAGE DR	7	1249-E5	SERRA MESA	Residential
SS-011045	FERMI AV	FORRESTER CT	MELBOURNE DR	7	1249-E5	SERRA MESA	Residential
SS-011103	FIGTREE ST	BEGIN	FIGTREE CT	5	1210-C3	SCRIPPS MIRAMAR RANCH	Residential
SS-011104	FIGTREE ST	FIGTREE CT	BIRCH BLUFF AV	5	1210-C3	SCRIPPS MIRAMAR RANCH	Residential
SS-031645	FLINTWOOD WY	SONOMA PL	BRIARCREST PL	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-011326	FORRESTER CT	AMULET ST	END	7	1249-E5	SERRA MESA	Residential
SS-011324	FORRESTER CT	BEGIN	FERMI AV	7	1249-E5	SERRA MESA	Residential
SS-011325	FORRESTER CT	BEGIN	END	7	1249-E5	SERRA MESA	Residential
SS-011403	FOXHOLLOW CT	BEGIN	CARMEL CENTER RD	1	1188-C6	CARMEL VALLEY	Residential
SS-011482	FRIANT ST	WESTONHILL DR	ISLEWORTH AV	6	1209-D4	MIRA MESA	Residential
SS-011483	FRIANT ST	BARON DR	WESTONHILL DR	6	1209-C4	MIRA MESA	Residential
SS-011652	FULLERTON AV	MELBOURNE DR	MISSION VILLAGE DR	7	1249-E5	SERRA MESA	Residential
SS-011653	FULLERTON AV	BRONX PL	MELBOURNE DR	7	1249-E5	SERRA MESA	Residential
SS-011654	FULLERTON AV	AMULET ST	BRONX PL	7	1249-E6	SERRA MESA	Residential
SS-011669	FUTURA ST	MISTRAL PL	CARMEL CENTER RD	1	1188-B6	CARMEL VALLEY	Residential
SS-011668	FUTURA ST	CARMEL CENTER RD	END	1	1188-B6	CARMEL VALLEY	Residential
SS-031702	GAMAY WY	OLD CARMEL VALLEY RD	CHAMBORD WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031703	GAMAY WY	CHAMBORD WY	SUNSTONE PE	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031707	GAMAY WY	SUNSTONE PE	DEER PARK WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-011913	GATEMOORE WY	SCRIPPS CREEK DR	MONTAUBON WY	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-011914	GATEMOORE WY	SCRIPPS CREEK DR	WALDORF WY	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-011915	GATEMOORE WY	WALDORF WY	END	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-012376	GOLDFISH CT	BEGIN	GOLDFISH WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-012378	GOLDFISH WY	SALVIA WY	GOLDFISH CT	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-012379	GOLDFISH WY	ROAN WY	END	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-012377	GOLDFISH WY	GOLDFISH CT	ROAN WY	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-012463	GRAINWOOD WY	BEGIN	KINGSPINE AV	5	1210-B4	SCRIPPS MIRAMAR RANCH	Residential
SS-012582	GRAYDON RD	LANSDALE DR	CLAYMONT CT	1	1188-B5	CARMEL VALLEY	Major
SS-012580	GRAYDON RD	TORREY BLUFF DR	FEDERMAN LN	1	1188-B5	CARMEL VALLEY	Major
SS-012581	GRAYDON RD	CRISTALLO PL	LANSDALE DR	1	1188-B5	CARMEL VALLEY	Major
SS-012583	GRAYDON RD	FEDERMAN LN	CAMARENA RD	1	1188-B5	CARMEL VALLEY	Major
SS-012584	GRAYDON RD	CAMARENA RD	CRISTALLO PL	1	1188-B5	CARMEL VALLEY	Major
SS-012585	GRAYDON RD	CLAYMONT CT	CARMEL CENTER RD	1	1188-C5	CARMEL VALLEY	Major
SS-012915	HALF MILE DR	LANDFAIR RD	EL CAM REAL	1	1188-A4	CARMEL VALLEY	Major
SS-012918	HALF MILE DR	HIGH BLUFF DR	TIVERTON RD	1	1188-A4	CARMEL VALLEY	Major
SS-012916	HALF MILE DR	TIVERTON RD	LANDFAIR RD	1	1188-A4	CARMEL VALLEY	Major
SS-013307	HELMER LN	BRIGHTON RIDGE CT	FRANK DANIELS WY	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-013308	HELMER LN	SUNSET RIDGE DR	BRIGHTON RIDGE CT	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-013360	HERITAGE GLEN CT	HERITAGE GLEN LN	END	1	1188-C6	CARMEL VALLEY	Residential
SS-013361	HERITAGE GLEN LN	BEGIN	HERITAGE GLEN CT	1	1188-B6	CARMEL VALLEY	Residential
SS-013362	HERITAGE GLEN LN	HERITAGE GLEN CT	CARMEL CENTER RD	1	1188-C6	CARMEL VALLEY	Residential
SS-013893	HUNTINGTON AV	WILBEE CT	EPAULETTE ST	7	1249-E6	SERRA MESA	Residential
SS-014258	IRVINGTON AV	EPAULETTE ST	AMULET ST	7	1249-E6	SERRA MESA	Residential
SS-014257	IRVINGTON AV	AMULET ST	MELBOURNE DR	7	1249-E6	SERRA MESA	Residential
SS-014259	IRVINGTON AV	WILBEE CT	EPAULETTE ST	7	1249-E6	SERRA MESA	Residential
SS-014315	ISLEWORTH AV	FRIANT ST	HEBRIDES DR	6	1209-D4	MIRA MESA	Residential
SS-014314	ISLEWORTH AV	HEBRIDES DR	FLANDERS DR	6	1209-D4	MIRA MESA	Residential
SS-014935	KATYDID CR	SALVIA WY	END	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-014936	KAUFMAN WY	CANRIGHT WY	NORTHROP DR	6	1209-A5	MIRA MESA	Residential
SS-015163	KERWOOD CT	CAMARENA RD	END	1	1188-B5	CARMEL VALLEY	Residential
SS-015162	KERWOOD CT	BEGIN	CAMARENA RD	1	1188-B5	CARMEL VALLEY	Residential
SS-015252	KINGSPINE AV	GRAINWOOD WY	SEMILLON BL	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-015254	KINGSPINE AV	BARRYWOOD WY	GRAINWOOD WY	5	1210-B4	SCRIPPS MIRAMAR RANCH	Residential
SS-015253	KINGSPINE AV	SPRUCE GROVE AV	BARRYWOOD WY	5	1210-B4	SCRIPPS MIRAMAR RANCH	Residential
SS-015962	LANDFAIR RD	NEWCREST PT	WINDSWPT TR	1	1187-J4	CARMEL VALLEY	Residential
SS-015963	LANDFAIR RD	HIGH BLUFF DR	NEWCREST PT	1	1187-J4	CARMEL VALLEY	Residential
SS-015967	LANDFAIR RD	WINDSWPT TR	HALF MILE DR	1	1188-A4	CARMEL VALLEY	Residential
SS-016040	LANSDALE DR	GRAYDON RD	DEL MAR HEIGHTS RD	1	1188-B5	CARMEL VALLEY	Major
SS-016087	LARMIER CR	BEGIN	POCHE PT	5	1209-J2	SCRIPPS MIRAMAR RANCH	Residential
SS-016088	LARMIER CR	POCHE PT	SPRING CANYON RD	5	1209-J2	SCRIPPS MIRAMAR RANCH	Residential
SS-016370	LICIA WY	SALIX PL	PARK VILLAGE RD	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-016369	LICIA WY	PARK VILLAGE RD	PIPIT PL	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-016619	LIVEWOOD WY	BEGIN	SEMILLON BL	5	1210-B4	SCRIPPS MIRAMAR RANCH	Residential
SS-016809	LONE CYPRESS PL	BEGIN	CARMEL CENTER RD	1	1188-B6	CARMEL VALLEY	Residential
SS-017011	LUPITA CT	BEGIN	CARMEL CENTER RD	1	1188-B6	CARMEL VALLEY	Residential
SS-017449	MARATHON DR	FULLERTON AV	FERMI AV	7	1249-E5	SERRA MESA	Residential
SS-017694	MARTINDALE CT	FULLERTON AV	FERMI AV	7	1249-E5	SERRA MESA	Residential
SS-017853	MC GUIRE DR	CARMEL COUNTRY RD	CARMEL CREEK RD	1	1188-B5	CARMEL VALLEY	Prime
SS-017960	MEADOWDALE LN	WALNUTDALE ST	END	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential

**Slurry Seal Group 2023  
Project Street List**

Segment ID	Street Name	Cross Street 1	Cross Street 2	CD	TB Map	Community Planning Area	Functional Classification
SS-017961	MEADOWDALE LN	PINECASTLE ST	WALNUTDALE ST	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-018006	MELBOURNE DR	FULLERTON AV	FERMI AV	7	1249-E5	SERRA MESA	Residential
SS-018005	MELBOURNE DR	FERMI AV	ADMIRAL AV	7	1249-E5	SERRA MESA	Residential
SS-018074	MENSHA PL	RALSTON CR	CARMEL CENTER RD	1	1188-C5	CARMEL VALLEY	Residential
SS-018075	MENSHA PL	BEGIN	RALSTON CR	1	1188-B5	CARMEL VALLEY	Residential
SS-031695	MILL CREEK RD	FLINTWOOD WY	DEER PARK WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031694	MILL CREEK RD	CHAMBORD WY	FLINTWOOD WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031693	MILL CREEK RD	OLD CARMEL VALLEY RD	CHAMBORD WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-018363	MIRA LAGO TR	SCRIPPS LAKE DR	MIRA LAGO WY	5	1209-J3	SCRIPPS MIRAMAR RANCH	Residential
SS-018364	MIRA LAGO WY	MIRA LAGO TR	SUNSET RIDGE DR	5	1209-J3	SCRIPPS MIRAMAR RANCH	Residential
SS-018670	MISTRAL PL	BEGIN	FUTURA ST	1	1188-B6	CARMEL VALLEY	Residential
SS-018669	MISTRAL PL	FUTURA ST	END	1	1188-B6	CARMEL VALLEY	Residential
SS-018829	MONTAUBON CR	MONTAUBON WY	MONTAUBON WY	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-018831	MONTAUBON WY	MONTAUBON CR	MONTAUBON CR	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-018833	MONTAUBON WY	WALDORF WY	GATEMOORE WY	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-018832	MONTAUBON WY	MONTAUBON CR	END	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-018830	MONTAUBON WY	WALDORF WY	MONTAUBON CR	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-018881	MONTEREY CYPRESS WY	BEGIN	CYPRESS GLEN PL	1	1188-C6	CARMEL VALLEY	Residential
SS-018880	MONTEREY CYPRESS WY	CYPRESS GLEN PL	CARMEL CENTER RD	1	1188-C6	CARMEL VALLEY	Residential
SS-018879	MONTEREY CYPRESS WY	CARMEL CENTER RD	END	1	1188-B6	CARMEL VALLEY	Residential
SS-019832	NEWCREST PT	LANDFAIR RD	END	1	1188-A4	CARMEL VALLEY	Residential
SS-020138	NORTHRUP DR	CANRIGHT WY	PARKDALE AV	6	1209-A5	MIRA MESA	Residential
SS-020143	NORTHRUP DR	BEGIN	OSGOOD WY	6	1208-J5	MIRA MESA	Residential
SS-020139	NORTHRUP DR	NORTHRUP PT	CANRIGHT WY	6	1209-A5	MIRA MESA	Residential
SS-020141	NORTHRUP DR	KAUFMAN WY	NORTHRUP PT	6	1209-A5	MIRA MESA	Residential
SS-020142	NORTHRUP DR	OSGOOD WY	KAUFMAN WY	6	1208-J5	MIRA MESA	Residential
SS-020145	NORTHRUP PT	BEGIN	NORTHRUP DR	6	1209-A5	MIRA MESA	Residential
SS-020231	OAKFORT CT	FAIRBROOK RD	END	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-020232	OAKFORT PL	BEGIN	FAIRBROOK RD	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-020294	OCEAN VALLEY LN	CARMEL CENTER RD	END	1	1188-C6	CARMEL VALLEY	Residential
SS-020295	OCEAN VALLEY LN	BEGIN	CARMEL CENTER RD	1	1188-C6	CARMEL VALLEY	Residential
SS-031648	OLD CARMEL VALLEY RD	SR-56 WB	WHITE OAK LN	1	1188-E6	PACIFIC HIGHLANDS RANCH	Residential
SS-006488	OLD CARMEL VALLEY RD	WHITE OAK LN	SANDOWN WY	1	1188-E6	PACIFIC HIGHLANDS RANCH	Major
SS-031692	OLD CARMEL VALLEY RD	GAMAY WY	DEL MAR HEIGHTS RD	1	1188-E4	PACIFIC HIGHLANDS RANCH	Major
SS-031691	OLD CARMEL VALLEY RD	MILL CREEK RD	GAMAY WY	1	1188-E5	CARMEL VALLEY	Major
SS-031271	OLD CARMEL VALLEY RD	SANDOWN WY	MILL CREEK RD	1	1188-E5	PACIFIC HIGHLANDS RANCH	Major
SS-020728	OSGOOD WY	PARKDALE AV	NORTHRUP DR	6	1208-J6	MIRA MESA	Residential
SS-020813	OVERTON AV	WILBEE CT	AMULET ST	7	1249-E6	SERRA MESA	Residential
SS-020988	PAGODA WY	WESTONHILL DR	GOLD COAST PL	6	1209-D4	MIRA MESA	Residential
SS-020987	PAGODA WY	BELFAST CR	WESTONHILL DR	6	1209-C4	MIRA MESA	Residential
SS-020990	PAGODA WY	SAN RAMON DR	BARON DR	6	1209-C5	MIRA MESA	Residential
SS-020989	PAGODA WY	BARON DR	BELFAST CR	6	1209-C5	MIRA MESA	Residential
SS-021451	PASEO MONTANAS	CARMEL CREEK RD	CALLE DE LA SIENA	1	1188-B6	CARMEL VALLEY	Residential
SS-021641	PEPPERBROOK LN	BIRCH GLEN CT	END	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-021642	PEPPERBROOK LN	TIMBERLAKE DR	BIRCH GLEN CT	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-021813	PINE MEADOW CT	SUNSET BLUFFS WY	END	1	1188-C5	CARMEL VALLEY	Residential
SS-021858	PIPIT CT	PIPIT PL	END	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-021861	PIPIT PL	PIPIT CT	LICIA WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-021862	PIPIT PL	SALVIA WY	PIPIT CT	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-021860	PIPIT PL	LICIA WY	PIPIT WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-021859	PIPIT PL	PIPIT WY	END	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-021863	PIPIT PL	DORMOUSE RD	SALVIA WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-021864	PIPIT WY	BEGIN	PIPIT PL	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-021933	PLAZA DE LA SIENA	CALLE DE LA SIENA	END	1	1188-B6	CARMEL VALLEY	Residential
SS-022039	POCHE PT	LARMIER CR	END	5	1209-J2	SCRIPPS MIRAMAR RANCH	Residential
SS-022088	POINTED OAK LN	ARBORLAKE WY	ARBORLAKE WY	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-022087	POINTED OAK LN	ARBORLAKE WY	SCRIPPS TL	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-031704	PORTER CREEK RD	CHAMBORD WY	DEER PARK WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-022320	POYNTELL CR	TIMBERLAKE DR	END	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-022481	QUARTER MILE DR	LONG RUN DR	EL CAM REAL	1	1188-A5	CARMEL VALLEY	Major
SS-022553	QUINNEL CT	BEGIN	FEDERMAN LN	1	1188-B5	CARMEL VALLEY	Residential
SS-031705	RABBIT RIDGE RD	CHAMBORD WY	DEER PARK WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-022653	RALSTON CR	MENSHA PL	END	1	1188-C5	CARMEL VALLEY	Residential
SS-023298	ROAN RD	ROAN WY	END	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-023297	ROAN RD	SALVIA WY	ROAN WY	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-023299	ROAN WY	GOLDFISH WY	ROAN RD	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-023644	ROUGEMONT PL	BEGIN	END	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023643	ROUGEMONT PL	RUE CHAMONIX	RUE CHANTEMAR	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023642	ROUGEMONT PL	BEGIN	RUE CHAMONIX	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023697	RUE CHAMONIX	ROUGEMONT PL	END	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023698	RUE CHAMONIX	BEGIN	ROUGEMONT PL	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023699	RUE CHANTEMAR	RUE MARABELLE	FAIRBROOK RD	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023706	RUE CHANTEMAR	ROUGEMONT PL	RUE PARC	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023701	RUE CHANTEMAR	RUE PARC	RUE SIENNE NORD	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023702	RUE CHANTEMAR	RUE VINCENNES	ROUGEMONT PL	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023703	RUE CHANTEMAR	RUE CHAMBERRY	RUE VINCENNES	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023700	RUE CHANTEMAR	RUE SIENNE NORD	RUE MARABELLE	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023725	RUE FINISTERRE	RUE RIVIERE VERTE	RUE RIVIERE VERTE	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023724	RUE FINISTERRE	RUE TOURAINE	RUE PARC	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential



**Slurry Seal Group 2023  
Project Street List**

Segment ID	Street Name	Cross Street 1	Cross Street 2	CD	TB Map	Community Planning Area	Functional Classification
SS-023723	RUE FINISTERRE	RUE PARC	RUE RIVIERE VERTE	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-032311	RUE FONTENAY	FAIRBROOK RD	RUE FONTENAY CT	5	1210-B4	SCRIPPS MIRAMAR RANCH	Local
SS-032312	RUE FONTENAY	RUE FONTENAY CT	END	5	1210-B4	SCRIPPS MIRAMAR RANCH	Local
SS-032313	RUE FONTENAY CT	BEGINNING	RUE FONTENAY	5	1210-B4	SCRIPPS MIRAMAR RANCH	Local
SS-023730	RUE MARABELLE	RUE CHANTEMAR	END	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023736	RUE PARC	RUE TOURAINE	RUE FINISTERRE	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023735	RUE PARC	RUE CHANTEMAR	RUE TOURAINE	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023737	RUE RIVIERE VERTE	RUE FINISTERRE	RUE FINISTERRE	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023739	RUE SIENNE NORD	BEGIN	RUE CHANTEMAR	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-023745	RUE TOURAINE	RUE PARC	RUE FINISTERRE	5	1210-C5	SCRIPPS MIRAMAR RANCH	Residential
SS-023802	RUFUS CT	BEGIN	DORMOUSE RD	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023876	SADDLE MTN CT	BEGIN	CHAPARRAL RIDGE RD	1	1188-C6	CARMEL VALLEY	Residential
SS-023910	SALIX CT	BEGIN	SALIX PL	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023911	SALIX PL	SALIX CT	LICIA WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023912	SALIX PL	LICIA WY	SALIX WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023913	SALIX PL	DORMOUSE RD	SALIX CT	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023915	SALIX WY	BEGIN	SALIX PL	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023914	SALIX WY	SALIX PL	END	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023949	SALVIA WY	ROAN RD	DORMOUSE RD	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-023952	SALVIA WY	PIPIP PL	KATYDID CR	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023951	SALVIA WY	KATYDID CR	GOLDFISH WY	6	1189-A7	RANCHO PENASQUITOS	Residential
SS-023950	SALVIA WY	GOLDFISH WY	ROAN RD	6	1189-A6	RANCHO PENASQUITOS	Residential
SS-024145	SAN RAMON DR	FLANDERS DR	IVORY COAST DR	6	1209-C4	MIRA MESA	Residential
SS-024146	SAN RAMON DR	HEBRIDES DR	FLANDERS DR	6	1209-C4	MIRA MESA	Residential
SS-024144	SAN RAMON DR	IVORY COAST DR	REAGAN RD	6	1209-C4	MIRA MESA	Residential
SS-024508	SCRIPPS CAPE VISTA PT	BEGIN	SUNSET RIDGE DR	5	1209-J3	SCRIPPS MIRAMAR RANCH	Residential
SS-024520	SCRIPPS CREEK DR	GATEMOORE WY	SPRING CANYON RD	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-024573	SCRIPPS TL	REDFERN CR	POINTED OAK LN	5	1210-A3	SCRIPPS MIRAMAR RANCH	Collector
SS-024572	SCRIPPS TL	POINTED OAK LN	WEATHERWOOD TR	5	1210-A3	SCRIPPS MIRAMAR RANCH	Collector
SS-024571	SCRIPPS TL	WEATHERWOOD TR	SEMILLON BL	5	1210-A3	SCRIPPS MIRAMAR RANCH	Collector
SS-024575	SCRIPPS TL	TIMBERLAKE DR	GLENCREEK CR	5	1210-A3	SCRIPPS MIRAMAR RANCH	Prime
SS-024574	SCRIPPS TL	GLENCREEK CR	REDFERN CR	5	1210-A3	SCRIPPS MIRAMAR RANCH	Collector
SS-024748	SEMILLON BL	FAIRBROOK RD	BIRCH BLUFF AV	5	1210-C4	SCRIPPS MIRAMAR RANCH	Major
SS-024746	SEMILLON BL	LIVEWOOD WY	KINGSPINE AV	5	1210-C4	SCRIPPS MIRAMAR RANCH	Prime
SS-024749	SEMILLON BL	BIRCH BLUFF AV	END	5	1210-C4	SCRIPPS MIRAMAR RANCH	Major
SS-024744	SEMILLON BL	SPRUCE GROVE AV	EDENOAKS ST	5	1210-B3	SCRIPPS MIRAMAR RANCH	Prime
SS-024743	SEMILLON BL	POMERADO RD	SPRUCE GROVE AV	5	1210-B3	SCRIPPS MIRAMAR RANCH	Prime
SS-024747	SEMILLON BL	KINGSPINE AV	FAIRBROOK RD	5	1210-C4	SCRIPPS MIRAMAR RANCH	Prime
SS-024745	SEMILLON BL	EDENOAKS ST	LIVEWOOD WY	5	1210-B3	SCRIPPS MIRAMAR RANCH	Prime
SS-024907	SHERRARD WY	WALDORF WY	END	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-031646	SONOMA PL	WHITE OAK LN	FLINTWOOD WY	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-025445	SPRUCE GROVE AV	SPRUCE GROVE PL	SEMILLON BL	5	1210-B3	SCRIPPS MIRAMAR RANCH	Residential
SS-025446	SPRUCE GROVE AV	KINGSPINE AV	SPRUCE GROVE PL	5	1210-B4	SCRIPPS MIRAMAR RANCH	Residential
SS-025447	SPRUCE GROVE PL	BEGIN	SPRUCE GROVE AV	5	1210-B3	SCRIPPS MIRAMAR RANCH	Residential
SS-025751	STURGEON CT	BEGIN	CAMARENA RD	1	1188-B5	CARMEL VALLEY	Residential
SS-025752	STURGEON CT	CAMARENA RD	END	1	1188-B5	CARMEL VALLEY	Residential
SS-025875	SUNSET BLUFFS WY	BEGIN	PINE MEADOW CT	1	1188-B5	CARMEL VALLEY	Residential
SS-025877	SUNSET BLUFFS WY	CARMEL CENTER RD	CHAPARRAL RIDGE RD	1	1188-C6	CARMEL VALLEY	Residential
SS-025876	SUNSET BLUFFS WY	PINE MEADOW CT	CARMEL CENTER RD	1	1188-C6	CARMEL VALLEY	Residential
SS-025938	SUNSET RIDGE DR	ASHLAR PL	ANCONA LN	5	1210-A2	SCRIPPS MIRAMAR RANCH	Prime
SS-025942	SUNSET RIDGE DR	HELMER LN	SCRIPPS CAPE VISTA PT	5	1210-A3	SCRIPPS MIRAMAR RANCH	Prime
SS-025939	SUNSET RIDGE DR	STEUER WY	ASHLAR PL	5	1209-J2	SCRIPPS MIRAMAR RANCH	Residential
SS-025940	SUNSET RIDGE DR	MIRA LAGO WY	STEUER WY	5	1209-J2	SCRIPPS MIRAMAR RANCH	Prime
SS-025941	SUNSET RIDGE DR	SCRIPPS CAPE VISTA PT	MIRA LAGO WY	5	1209-J3	SCRIPPS MIRAMAR RANCH	Prime
SS-025944	SUNSET RIDGE DR	TIMBERLAKE DR	SCRIPPS LAKE DR	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-025943	SUNSET RIDGE DR	SCRIPPS LAKE DR	HELMER LN	5	1210-A3	SCRIPPS MIRAMAR RANCH	Prime
SS-025937	SUNSET RIDGE DR	ANCONA LN	CANARYWOOD CT	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-031708	SUNSTONE PE	GAMAY WY	CHAMBORD WY	1	1188-E4	PACIFIC HIGHLANDS RANCH	Residential
SS-031929	SUNSTONE PE	CHAMBORD WY	END	1	1188-E4	PACIFIC HIGHLANDS RANCH	Residential
SS-026052	SYCAMORE RIDGE CT	CHAPARRAL VALLEY CT	END	5	1210-C3	SCRIPPS MIRAMAR RANCH	Residential
SS-026453	THORNBRUSH CT	BEGIN	FAIRBROOK RD	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-026511	TIMBER RIDGE RD	CARMEL CENTER RD	CORBETT CT	1	1188-C5	CARMEL VALLEY	Residential
SS-026510	TIMBER RIDGE RD	CORBETT CT	CHAPARRAL RIDGE RD	1	1188-C5	CARMEL VALLEY	Residential
SS-026516	TIMBERLAKE DR	SUMMERWOOD CT	PEPPERBROOK LN	5	1210-A3	SCRIPPS MIRAMAR RANCH	Prime
SS-026517	TIMBERLAKE DR	QUAIL SPRINGS CT	SUMMERWOOD CT	5	1209-J3	SCRIPPS MIRAMAR RANCH	Prime
SS-026515	TIMBERLAKE DR	PEPPERBROOK LN	SUNSET RIDGE DR	5	1210-A3	SCRIPPS MIRAMAR RANCH	Prime
SS-026518	TIMBERLAKE DR	SCRIPPS LAKE DR	QUAIL SPRINGS CT	5	1209-J3	SCRIPPS MIRAMAR RANCH	Prime
SS-026514	TIMBERLAKE DR	SUNSET RIDGE DR	POYNTELL CR	5	1210-A3	SCRIPPS MIRAMAR RANCH	Prime
SS-026513	TIMBERLAKE DR	POYNTELL CR	SCRIPPS TL	5	1210-A3	SCRIPPS MIRAMAR RANCH	Prime
SS-026549	TIVERTON RD	WYNDHAVEN DR	HALF MILE DR	1	1188-A4	CARMEL VALLEY	Residential
SS-026598	TONDINO CT	BEGIN	TONDINO RD	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-026600	TONDINO RD	WEATHERWOOD TR	TONDINO CT	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-026599	TONDINO RD	TONDINO CT	ACCRA LN	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-026657	TORREY BLUFF DR	CARMEL CREEK RD	GRAYDON RD	1	1188-B5	CARMEL VALLEY	Major
SS-026693	TORREY RIDGE DR	GRAYDON RD	DEL MAR HEIGHTS RD	1	1188-B5	CARMEL VALLEY	Major
SS-027025	TWINLEAF CT	TWINLEAF WY	END	5	1209-H2	MIRAMAR RANCH NORTH	Residential
SS-027027	TWINLEAF WY	TWINLEAF CT	MONTAUBON WY	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-027028	TWINLEAF WY	BEGIN	TWINLEAF CT	5	1209-H2	MIRAMAR RANCH NORTH	Residential
SS-027923	VIA VALARTA	VIA DOMINIQUE	COLLEGIO DR	7	1250-A1	TIERRASANTA	Collector

**Slurry Seal Group 2023  
Project Street List**

Segment ID	Street Name	Cross Street 1	Cross Street 2	CD	TB Map	Community Planning Area	Functional Classification
SS-027920	VIA VALARTA	CAM PLAYA NORTE	AVNDA PLAYA CANCUN	7	1230-A7	TIERRASANTA	Collector
SS-027924	VIA VALARTA	CLAIREMONT MESA BL	VIA DOMINIQUE	7	1250-A1	TIERRASANTA	Collector
SS-027919	VIA VALARTA	AVNDA PLAYA CANCUN	ANTIGUA BL	7	1230-A7	TIERRASANTA	Collector
SS-027921	VIA VALARTA	VIA PLAYA DE CORTES	CAM PLAYA NORTE	7	1230-A7	TIERRASANTA	Collector
SS-027922	VIA VALARTA	COLLEGIO DR	VIA PLAYA DE CORTES	7	1250-A1	TIERRASANTA	Collector
SS-027925	VIA VALARTA	ANTIGUA BL	CAM PLAYA CANCUN	7	1230-A7	TIERRASANTA	Collector
SS-027995	VILLARRICA WY	CTE PLAYA BARCELONA	PORTOBELLO DR	7	1229-J7	TIERRASANTA	Local
SS-027994	VILLARRICA WY	ANTIGUA BL	CAM PLAYA CARMEL	7	1229-J7	TIERRASANTA	Local
SS-027993	VILLARRICA WY	CAM PLAYA CARMEL	CTE PLAYA BARCELONA	7	1229-J7	TIERRASANTA	Local
SS-031647	VINWOOD CT	BRIARCREST PL	END	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-028189	WALDORF WY	MONTAUBON WY	SHERRARD WY	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-028188	WALDORF WY	SHERRARD WY	GATEMOORE WY	5	1209-J2	MIRAMAR RANCH NORTH	Residential
SS-028221	WALNUTDALE ST	MEADOWDALE LN	PINECASTLE ST	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-028220	WALNUTDALE ST	PINECASTLE ST	FAIRBROOK RD	5	1210-C4	SCRIPPS MIRAMAR RANCH	Residential
SS-028351	WEATHERWOOD PL	BEGIN	WEATHERWOOD TR	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-028356	WEATHERWOOD TR	SCRIPPS TL	TONDINO RD	5	1210-A3	SCRIPPS MIRAMAR RANCH	Residential
SS-028354	WEATHERWOOD TR	ACCRA LN	ACCRA LN	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-028355	WEATHERWOOD TR	TONDINO RD	ACCRA LN	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-028353	WEATHERWOOD TR	ACCRA LN	WEATHERWOOD PL	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-028352	WEATHERWOOD TR	WEATHERWOOD PL	END	5	1210-A2	SCRIPPS MIRAMAR RANCH	Residential
SS-031640	WHITE OAK LN	OLD CARMEL VALLEY RD	SONOMA PL	1	1188-E5	PACIFIC HIGHLANDS RANCH	Residential
SS-031641	WHITE OAK LN	SONOMA PL	BRIARCREST PL	1	1188-E6	PACIFIC HIGHLANDS RANCH	Residential
SS-028768	WILBEE CT	OVERTON AV	IRVINGTON AV	7	1249-E6	SERRA MESA	Residential
SS-028767	WILBEE CT	IRVINGTON AV	HUNTINGTON AV	7	1249-E6	SERRA MESA	Residential
SS-028933	WINDSWEPT TR	LANDFAIR RD	END	1	1188-A4	CARMEL VALLEY	Residential
SS-029010	WISPERING WOODS CT	CHAPARRAL RIDGE RD	END	1	1188-C5	CARMEL VALLEY	Residential

**ATTACHMENT F**  
**RESERVED**

**ATTACHMENT G**  
**CONTRACT AGREEMENT**

## CONTRACT AGREEMENT

---

### CONSTRUCTION CONTRACT

This contract is made and entered into between THE CITY OF SAN DIEGO, a municipal corporation, herein called "City", and VSS International, Inc., herein called "Contractor" for construction of **Slurry Seal Group 2023**; Bid No: **K-21-1975-DBB-3**; in the total amount Three Million Nine Hundred Ninety Four Thousand One Hundred Twenty Dollars and Zero Cents (\$3,994,120.00), which is comprised of the Base Bid.

IN CONSIDERATION of the payments to be made hereunder and the mutual undertakings of the parties hereto, City and Contractor agree as follows:

1. The following are incorporated into this contract as though fully set forth herein:
  - (a) The attached Faithful Performance and Payment Bonds.
  - (b) The attached Proposal included in the Bid documents by the Contractor.
  - (c) Reference Standards listed in the Instruction to Bidders and the Supplementary Special Provisions (SSP).
  - (d) That certain documents entitled **Slurry Seal Group 2023**, on file in the office of the Engineering & Capital Projects Department as Document No. **21004779**, as well as all matters referenced therein.
2. The Contractor shall perform and be bound by all the terms and conditions of this contract and in strict conformity therewith shall perform and complete in a good and workmanlike manner **Slurry Seal Group 2023** , Bid Number **K-21-1975-DBB -3**, San Diego, California.
3. For such performances, the City shall pay to Contractor the amounts set forth at the times and in the manner and with such additions or deductions as are provided for in this contract, and the Contractor shall accept such payment in full satisfaction of all claims incident to such performances
4. No claim or suit whatsoever shall be made or brought by Contractor against any officer, agent, or employee of the City for or on account of anything done or omitted to be done in connection with this contract, nor shall any such officer, agent, or employee be liable hereunder.
5. This contract is effective as of the date that the Mayor or designee signs the agreement and is approved by the City Attorney in accordance with San Diego Charter Section 40.

**CONTRACT AGREEMENT (continued)**


**IN WITNESS WHEREOF**, this Agreement is signed by the City of San Diego, acting by and through its Mayor or designee, pursuant to Municipal Code §22.3102 authorizing such execution.

**THE CITY OF SAN DIEGO**

**APPROVED AS TO FORM**

Mara W. Elliott, City Attorney

By 

By 

Print Name: Stephen Samara  
Principal Contract Specialist  
Engineering & Capital Projects Department

Print Name: Cassandra Mouglin  
Deputy City Attorney

Date: 3/9/2021

Date: 3/24/2021

**CONTRACTOR**

By 

Print Name: Jeff Roberts, Senior Vice President

Title: Jeff Roberts, Senior Vice President

Date: \_\_\_\_\_

City of San Diego License No.: \_\_\_\_\_

State Contractor's License No.: 243727

DEPARTMENT OF INDUSTRIAL RELATIONS (DIR) REGISTRATION NUMBER: 1000001231

## **CERTIFICATIONS AND FORMS**

The Bidder, by submitting its electronic bid, agrees to and certifies under penalty of perjury under the laws of the State of California, that the certifications, forms and affidavits submitted as part of this bid are true and correct.

## **BIDDER'S GENERAL INFORMATION**

To the City of San Diego:

Pursuant to "Notice Inviting Bids", specifications, and requirements on file with the City Clerk, and subject to all provisions of the Charter and Ordinances of the City of San Diego and applicable laws and regulations of the United States and the State of California, the undersigned hereby proposes to furnish to the City of San Diego, complete at the prices stated herein, the items or services hereinafter mentioned. The undersigned further warrants that this bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the bid is genuine and not collusive or sham; that the bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any bidder or anyone else to put in a sham bid, or that anyone shall refrain from bidding; that the bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid price of the bidder or any other bidder, or to fix any overhead, profit, or cost element of the bid price, or of that of any other bidder, or to secure any advantage against the public body awarding the contract of anyone interested in the proposed contract; that all statements contained in the bid are true; and, further, that the bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay, any fee to any corporation, partnership, company, association, organization, bid depository, or to any member or agent thereof to effectuate a collusive or sham bid.

The undersigned bidder(s) further warrants that bidder(s) has thoroughly examined and understands the entire Contract Documents (plans and specifications) and the Bidding Documents therefore, and that by submitting said Bidding Documents as its bid proposal, bidder(s) acknowledges and is bound by the entire Contract Documents, including any addenda issued thereto, as such Contract Documents incorporated by reference in the Bidding Documents.



**NON-COLLUSION AFFIDAVIT TO BE EXECUTED BY BIDDER AND SUBMITTED WITH BID UNDER 23  
UNITED STATES CODE 112 AND PUBLIC CONTRACT CODE 7106**

State of California

County of San Diego

The bidder, being first duly sworn, deposes and says that he or she is authorized by the party making the foregoing bid that the bid is not made in the interest of, or on behalf of, any undisclosed person, partnership, company, association, organization, or corporation; that the bid is genuine and not collusive or sham; that the bidder has not directly or indirectly induced or solicited any other bidder to put in a false or sham bid, and has not directly or indirectly colluded, conspired, connived, or agreed with any bidder or anyone else to put in a sham bid, or that anyone shall refrain from bidding; that the bidder has not in any manner, directly or indirectly, sought by agreement, communication, or conference with anyone to fix the bid price of the bidder or any other bidder, or to fix any overhead, profit, or cost element of the bid price, or of that of any other bidder, or to secure any advantage against the public body awarding the contract of anyone interested in the proposed contract; that all statements contained in the bid are true; and further, that the bidder has not, directly or indirectly, submitted his or her bid price or any breakdown thereof, or the contents thereof, or divulged information or data relative thereto, or paid, and will not pay, any fee to any corporation, partnership, company association, organization, bid depository, or to any member or agent thereof to effectuate a collusive or sham bid.

## **CONTRACTOR CERTIFICATION**

---

### **DRUG-FREE WORKPLACE**

I hereby certify that I am familiar with the requirements of San Diego City Council Policy No. 100-17 regarding Drug-Free Workplace as outlined in the WHITEBOOK, Section 5-1.3, "Drug-Free Workplace", of the project specifications, and that;

This company has in place a drug-free workplace program that complies with said policy. I further certify that each subcontract agreement for this project contains language which indicates the subcontractor's agreement to abide by the provisions of subdivisions a) through c) of the policy as outlined.

## **CONTRACTOR CERTIFICATION**

---

### **AMERICANS WITH DISABILITIES ACT (ADA) COMPLIANCE CERTIFICATION**

I hereby certify that I am familiar with the requirements of San Diego City Council Policy No. 100-4 regarding the Americans With Disabilities Act (ADA) outlined in the WHITEBOOK, Section 5-1.2, "California Building Code, California Code of Regulations Title 24 and Americans with Disabilities Act", of the project specifications, and that:

This company has in place workplace program that complies with said policy. I further certify that each subcontract agreement for this project contains language which indicates the subcontractor's agreement to abide by the provisions of the policy as outlined.

## **CONTRACTOR CERTIFICATION**

---

### **CONTRACTOR STANDARDS – PLEDGE OF COMPLIANCE**

I declare under penalty of perjury that I am authorized to make this certification on behalf of the company submitting this bid/proposal, that as Contractor, I am familiar with the requirements of City of San Diego Municipal Code § 22.3004 regarding Contractor Standards as outlined in the WHITEBOOK, Section 5-1.4, ("Contractor Standards and Pledge of Compliance"), of the project specifications, and that Contractor has complied with those requirements.

I further certify that each of the Contractor's subcontractors has completed a Pledge of Compliance attesting under penalty of perjury of having complied with City of San Diego Municipal Code § 22.3004.

## **CONTRACTOR CERTIFICATION**

---

### **EQUAL BENEFITS ORDINANCE CERTIFICATION**

I declare under penalty of perjury that I am familiar with the requirements of and in compliance with the City of San Diego Municipal Code § 22.4300 regarding Equal Benefits Ordinance.

## **CONTRACTOR CERTIFICATION**

---

### **EQUAL PAY ORDINANCE CERTIFICATION**

Contractor shall comply with the Equal Pay Ordinance (EPO) codified in the San Diego Municipal Code (SDMC) at section 22.4801 through 22.4809, unless compliance is not required based on an exception listed in SDMC section 22.4804.

Contractor shall require all of its subcontractors to certify compliance with the EPO in their written subcontracts.

Contractor must post a notice informing its employees of their rights under the EPO in the workplace or job site.

By signing this Contract with the City of San Diego, Contractor acknowledges the EPO requirements and pledges ongoing compliance with the requirements of SDMC Division 48, section 22.4801 et seq., throughout the duration of this Contract.

**AFFIDAVIT OF DISPOSAL**

**(To be submitted upon completion of Construction pursuant to the contracts Certificate of Completion)**

**WHEREAS**, on the \_\_\_\_\_ DAY OF \_\_\_\_\_, 2\_\_\_\_\_ the undersigned entered into and executed a contract with the City of San Diego, a municipal corporation, for:

**Slurry Seal Group 2023**

(Project Title)

as particularly described in said contract and identified as Bid No. **K-21-1975-DBB-3**; SAP No. IO **21004779**; and **WHEREAS**, the specification of said contract requires the Contractor to affirm that "all brush, trash, debris, and surplus materials resulting from this project have been disposed of in a legal manner"; and **WHEREAS**, said contract has been completed and all surplus materials disposed of:

**NOW, THEREFORE**, in consideration of the final payment by the City of San Diego to said Contractor under the terms of said contract, the undersigned Contractor, does hereby affirm that all surplus materials as described in said contract have been disposed of at the following location(s)

and that they have been disposed of according to all applicable laws and regulations.

Dated this \_\_\_\_\_ DAY OF \_\_\_\_\_, \_\_\_\_\_.

By: \_\_\_\_\_  
Contractor

**ATTEST:**

State of \_\_\_\_\_ County of \_\_\_\_\_

On this \_\_\_\_\_ DAY OF \_\_\_\_\_, 2\_\_\_\_\_, before the undersigned, a Notary Public in and for said County and State, duly commissioned and sworn, personally appeared \_\_\_\_\_ known to me to be the \_\_\_\_\_ Contractor named in the foregoing Release, and whose name is subscribed thereto, and acknowledged to me that said Contractor executed the said Release.

Notary Public in and for said County and State

**LIST OF SUBCONTRACTORS**

**\*\*\* PROVIDED FOR ILLUSTRATIVE PURPOSES ONLY \*\*\* TO BE SUBMITTED IN ELECTRONIC FORMAT ONLY\*\*\* SEE INSTRUCTIONS TO BIDDERS, FOR FURTHER INFORMATION**

In accordance with the requirements of the "Subletting and Subcontracting Fair Practices Act", Section 4100, of the California Public Contract Code (PCC), the Bidder is to list below the name, address and license number of each Subcontractor who will perform work, labor, render services or specially fabricate and install a portion [type] of the work or improvement, in an amount of or in excess of 0.5% of the Contractor's total Bid. Failure to comply with this requirement may result in the Bid being rejected as non-responsive. The Contractor is to list only one Subcontractor for each portion of the Work. The Bidder's attention is directed to the Special Provisions - Section 3-2, "SELF-PERFORMANCE", which stipulates the percentage of the Work to be performed with the Bidder's own forces. The Bidder is to also list all SLBE, ELBE, DBE, DVBE, MBE, WBE, OBE, SDB, WoSB, HUBZone, and SDVOSB Subcontractors for which the Bidders are seeking recognition towards achieving any mandatory, voluntary, or both subcontracting participation percentages.

NAME, ADDRESS AND TELEPHONE NUMBER OF SUBCONTRACTOR	CONSTRUCTOR OR DESIGNER	SUBCONTRACTOR LICENSE NUMBER	TYPE OF WORK	DOLLAR VALUE OF SUBCONTRACT	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSB <sup>①</sup>	WHERE CERTIFIED <sup>②</sup>	CHECK IF JOINT VENTURE PARTNERSHIP
Name: _____ Address: _____ City: _____ State: _____ Zip: _____ Phone: _____ Email: _____							
Name: _____ Address: _____ City: _____ State: _____ Zip: _____ Phone: _____ Email: _____							

- ① As appropriate, Bidder shall identify Subcontractor as one of the following and shall include a valid proof of certification (except for OBE, SLBE and ELBE):
- |   |        |  |         |
|---|--------|--|---------|
| Certified Minority Business Enterprise        | MBE    | Certified Woman Business Enterprise            | WBE     |
| Certified Disadvantaged Business Enterprise   | DBE    | Certified Disabled Veteran Business Enterprise | DVBE    |
| Other Business Enterprise                     | OBE    | Certified Emerging Local Business Enterprise   | ELBE    |
| Certified Small Local Business Enterprise     | SLBE   | Small Disadvantaged Business                   | SDB     |
| Woman-Owned Small Business                    | WoSB   | HUBZone Business                               | HUBZone |
| Service-Disabled Veteran Owned Small Business | SDVOSB |  |         |
- ② As appropriate, Bidder shall indicate if Subcontractor is certified by:
- |  |        |  |          |
|--|--------|--|----------|
| City of San Diego                                    | CITY   | State of California Department of Transportation | CALTRANS |
| California Public Utilities Commission               | CPUC   |  |          |
| State of California's Department of General Services | CADoGS | City of Los Angeles                              | LA       |
| State of California                                  | CA     | U.S. Small Business Administration               | SBA      |

**The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.**



**NAMED EQUIPMENT/MATERIAL SUPPLIER LIST**

**\*\*\* PROVIDED FOR ILLUSTRATIVE PURPOSES ONLY \*\*\* TO BE SUBMITTED IN ELECTRONIC FORMAT ONLY \*\*\* SEE INSTRUCTIONS TO BIDDERS FOR FURTHER INFORMATION**

NAME, ADDRESS AND TELEPHONE NUMBER OF VENDOR/SUPPLIER	MATERIALS OR SUPPLIES	DOLLAR VALUE OF MATERIAL OR SUPPLIES	SUPPLIER (Yes/No)	MANUFACTURER (Yes/No)	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSB <sup>①</sup>	WHERE CERTIFIED <sup>②</sup>
Name: _____ Address: _____ City: _____ State: _____ Zip: _____ Phone: _____ Email: _____						
Name: _____ Address: _____ City: _____ State: _____ Zip: _____ Phone: _____ Email: _____						

- ① As appropriate, Bidder shall identify Vendor/Supplier as one of the following and shall include a valid proof of certification (except for OBE, SLBE and ELBE):
- |   |        |  |         |
|---|--------|--|---------|
| Certified Minority Business Enterprise        | MBE    | Certified Woman Business Enterprise            | WBE     |
| Certified Disadvantaged Business Enterprise   | DBE    | Certified Disabled Veteran Business Enterprise | DVBE    |
| Other Business Enterprise                     | OBE    | Certified Emerging Local Business Enterprise   | ELBE    |
| Certified Small Local Business Enterprise     | SLBE   | Small Disadvantaged Business                   | SDB     |
| Woman-Owned Small Business                    | WoSB   | HUBZone Business                               | HUBZone |
| Service-Disabled Veteran Owned Small Business | SDVOSB |  |         |
- ② As appropriate, Bidder shall indicate if Vendor/Supplier is certified by:
- |  |        |  |          |
|--|--------|--|----------|
| City of San Diego                                    | CITY   | State of California Department of Transportation | CALTRANS |
| California Public Utilities Commission               | CPUC   |  |          |
| State of California's Department of General Services | CADoGS | City of Los Angeles                              | LA       |
| State of California                                  | CA     | U.S. Small Business Administration               | SBA      |

**The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.**

## **ELECTRONICALLY SUBMITTED FORMS**

**FAILURE TO FULLY COMPLETE AND SUBMIT ANY OF THE FOLLOWING FORMS WILL DEEM YOUR BID NON-RESPONSIVE.**

**PLANETBIDS WILL NOT ALLOW FOR BID SUBMISSIONS WITHOUT THE ATTACHMENT OF THESE FORMS**

The following forms are to be completed by the bidder and submitted (uploaded) electronically with the bid in PlanetBids.

- A. BID BOND – See Instructions to Bidders, Bidders Guarantee of Good Faith (Bid Security) for further instructions**
- B. CONTRACTOR’S CERTIFICATION OF PENDING ACTIONS**
- C. MANDATORY DISCLOSURE OF BUSINESS INTERESTS FORM**
- D. DEBARMENT AND SUSPENSION CERTIFICATION FOR PRIME CONTRACTOR**
- E. DEBARMENT AND SUSPENSION CERTIFICATION FOR SUBCONTRACTORS, SUPPLIERS AND MANUFACTURERS**

**BID BOND**

**See Instructions to Bidders, Bidder Guarantee of Good Faith  
(Bid Security)**

KNOW ALL MEN BY THESE PRESENTS,

That VSS International, Inc. as Principal,  
and Western Surety Company as Surety, are held  
and firmly bound unto The City of San Diego hereinafter called "OWNER," in the sum  
of **10% OF THE TOTAL BID AMOUNT** for the payment of which sum, well and truly to be made, we bind  
ourselves, our heirs, executors, administrators, successors, and assigns, jointly and severally, firmly by these  
presents.

WHEREAS, said Principal has submitted a Bid to said OWNER to perform the WORK required under the  
bidding schedule(s) of the OWNER's Contract Documents entitled

SLURRY SEAL GROUP 2023

NOW THEREFORE, if said Principal is awarded a contract by said OWNER and, within the time and in the  
manner required in the "Notice Inviting Bids" enters into a written Agreement on the form of agreement  
bound with said Contract Documents, furnishes the required certificates of insurance, and furnishes the  
required Performance Bond and Payment Bond, then this obligation shall be null and void, otherwise it shall  
remain in full force and effect. In the event suit is brought upon this bond by said OWNER and OWNER  
prevails, said Surety shall pay all costs incurred by said OWNER in such suit, including a reasonable attorney's  
fee to be fixed by the court.

SIGNED AND SEALED, this 16th day of November, 2020


VSS International, Inc. (SEAL)  
(Principal)

Western Surety Company (SEAL)  
(Surety)

By: [Signature]  
(Signature)  
**Jeff Roberts, Sr. Vice President**

By: [Signature]  
(Signature)  
**Anibal Samuel Campos, Attorney-in-Fact**

(SEAL AND NOTARIAL ACKNOWLEDGEMENT OF SURETY)



**CALIFORNIA ACKNOWLEDGMENT**

CIVIL CODE § 1189

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.


State of California }  
County of Contra Costa }

On NOV 16 2020 before me, Chelsea Arnold, Notary Public  
*Date Here Insert Name and Title of the Officer*  
personally appeared Anibal Samuel Campos  
*Name(s) of Signer(s)*

who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.



Place Notary Seal and/or Stamp Above

Signature *Chelsea Arnold*  
*Signature of Notary Public*

**OPTIONAL**

*Completing this information can deter alteration of the document or fraudulent reattachment of this form to an unintended document.*

**Description of Attached Document**

Title or Type of Document: \_\_\_\_\_  
Document Date: \_\_\_\_\_ Number of Pages: \_\_\_\_\_  
Signer(s) Other Than Named Above: \_\_\_\_\_

**Capacity(ies) Claimed by Signer(s)**

Signer's Name: \_\_\_\_\_ Signer's Name: \_\_\_\_\_  
 Corporate Officer – Title(s): \_\_\_\_\_  Corporate Officer – Title(s): \_\_\_\_\_  
 Partner –  Limited  General  Partner –  Limited  General  
 Individual  Attorney in Fact  Individual  Attorney in Fact  
 Trustee  Guardian or Conservator  Trustee  Guardian or Conservator  
 Other: \_\_\_\_\_  Other: \_\_\_\_\_  
Signer is Representing: \_\_\_\_\_ Signer is Representing: \_\_\_\_\_

# Western Surety Company

## POWER OF ATTORNEY APPOINTING INDIVIDUAL ATTORNEY-IN-FACT

Know All Men By These Presents, That WESTERN SURETY COMPANY, a South Dakota corporation, is a duly organized and existing corporation having its principal office in the City of Sioux Falls, and State of South Dakota, and that it does by virtue of the signature and seal herein affixed hereby make, constitute and appoint

**Steven N Passerine, Kathleen E Earle, Benjamin Wolfe, Anibal Samuel Campos, Chelsea Arnold, Individually**

of San Ramon, CA, its true and lawful Attorney(s)-in-Fact with full power and authority hereby conferred to sign, seal and execute for and on its behalf bonds, undertakings and other obligatory instruments of similar nature

### - In Unlimited Amounts -

and to bind it thereby as fully and to the same extent as if such instruments were signed by a duly authorized officer of the corporation and all the acts of said Attorney, pursuant to the authority hereby given, are hereby ratified and confirmed.

This Power of Attorney is made and executed pursuant to and by authority of the By-Law printed on the reverse hereof, duly adopted, as indicated, by the shareholders of the corporation.

In Witness Whereof, WESTERN SURETY COMPANY has caused these presents to be signed by its Vice President and its corporate seal to be hereto affixed on this 7th day of May, 2020.

WESTERN SURETY COMPANY



Paul T. Bruflat  
Paul T. Bruflat, Vice President

State of South Dakota }  
County of Minnehaha } ss

On this 7th day of May, 2020, before me personally came Paul T. Bruflat, to me known, who, being by me duly sworn, did depose and say: that he resides in the City of Sioux Falls, State of South Dakota; that he is the Vice President of WESTERN SURETY COMPANY described in and which executed the above instrument; that he knows the seal of said corporation; that the seal affixed to the said instrument is such corporate seal; that it was so affixed pursuant to authority given by the Board of Directors of said corporation and that he signed his name thereto pursuant to like authority, and acknowledges same to be the act and deed of said corporation.

My commission expires

June 23, 2021



J. Mohr  
J. Mohr, Notary Public

### CERTIFICATE

I, L. Nelson, Assistant Secretary of WESTERN SURETY COMPANY do hereby certify that the Power of Attorney hereinabove set forth is still in force, and further certify that the By-Law of the corporation printed on the reverse hereof is still in force. In testimony whereof I have hereunto subscribed my name and affixed the seal of the said corporation this 16th day of November, 2020.



WESTERN SURETY COMPANY

L. Nelson  
L. Nelson, Assistant Secretary



## ACKNOWLEDGMENT

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California  
County of Yolo )


On 11/16/2020 before me, Faye K. Alano, Notary Public  
(insert name and title of the officer)

personally appeared Jeff Roberts,  
who proved to me on the basis of satisfactory evidence to be the person(s) whose name(s) is/are subscribed to the within instrument and acknowledged to me that he/she/they executed the same in his/her/their authorized capacity(ies), and that by his/her/their signature(s) on the instrument the person(s), or the entity upon behalf of which the person(s) acted, executed the instrument.

I certify under PENALTY OF PERJURY under the laws of the State of California that the foregoing paragraph is true and correct.

WITNESS my hand and official seal.

Signature  (Seal)





**CONTRACTOR'S CERTIFICATION OF PENDING ACTIONS**

As part of its bid or proposal (Non-Price Proposal in the case of Design-Build contracts), the Bidder shall provide to the City a list of all instances within the past 10 years where a complaint was filed or pending against the Bidder in a legal or administrative proceeding alleging that Bidder discriminated against its employees, subcontractors, vendors or suppliers, and a description of the status or resolution of that complaint, including any remedial action taken.

CHECK ONE BOX ONLY.

- The undersigned certifies that within the past 10 years the Bidder has NOT been the subject of a complaint or pending action in a legal administrative proceeding alleging that Bidder discriminated against its employees, subcontractors, vendors or suppliers.
  
- The undersigned certifies that within the past 10 years the Bidder has been the subject of a complaint or pending action in a legal administrative proceeding alleging that Bidder discriminated against its employees, subcontractors, vendors or suppliers. A description of the status or resolution of that complaint, including any remedial action taken and the applicable dates is as follows:

DATE OF CLAIM	LOCATION	DESCRIPTION OF CLAIM	LITIGATION (Y/N)	STATUS	RESOLUTION/REMEDIAL ACTION TAKEN

Contractor Name: VSS International, Inc.

Certified By Jeff Roberts Title Senior Vice President

  
 Name \_\_\_\_\_  
 Signature \_\_\_\_\_ Date 11/02/2020

**USE ADDITIONAL FORMS AS NECESSARY**

## Mandatory Disclosure of Business Interests Form

### BIDDER/PROPOSER INFORMATION

Legal Name		DBA	
VSS International, Inc.		N/A	
Street Address	City	State	Zip
3785 Channel Drive, West Sacramento	California	95691	
Contact Person, Title		Phone	Fax
Jeff Roberts, Senior Vice President		916-373-1500	916-373-0183

Provide the name, identity, and precise nature of the interest\* of all persons who are directly or indirectly involved\*\* in this proposed transaction (SDMC § 21.0103).

\* The precise nature of the interest includes:

- the percentage ownership interest in a party to the transaction,
- the percentage ownership interest in any firm, corporation, or partnership that will receive funds from the transaction, the value of any financial interest in the transaction,
- any contingent interest in the transaction and the value of such interest should the contingency be satisfied, and any
- philanthropic, scientific, artistic, or property interest in the transaction.

\*\* Directly or indirectly involved means pursuing the transaction by:

- communicating or negotiating with City officers or employees,
- submitting or preparing applications, bids, proposals or other documents for purposes of contracting with the City,
- or directing or supervising the actions of persons engaged in the above activity.

Name	Title/Position
Basic Resources, Inc.	Owner
City and State of Residence	Employer (if different than Bidder/Proposer)
Modesto, CA	Basic Resource, Inc.
Interest in the transaction	
100%	

Name	Title/Position
Jeff Reed	President, Owner
City and State of Residence	Employer (if different than Bidder/Proposer)
West Sacramento, CA	
Interest in the transaction	
100%	

### \* Use Additional Pages if Necessary \*

Under penalty of perjury under the laws of the State of California, I certify that I am responsible for the completeness and accuracy of the responses contained herein, and that all information provided is true, full and complete to the best of my knowledge and belief. I agree to provide written notice to the Mayor or Designee within five (5) business days if, at any time, I learn that any portion of this Mandatory Disclosure of Business Interests Form requires an updated response. Failure to timely provide the Mayor or Designee with written notice is grounds for Contract termination.

Jeff Roberts, Senior Vice President



11/02/2020

Print Name, Title

Signature

Date

**Failure to sign and submit this form with the bid/proposal shall make the bid/proposal non-responsive. In the case of an informal solicitation, the contract will not be awarded unless a signed and completed Mandatory Disclosure of Business Interests Form is submitted.**



**DEBARMENT AND SUSPENSION CERTIFICATION**  
**PRIME CONTRACTOR**  
**FAILURE TO COMPLETE AND SUBMIT AT TIME OF BID SHALL RENDER BID NON-RESPONSIVE**

EFFECT OF DEBARMENT OR SUSPENSION
To promote integrity in the City's contracting processes and to protect the public interest, the City shall only enter into contracts with responsible- bidders and contractors. In accordance with San Diego Municipal Code §22.0814 (a): <i>Bidders</i> and <i>contractors</i> who have been <i>debarred</i> or <i>suspended</i> are excluded from submitting bids, submitting responses to requests for proposal or qualifications, receiving <i>contract</i> awards, executing <i>contracts</i> , participating as a <i>subcontractor</i> , employee, agent or representative of another <i>person</i> contracting with the City.

As part of its bid or proposal (Non-Price Proposal in the case of Design-Build contracts), the Bidder shall provide to the City a list of Names of the Principal Individual owner(s).

The names of all persons interested in the foregoing proposal as Principals are as follows:

NAME	TITLE
Jeffrey Reed	President
Jeff Roberts	Senior Vice President
Jordan Reed	Secretary
Jordan Reed	Treasurer

**IMPORTANT NOTICE:** If Bidder or other interested person is a corporation, state secretary, treasurer, and manager thereof; if a co-partnership, state true name of firm, also names of all individual co-partners composing firm; if Bidder or other interested person is an individual, state first and last names in full.

The Bidder, under penalty of perjury, certifies that, except as noted below, he/she or any person associated therewith in the capacity of owner, partner, director, officer, manager:

- Is not currently under suspension, debarment, voluntary exclusion, or determination of ineligibility by any Federal, State or local agency;
- has not been suspended, debarred, voluntarily excluded or determined ineligible by any Federal, State or local agency within the past 3 years;
- does not have a proposed debarment pending; and
- has not been indicted, convicted, or had a civil judgment rendered against it by a court of competent jurisdiction in any matter involving fraud or official misconduct within the past 3 years.


If there are any exceptions to this certification, insert the exceptions in the following space.

NONE

Exceptions will be considered in determining bidder responsibility. For any exception noted above, indicate below to whom it applies, initiating agency, and dates of action.

Contractor Name: VSS International, Inc.

Certified By Jeff Roberts Title Senior Vice President

  
 Name \_\_\_\_\_  
 Signature \_\_\_\_\_

Date 11/02/2020

**NOTE:** Providing false information may result in criminal prosecution or administrative sanctions.

**DEBARMENT AND SUSPENSION CERTIFICATION**  
**SUBCONTRACTORS, SUPPLIERS AND MANUFACTURERS**  
**\*TO BE COMPLETED BY BIDDER\***  
**FAILURE TO COMPLETE AND SUBMIT AT TIME OF BID SHALL RENDER BID NON-RESPONSIVE**

Names of the Principal individual owner(s)

As part of its bid or proposal (Non-Price Proposal in the case of Design-Build contracts), the Bidder shall provide to the City a list of Names of the Principal Individual owner(s) for their subcontractor/supplier/manufacturers.

Please indicate if principal owner is serving in the capacity of **subcontractor**, **supplier**, and/or **manufacturer**:

SUBCONTRACTOR       SUPPLIER       MANUFACTURER

NAME	TITLE
Global Road Sealing, Inc. - Terri La	Secretary
Miramar General Engineering - Ala Karaja	President
Frank & Son Paving Inc - Alicia Vasquez	President
CTE inc. - William Clark	Owner/President

SUBCONTRACTOR       SUPPLIER       MANUFACTURER

NAME	TITLE
Payco Specialties, Inc. - Rebecca Llewellyn	President

SUBCONTRACTOR       SUPPLIER       MANUFACTURER

NAME	TITLE
Chandler Aggregates - Eric Werner	President
California Commercial Asphalt - Matt Pound	Sales Manager

SUBCONTRACTOR       SUPPLIER       MANUFACTURER

NAME	TITLE

Contractor Name: VSS International, Inc.

Certified By Jeff Roberts Title Senior Vice President

  
 Name \_\_\_\_\_  
 Signature \_\_\_\_\_ Date 11/02/2020

**\*USE ADDITIONAL FORMS AS NECESSARY\*\***

**NAMED EQUIPMENT/MATERIAL SUPPLIER LIST**

**\*\*\* PROVIDED FOR ILLUSTRATIVE PURPOSES ONLY \*\*\* TO BE SUBMITTED IN ELECTRONIC FORMAT ONLY \*\*\* SEE INSTRUCTIONS TO BIDDERS FOR FURTHER INFORMATION**

NAME, ADDRESS AND TELEPHONE NUMBER OF VENDOR/SUPPLIER	MATERIALS OR SUPPLIES	DOLLAR VALUE OF MATERIAL OR SUPPLIES	SUPPLIER (Yes/No)	MANUFACTURER (Yes/No)	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSB <sup>①</sup>	WHERE CERTIFIED <sup>②</sup>
Name: <u>Chandler Aggregates</u> Address: <u>24867 Maltri Rd</u> City: <u>Corona</u> State: <u>CA</u> Zip: <u>92883</u> Phone: <u>951-277-9110</u> Email: <u>jgilmore@wernercorp.net</u>	Slurry Seal Aggregate Supplier	\$173,262.50	YES	NO	N/A	N/A
Name: <u>California Commercial Asphalt</u> Address: <u>9229 Harris Plant Rd</u> City: <u>San Diego</u> State: <u>CA</u> Zip: <u>92145</u> Phone: <u>858-513-0611</u> Email: <u>wade.anderson@lehighhanson.com</u>	Emulsion Supplier	\$391,779.00	YES	NO	N/A	N/A

- ① As appropriate, Bidder shall identify Vendor/Supplier as one of the following and shall include a valid proof of certification (except for OBE, SLBE and ELBE):
- |   |        |  |         |
|---|--------|--|---------|
| Certified Minority Business Enterprise        | MBE    | Certified Woman Business Enterprise            | WBE     |
| Certified Disadvantaged Business Enterprise   | DBE    | Certified Disabled Veteran Business Enterprise | DVBE    |
| Other Business Enterprise                     | OBE    | Certified Emerging Local Business Enterprise   | ELBE    |
| Certified Small Local Business Enterprise     | SLBE   | Small Disadvantaged Business                   | SDB     |
| Woman-Owned Small Business                    | WoSB   | HUBZone Business                               | HUBZone |
| Service-Disabled Veteran Owned Small Business | SDVOSB |  |         |
- ② As appropriate, Bidder shall indicate if Vendor/Supplier is certified by:
- |  |        |  |          |
|--|--------|--|----------|
| City of San Diego                                    | CITY   | State of California Department of Transportation | CALTRANS |
| California Public Utilities Commission               | CPUC   |  |          |
| State of California's Department of General Services | CADoGS | City of Los Angeles                              | LA       |
| State of California                                  | CA     | U.S. Small Business Administration               | SBA      |

**The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.**

**LIST OF SUBCONTRACTORS**

**\*\*\* PROVIDED FOR ILLUSTRATIVE PURPOSES ONLY \*\*\* TO BE SUBMITTED IN ELECTRONIC FORMAT ONLY\*\*\* SEE INSTRUCTIONS TO BIDDERS, FOR FURTHER INFORMATION**

In accordance with the requirements of the "Subletting and Subcontracting Fair Practices Act", Section 4100, of the California Public Contract Code (PCC), the Bidder is to list below the name, address and license number of each Subcontractor who will perform work, labor, render services or specially fabricate and install a portion [type] of the work or improvement, in an amount of or in excess of 0.5% of the Contractor's total Bid. Failure to comply with this requirement may result in the Bid being rejected as non-responsive. The Contractor is to list only one Subcontractor for each portion of the Work. The Bidder's attention is directed to the Special Provisions - Section 3-2, "SELF-PERFORMANCE", which stipulates the percentage of the Work to be performed with the Bidder's own forces. The Bidder is to also list all SLBE, ELBE, DBE, DVBE, MBE, WBE, OBE, SDB, WoSB, HUBZone, and SDVOSB Subcontractors for which the Bidders are seeking recognition towards achieving any mandatory, voluntary, or both subcontracting participation percentages.

NAME, ADDRESS AND TELEPHONE NUMBER OF SUBCONTRACTOR	CONSTRUCTOR OR DESIGNER	SUBCONTRACTOR LICENSE NUMBER	TYPE OF WORK	DOLLAR VALUE OF SUBCONTRACT	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSB①	WHERE CERTIFIED②	CHECK IF JOINT VENTURE PARTNERSHIP
Name: <u>Global Road Sealing, Inc</u> Address: <u>10832 Dorothy Ave</u> City: <u>Garden Grove</u> State: <u>CA</u> Zip: <u>92843</u> Phone: <u>(714)893-0845</u> Email: <u>terri@globalroadsealing.com</u>	Constructor	757584	Crack Seal	\$250,971.76	SBE, MBE	CA	
Name: <u>Miramar General Engineering</u> Address: <u>1827 Cleveland Ave</u> City: <u>National City</u> State: <u>CA</u> Zip: <u>91950</u> Phone: <u>(619)434-5900</u> Email: <u>liz@miramargeneral.com</u>	Constructor	1009541	Utilities Adjustments	\$98,500.00	ELBE	CITY	

- ① As appropriate, Bidder shall identify Subcontractor as one of the following and shall include a valid proof of certification (except for OBE, SLBE and ELBE):
- |   |        |  |         |
|---|--------|--|---------|
| Certified Minority Business Enterprise        | MBE    | Certified Woman Business Enterprise            | WBE     |
| Certified Disadvantaged Business Enterprise   | DBE    | Certified Disabled Veteran Business Enterprise | DVBE    |
| Other Business Enterprise                     | OBE    | Certified Emerging Local Business Enterprise   | ELBE    |
| Certified Small Local Business Enterprise     | SLBE   | Small Disadvantaged Business                   | SDB     |
| Woman-Owned Small Business                    | WoSB   | HUBZone Business                               | HUBZone |
| Service-Disabled Veteran Owned Small Business | SDVOSB |  |         |
- ② As appropriate, Bidder shall indicate if Subcontractor is certified by:
- |  |        |  |          |
|--|--------|--|----------|
| City of San Diego                                    | CITY   | State of California Department of Transportation | CALTRANS |
| California Public Utilities Commission               | CPUC   |  |          |
| State of California's Department of General Services | CADoGS | City of Los Angeles                              | LA       |
| State of California                                  | CA     | U.S. Small Business Administration               | SBA      |

**The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.**



**LIST OF SUBCONTRACTORS**

**\*\*\* PROVIDED FOR ILLUSTRATIVE PURPOSES ONLY \*\*\* TO BE SUBMITTED IN ELECTRONIC FORMAT ONLY\*\*\* SEE INSTRUCTIONS TO BIDDERS, FOR FURTHER INFORMATION**

In accordance with the requirements of the "Subletting and Subcontracting Fair Practices Act", Section 4100, of the California Public Contract Code (PCC), the Bidder is to list below the name, address and license number of each Subcontractor who will perform work, labor, render services or specially fabricate and install a portion [type] of the work or improvement, in an amount of or in excess of 0.5% of the Contractor's total Bid. Failure to comply with this requirement may result in the Bid being rejected as non-responsive. The Contractor is to list only one Subcontractor for each portion of the Work. The Bidder's attention is directed to the Special Provisions - Section 3-2, "SELF-PERFORMANCE", which stipulates the percentage of the Work to be performed with the Bidder's own forces. The Bidder is to also list all SLBE, ELBE, DBE, DVBE, MBE, WBE, OBE, SDB, WoSB, HUBZone, and SDVOSB Subcontractors for which the Bidders are seeking recognition towards achieving any mandatory, voluntary, or both subcontracting participation percentages.

NAME, ADDRESS AND TELEPHONE NUMBER OF SUBCONTRACTOR	CONSTRUCTOR OR DESIGNER	SUBCONTRACTOR LICENSE NUMBER	TYPE OF WORK	DOLLAR VALUE OF SUBCONTRACT	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSB <sup>①</sup>	WHERE CERTIFIED <sup>②</sup>	CHECK IF JOINT VENTURE PARTNERSHIP
Name: <u>Frank and Son Paving, Inc</u> Address: <u>1019 3rd Avenue</u> City: <u>Chula Vista</u> State: <u>CA</u> Zip: <u>91911</u> Phone: <u>(619)422-8322</u> Email: <u>franksonpaving@yahoo.com</u>	Constructor	612545	AC PAVING	\$709,659.75	ELBE, SBE	CITY, CA	
Name: <u>CTE inc</u> Address: <u>9991 Possum Creek Lane</u> City: <u>El Cajon</u> State: <u>CA</u> Zip: <u>92021</u> Phone: <u>(619)561-3633</u> Email: <u>reggie@cte-ca.com</u>	Constructor	786098	LOOPS	\$12,960.00	ELBE	CITY	

- ① As appropriate, Bidder shall identify Subcontractor as one of the following and shall include a valid proof of certification (except for OBE, SLBE and ELBE):
- |   |        |  |         |
|---|--------|--|---------|
| Certified Minority Business Enterprise        | MBE    | Certified Woman Business Enterprise            | WBE     |
| Certified Disadvantaged Business Enterprise   | DBE    | Certified Disabled Veteran Business Enterprise | DVBE    |
| Other Business Enterprise                     | OBE    | Certified Emerging Local Business Enterprise   | ELBE    |
| Certified Small Local Business Enterprise     | SLBE   | Small Disadvantaged Business                   | SDB     |
| Woman-Owned Small Business                    | WoSB   | HUBZone Business                               | HUBZone |
| Service-Disabled Veteran Owned Small Business | SDVOSB |  |         |
- ② As appropriate, Bidder shall indicate if Subcontractor is certified by:
- |  |        |  |          |
|--|--------|--|----------|
| City of San Diego                                    | CITY   | State of California Department of Transportation | CALTRANS |
| California Public Utilities Commission               | CPUC   |  |          |
| State of California's Department of General Services | CADoGS | City of Los Angeles                              | LA       |
| State of California                                  | CA     | U.S. Small Business Administration               | SBA      |

**The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.**

**LIST OF SUBCONTRACTORS**

**\*\*\* PROVIDED FOR ILLUSTRATIVE PURPOSES ONLY \*\*\* TO BE SUBMITTED IN ELECTRONIC FORMAT ONLY\*\*\* SEE INSTRUCTIONS TO BIDDERS, FOR FURTHER INFORMATION**

In accordance with the requirements of the "Subletting and Subcontracting Fair Practices Act", Section 4100, of the California Public Contract Code (PCC), the Bidder is to list below the name, address and license number of each Subcontractor who will perform work, labor, render services or specially fabricate and install a portion [type] of the work or improvement, in an amount of or in excess of 0.5% of the Contractor's total Bid. Failure to comply with this requirement may result in the Bid being rejected as non-responsive. The Contractor is to list only one Subcontractor for each portion of the Work. The Bidder's attention is directed to the Special Provisions - Section 3-2, "SELF-PERFORMANCE", which stipulates the percentage of the Work to be performed with the Bidder's own forces. The Bidder is to also list all SLBE, ELBE, DBE, DVBE, MBE, WBE, OBE, SDB, WoSB, HUBZone, and SDVOSB Subcontractors for which the Bidders are seeking recognition towards achieving any mandatory, voluntary, or both subcontracting participation percentages.

NAME, ADDRESS AND TELEPHONE NUMBER OF SUBCONTRACTOR	CONSTRUCTOR OR DESIGNER	SUBCONTRACTOR LICENSE NUMBER	TYPE OF WORK	DOLLAR VALUE OF SUBCONTRACT	MBE, WBE, DBE, DVBE, OBE, ELBE, SLBE, SDB, WoSB, HUBZone, OR SDVOSB①	WHERE CERTIFIED②	CHECK IF JOINT VENTURE PARTNERSHIP
Name: <u>Payco Specialties, Inc.</u> Address: <u>120 north second ave</u> City: <u>chula vista</u> State: <u>ca</u> Zip: <u>91910-1127</u> Phone: <u>619-422-9204</u> Email: <u>estimating@payco.biz</u>	Constructor	298637	Striping	\$170,625.00	SLBE, SBE, DBE, WBE	CITY, CA	
Name: _____ Address: _____ City: _____ State: _____ Zip: _____ Phone: _____ Email: _____							

- ① As appropriate, Bidder shall identify Subcontractor as one of the following and shall include a valid proof of certification (except for OBE, SLBE and ELBE):
- |   |        |  |         |
|---|--------|--|---------|
| Certified Minority Business Enterprise        | MBE    | Certified Woman Business Enterprise            | WBE     |
| Certified Disadvantaged Business Enterprise   | DBE    | Certified Disabled Veteran Business Enterprise | DVBE    |
| Other Business Enterprise                     | OBE    | Certified Emerging Local Business Enterprise   | ELBE    |
| Certified Small Local Business Enterprise     | SLBE   | Small Disadvantaged Business                   | SDB     |
| Woman-Owned Small Business                    | WoSB   | HUBZone Business                               | HUBZone |
| Service-Disabled Veteran Owned Small Business | SDVOSB |  |         |
- ② As appropriate, Bidder shall indicate if Subcontractor is certified by:
- |  |        |  |          |
|--|--------|--|----------|
| City of San Diego                                    | CITY   | State of California Department of Transportation | CALTRANS |
| California Public Utilities Commission               | CPUC   |  |          |
| State of California's Department of General Services | CADoGS | City of Los Angeles                              | LA       |
| State of California                                  | CA     | U.S. Small Business Administration               | SBA      |

**The Bidder will not receive any subcontracting participation percentages if the Bidder fails to submit the required proof of certification.**

# City of San Diego

CITY CONTACT: Juan E. Espindola, Contract Specialist, Email: [JEEpindola@sandiego.gov](mailto:JEEpindola@sandiego.gov)  
Phone No. (619) 533-4491

## ADDENDUM A



**FOR**

**SLURRY SEAL GROUP 2023**

BID NO.:	<u>K-21-1975-DBB-3</u>
SAP NO. (WBS/IO/CC):	<u>21004779</u>
CLIENT DEPARTMENT:	<u>2116</u>
COUNCIL DISTRICT:	<u>1, 5, 6, 7</u>
PROJECT TYPE:	<u>ID</u>

**BID DUE DATE:**

**2:00 PM  
DECEMBER 1, 2020**

**CITY OF SAN DIEGO'S ELECTRONIC BIDDING SITE, PLANETBIDS**

<http://www.sandiego.gov/cip/bidopps/index.shtml>

**A. CHANGES TO CONTRACT DOCUMENTS**

The following changes to the Contract Documents are hereby made effective as though originally issued with the bid package. Bidders are reminded that all previous requirements to this solicitation remain in full force and effect.

**B. ADDITIONAL CHANGES**

1. The following are additional changes to the Line Items in the PlanetBids Tab:

For clarity where applicable, **ADDITIONS**, if any, have been **Underlined** and **DELETIONS**, if any, have been **Stricken out**.

<b>Section</b>	<b>Item Code</b>	<b>Description</b>	<b>UoM</b>	<b>Quantity</b>	<b>Payment Reference</b>	<b>Extension</b>
Main Bid	237310	<del>Class 2 Aggregate Base</del> <u>Crushed</u> <del>Miscellaneous Base</del>	TON	100	301-2.4	
Main Bid	237310	<u>Striping Modifications -</u> <u>EOC Type I</u>	AL	1	314-5.7	60000

James Nagelvoort, Director  
Engineering & Capital Projects Department

Dated: *November 19, 2020*  
San Diego, California

JN/EW/rd

**Bid Results**

**Bidder Details**

**Vendor Name** VSS International, Inc.  
**Address** 3785 Channel Drive  
 West Sacramento, CA 95691  
 United States  
**Respondee** Jeff Roberts  
**Respondee Title** Senior Vice President  
**Phone** 916-373-1500 Ext.  
**Email** vssi\_contracts@slurry.com  
**Vendor Type** CADIR,PQUAL  
**License #** 293727  
**CADIR** 1000001231

**Bid Detail**

**Bid Format** Electronic  
**Submitted** December 1, 2020 1:49:55 PM (Pacific)  
**Delivery Method**  
**Bid Responsive**  
**Bid Status** Submitted  
**Confirmation #** 233119  
**Ranking** 0

**Respondee Comment**

Please accept our bid.

**Buyer Comment**

**Attachments**

File Title	File Name	File Type
Contractors Certification	Contractors Certification of Pending Actions.pdf	CONTRACTOR'S CERTIFICATION OF PENDING ACTIONS
Mandatory Disclosure of Business	Mandatory Disclosure.pdf	MANDATORY DISCLOSURE OF BUSINESS INTERESTS FORM
Prime Debarment & Suspension	Debarment & Suspension.pdf	PRIME - DEBARMENT AND SUSPENSION CERTIFICATION
Subs Debarment and Suspension	SUB Debarment and Suspension Certification.pdf	SUBS - DEBARMENT AND SUSPENSION CERTIFICATION
Bid Bond	BOND.pdf	Bid Bond

**Line Items**

Type	Item Code	UOM	Qty	Unit Price	Line Total	Comment
<b>Main Bid</b>						
1	Raise Appurtenance to Grade (Water, Sewer)					
	237310	EA	65	\$682.50	\$44,362.50	
2	Adjust Existing Manhole Frame and Cover to Grade					
	237310	EA	40	\$1,155.00	\$46,200.00	

**Bid Results**

Type	Item Code	UOM	Qty	Unit Price	Line Total	Comment
3	Reconstruct Survey Monument Box					
	237310	EA	10	\$997.50	\$9,975.00	
4	Adjust Existing Survey Monument to Grade					
	237310	EA	5	\$577.50	\$2,887.50	
5	Crushed Miscellaneous Base					
	237310	TON	100	\$47.25	\$4,725.00	
6	Traffic Detector Loop Replacement or Conduit Stub Installed					
	237310	EA	27	\$504.00	\$13,608.00	
7	Removal of Humps, Lumps, and Pavement Irregularities					
	237310	LF	2749	\$2.89	\$7,944.61	
8	Asphalt Pavement Repair					
	237310	TON	4200	\$155.40	\$652,680.00	
9	Asphalt Concrete with Pavement Fabric Material					
	237310	TON	800	\$99.75	\$79,800.00	
10	Rubber Polymer Modified Slurry (RPMS) Type I (Bike Lane)					
	237310	SF	256932	\$0.20	\$51,386.40	
11	Rubber Polymer Modified Slurry (RPMS) Type I Over Type II					
	237310	SF	6006592	\$0.31	\$1,862,043.52	
12	Rubber Polymer Modified Slurry (RPMS) Type II Over Type III					
	237310	SF	668304	\$0.34	\$227,223.36	
13	Crack Seal					
	237310	LB	101608	\$2.59	\$263,164.72	
14	Post-construction Requirements - Inlet Markers					
	237310	EA	169	\$18.90	\$3,194.10	
15	Bonds (Payment and Performance)					
	524126	LS	1	\$18,000.00	\$18,000.00	
16	Water Pollution Control Program Development					
	541330	LS	1	\$12,730.00	\$12,730.00	
17	Water Pollution Control Program Implementation					
	541330	LS	1	\$12,100.00	\$12,100.00	
18	Field Orders - EOC Type II					
		AL	1	\$100,000.00	\$100,000.00	



**Bid Results**

Type	Item Code	UOM	Qty	Unit Price	Line Total	Comment
19	Remove, Replace & Install Traffic Striping, Markers, Markings, and Devices					
	237310	LS	1	\$195,962.15	\$195,962.15	
20	Traffic Control and Working Drawings					
	541330	LS	1	\$326,133.14	\$326,133.14	
21	Striping Modifications - EOC Type I					
	237310	AL	1	\$60,000.00	\$60,000.00	
<b>Subtotal</b>					<b>\$3,994,120.00</b>	
<b>Total</b>					<b>\$3,994,120.00</b>	

**Subcontractors**

Name & Address	Description	License Num	CADIR	Amount	Type
<b>Global Road Sealing Inc</b> 10832 Dorothy Ave Garden Grove, CA 92843 United States	Crack Seal Subcontractor	757584	1000007714	\$250,971.76	
<b>Jerusalem Construction, Inc.</b> <b>DBA Miramar General Engineering</b> 1827 Cleveland Ave National City, CA 91950 United States	Utility Adjustment Subcontractor	1009541	1000033057	\$98,500.00	ELBE,PQUAL,CADIR
<b>Frank and Son Paving, Inc.</b> 1019 3rd Avenue Chula Vista, CA 91911 United States	Paving Subcontractor	612545	1000009502	\$709,659.75	ELBE
<b>CTE inc.</b> 9991 Possum Creek Lane El Cajon, CA 92021 United States	Traffic Loops Subcontractor	786098	1000011764	\$12,960.00	ELBE,PQUAL,CADIR
<b>payco specialties, inc</b> 120 North Second Avenue Chula Vista, CA 91910 United States	Striping Subcontractor	298637	1000003515	\$170,625.00	DBE, MBE, WBE

Line Totals (Unit Price * Quantity)								
Item Num	Section	Item Code	Description	Reference	Unit of Measure	Quantity	VSS International, Inc. - Unit Price	VSS International, Inc. - Line Total
1	Main Bid	237310	Raise Appurtenance to Grade (Water, Sewer)	403-5	EA	65	\$682.50	\$44,362.50
2	Main Bid	237310	Adjust Existing Manhole Frame and Cover to Grade	403-5	EA	40	\$1,155.00	\$46,200.00
3	Main Bid	237310	Reconstruct Survey Monument Box	403-5	EA	10	\$997.50	\$9,975.00
4	Main Bid	237310	Adjust Existing Survey Monument to Grade	403-5	EA	5	\$577.50	\$2,887.50
5	Main Bid	237310	Crushed Miscellaneous Base	301-2.4	TON	100	\$47.25	\$4,725.00
6	Main Bid	237310	Traffic Detector Loop Replacement or Conduit Stub Installed	404-12	EA	27	\$504.00	\$13,608.00

7	Main Bid	237310	Removal of Humps, Lumps, and Pavement Irregularities	<b>404-12</b>	LF	2749	\$2.89	\$7,944.61
8	Main Bid	237310	Asphalt Pavement Repair	<b>301-1.7</b>	TON	4200	\$155.40	\$652,680.00
9	Main Bid	237310	Asphalt Concrete with Pavement Fabric Material	<b>404-12</b>	TON	800	\$99.75	\$79,800.00
10	Main Bid	237310	Rubber Polymer Modified Slurry (RPMS) Type I (Bike Lane)	<b>302-4.12.4</b>	SF	256932	\$0.20	\$51,386.40
11	Main Bid	237310	Rubber Polymer Modified Slurry (RPMS) Type I Over Type II	<b>302-4.12.4</b>	SF	6006592	\$0.31	\$1,862,043.52
12	Main Bid	237310	Rubber Polymer Modified Slurry (RPMS) Type II Over Type III	<b>302-4.12.4</b>	SF	668304	\$0.34	\$227,223.36
13	Main Bid	237310	Crack Seal	<b>302-15.5</b>	LB	101608	\$2.59	\$263,164.72

14	Main Bid	237310	Post-construction Requirements - Inlet Markers	<b>1001-4.2</b>	EA	169	\$18.90	\$3,194.10
15	Main Bid	524126	Bonds (Payment and Performance)	<b>1-7.2.1</b>	LS	1	\$18,000.00	\$18,000.00
16	Main Bid	541330	Water Pollution Control Program Development	<b>1001-4.2</b>	LS	1	\$12,730.00	\$12,730.00
17	Main Bid	541330	Water Pollution Control Program Implementation	<b>1001-4.2</b>	LS	1	\$12,100.00	\$12,100.00
18	Main Bid		Field Orders - EOC Type II	<b>7-3.9</b>	AL	1	\$100,000.00	\$100,000.00
19	Main Bid	237310	Remove, Replace & Install Traffic Striping, Markers, Markings, and Devices	<b>314-5.7</b>	LS	1	\$195,962.15	\$195,962.15
20	Main Bid	541330	Traffic Control and Working Drawings	<b>601-7</b>	LS	1	\$326,133.14	\$326,133.14

21	Main Bid	237310	Striping Modifications - EOC Type I	<b>314-5.7</b>	AL	1	\$60,000.00	\$60,000.00
							Subtotal	\$3,994,120.00
							Total	\$3,994,120.00
